



Caltrain Modernization Program Peninsula Corridor Electrification Project (PCEP)



May 2020 Monthly Progress Report

May 31, 2020

Funding Partners



Federal Transit Administration (FTA) Core Capacity
FTA Section 5307 (Environmental / Pre Development only)
FTA Section 5307 (Electric Multiple Unit (EMU) only)



Prop 1B (Public Transportation Modernization & Improvement Account)
Caltrain Low Carbon Transit Operations Cap and Trade



Proposition 1A
California High Speed Rail Authority (CHSRA) Cap and Trade



Carl Moyer Fund



Bridge Tolls (Funds Regional Measure (RM) 1/RM2)



San Francisco
County Transportation
Authority



San Francisco County Transportation Authority (SFCTA)/San Francisco
Municipal Transportation Agency (SFMTA)



San Mateo County Transportation Authority (SMCTA) Contribution
SMCTA Measure A



Santa Clara Valley Transportation Authority (VTA) Measure A
VTA Contribution



City and County of San Francisco (CCSF) Contribution

THIS PAGE INTENTIONALLY LEFT BLANK

Table of Contents

	Page
1.0 Background	1-1
2.0 Executive Summary.....	2-1
2.1. Monthly Dashboards	2-2
2.2. Funding Partners Participation in PCEP.....	2-5
2.3. Schedule.....	2-8
2.4. Budget	2-9
2.5. Board Actions	2-9
2.6. Government and Community Affairs	2-10
3.0 Electrification – Infrastructure	3-1
3.1. Electrification	3-1
3.2. Supervisory Control and Data Acquisition	3-3
3.3. Tunnel Modification.....	3-4
4.0 Electric Multiple Units	3-2
4.1. Electric Multiple Units.....	4-1
4.2. Centralized Equipment Maintenance and Operations Facility Modifications	4-1
5.0 Safety	5-1
6.0 Quality Assurance	6-1
7.0 Schedule	7-1
8.0 Budget and Expenditures	7-2
9.0 Change Management	9-1
10.0 Funding	10-1
11.0 Risk Management	11-1
12.0 Environmental	12-1
12.1. Permits	12-1
12.2. Mitigation Monitoring and Reporting Program (MMRP)	12-1
13.0 Utility Relocation.....	13-1
14.0 Real Estate.....	14-1
15.0 Third Party Agreements.....	15-1
16.0 Government and Community Affairs.....	16-1
17.0 Disadvantaged Business Enterprise (DBE) Participation and Labor Statistics	17-1
18.0 Procurement.....	18-1
19.0 Timeline of Major Project Accomplishments	19-1

List of Tables

	Page
Table 2-1 Schedule Status.....	2-9
Table 2-2 Budget and Expenditure Status.....	2-9
Table 3-1 Work Progress by Segment	3-1
Table 6-1 Quality Assurance Audit Summary.....	6-2
Table 7-1 Schedule Status.....	7-1
Table 7-2 Critical Path Summary	7-2
Table 7-3 Schedule Hold Points.....	7-2
Table 8-1 Electrification Budget & Expenditure Status	8-1
Table 8-2 EMU Budget & Expenditure Status	8-2
Table 8-3 PCEP Budget & Expenditure Status.....	8-2
Table 8-4 Third Party Improvements/CNPA Budget & Expenditure Status.....	8-2
Table 8-5 Budget Transfers of Contingency.....	8-3
Table 15-1 Third-Party Agreement Status.....	15-1

List of Figures

	Page
Figure 2-1 PCEP Work Segments.....	2-1
Figure 2-2 Expenditure – Planned vs. Actual.....	2-2
Figure 2-3 Spending Rate vs Required.....	2-3
Figure 2-4 Construction Contract Budgets.....	2-3
Figure 2-5 OCS Foundation Production.....	2-4
Figure 2-6 Contractor Completion Schedule.....	2-4
Figure 10-1 Funding Plan.....	10-1
Figure 11-1 Monthly Status of Risks.....	11-1
Figure 11-2 Risk Classification.....	11-3
Figure 17-1 DBE Participation.....	17-1

List of Appendices

	Page
Appendix A – Acronyms.....	A-1
Appendix B – Funding Partner Meetings.....	B-1
Appendix C – Schedule.....	C-1
Appendix D – Standard Cost Codes.....	D-1
Appendix E – Change Order Logs.....	E-1
Appendix F – Risk Table	F-1
Appendix G – MMRP Status Log	G-1

1.0 BACKGROUND

Over the last decade, Caltrain has experienced a substantial increase in ridership and anticipates further increases in ridership demand as the San Francisco Bay Area's population grows. The Caltrain Modernization (CalMod) Program, scheduled to be implemented by 2021, will electrify and upgrade the performance, operating efficiency, capacity, safety, and reliability of Caltrain's commuter rail service.

The PCEP is a key component of the CalMod Program and consists of converting Caltrain from diesel-hauled to Electric Multiple Unit (EMU) trains for service between the San Francisco Station (at the intersection of Fourth and King Streets in San Francisco) and the Tamien Station in San Jose. Caltrain will continue Gilroy service and support existing tenants.

An electrified Caltrain will better address Peninsula commuters' vision of environmentally friendly, fast and reliable service. Electrification will modernize Caltrain and make it possible to increase service while offering several advantages in comparison with existing diesel power use, including:


- **Improved Train Performance, Increased Ridership Capacity and Increased Service:** Electrified trains can accelerate and decelerate more quickly than diesel-powered trains, allowing Caltrain to run more efficiently. In addition, because of their performance advantages, electrified trains will enable more frequent and/or faster train service to more riders.
- **Increased Revenue and Reduced Fuel Cost:** An electrified Caltrain will increase ridership and fare revenues while decreasing fuel costs.
- **Reduced Engine Noise Emanating from Trains:** Noise from electrified train engines is measurably less than noise from diesel train engines. Train horns will continue to be required at grade crossings, adhering to current safety regulations.
- **Improved Regional Air Quality and Reduced Greenhouse Gas Emissions:** Electrified trains will produce substantially less corridor air pollution compared with diesel trains even when the indirect emissions from electrical power generation are included. Increased ridership will reduce automobile usage, resulting in additional air quality benefits. In addition, the reduction of greenhouse gas emissions will improve our regional air quality, and will also help meet the state's emission reduction goals.

THIS PAGE INTENTIONALLY LEFT BLANK

2.0 EXECUTIVE SUMMARY

The Monthly Progress Report is intended to provide an overview of the PCEP and provide funding partners, stakeholders, and the public an overall update on the progress of the project. This document provides information on the scope, cost, funding, schedule, and project implementation. Work along the Caltrain Electrification Corridor has been divided into four work segments and respective work areas (WA) as shown in Figure 2-1. PCEP activities are described and summarized by segments and work areas.

Figure 2-1 PCEP Work Segments

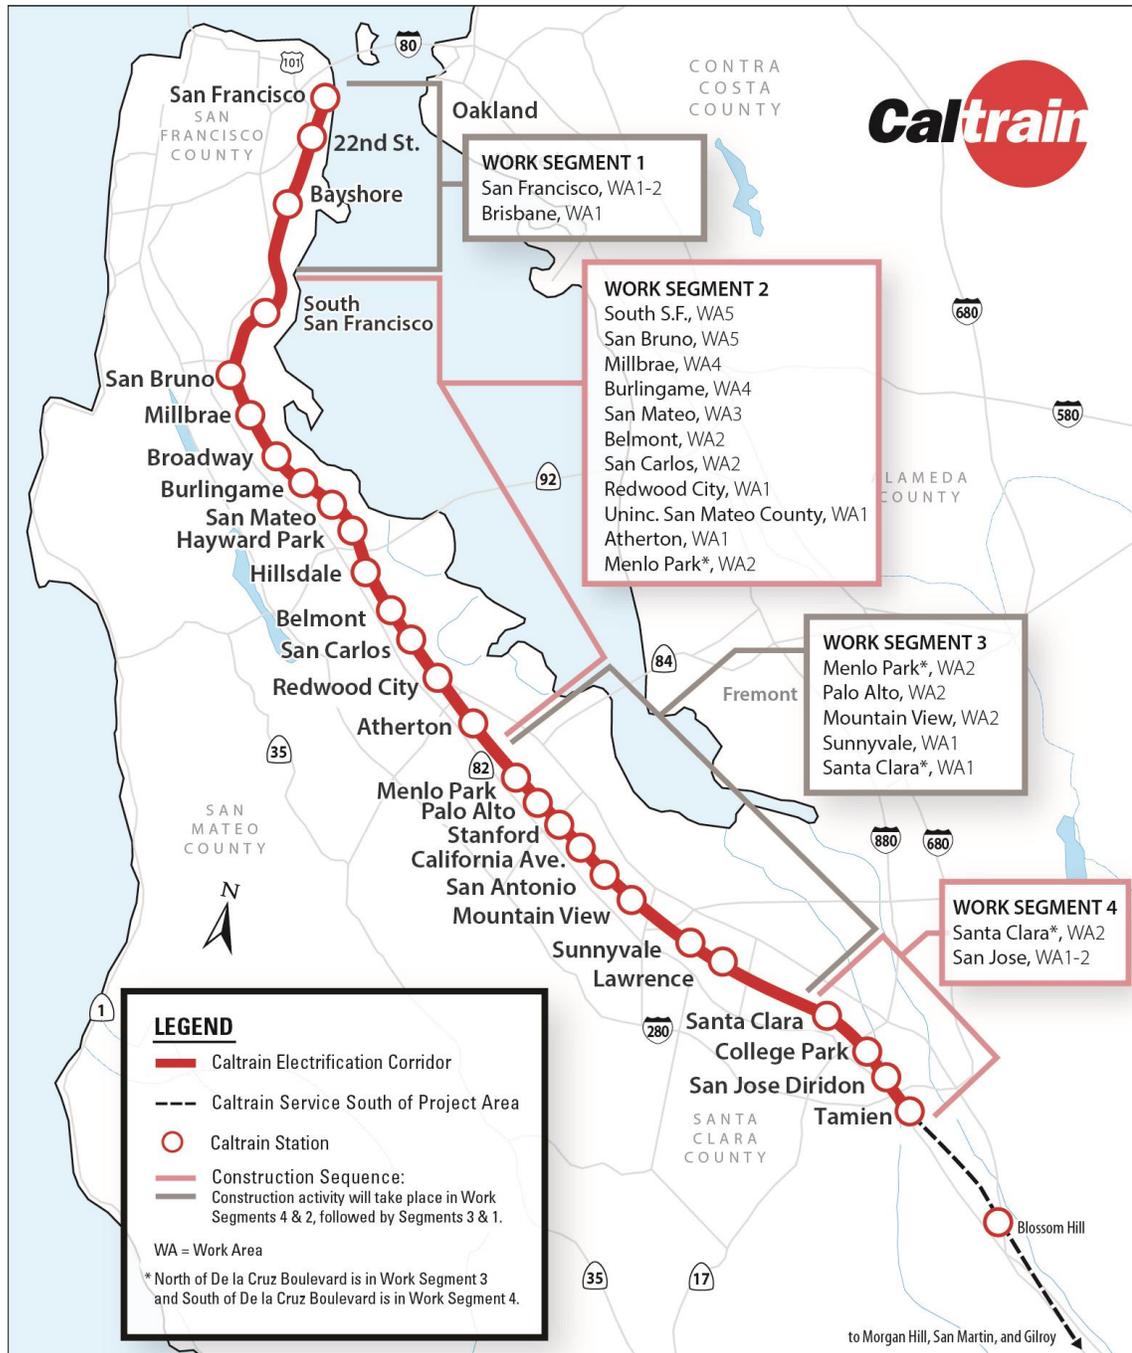

Peninsula Corridor Electrification Project
Monthly Progress Report

Electrification construction progress in May included installation of Overhead Contact System (OCS) static and feeder wires in Segment 2 and OCS foundations in Segment 3. As a result of the Design-Build contractor’s (Balfour Beatty Infrastructure, Inc. (BBII)) failure to order a sufficient number of rebar cages for foundation installation, only 44 foundations were installed in May, temporarily slowing progress. Anticipating the procurement of rebar cages, PCEP continued working with BBII to advance a schedule that has an anticipated foundation installation completion date of December 31, 2020. BBII installed signal houses in Segment 4 and continued with installation of signal ductbanks, conduit, and cable in Segments 2 and 4. Site work and foundation installation progressed in Traction Power Substation (TPS) TPS-1 and Paralleling Stations (PS) PS-4 and PS-5.

The JPB-approved agreement with PG&E to construct 115 kilovolt (kV) interconnections between TPS-1 and TPS-2 was executed in May, and coordination between the JPB and PG&E began in preparation for upcoming construction work.

The Federal Railroad Administration approved the waiver regarding the use of an Alternative Vehicle Technology for crashworthiness design. EMU production is still on schedule, although Stadler expects production delays due to disruption in the supply chain from Coronavirus Disease 2019 (COVID-19). Type Testing of Trainset No. 1 is still on hold as travel remains restricted for the personnel who are needed to conduct the test.

The Centralized Equipment Maintenance and Operations Facility (CEMOF) work includes completion of installation of conduit and wire inside the maintenance building, catch basins, and a storm drain line.

2.1. Monthly Dashboards

Dashboard progress charts are included below to summarize construction progress.

Figure 2-2 Expenditure – Planned vs. Actual

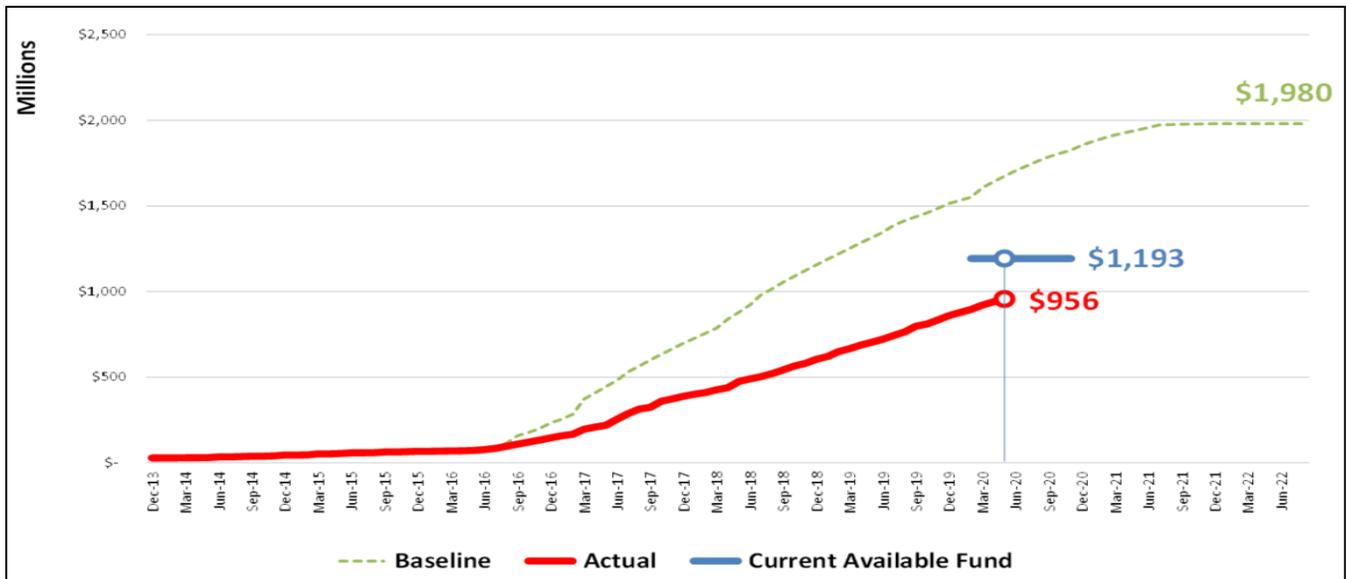


Figure 2-3 Spending Rate vs. Required

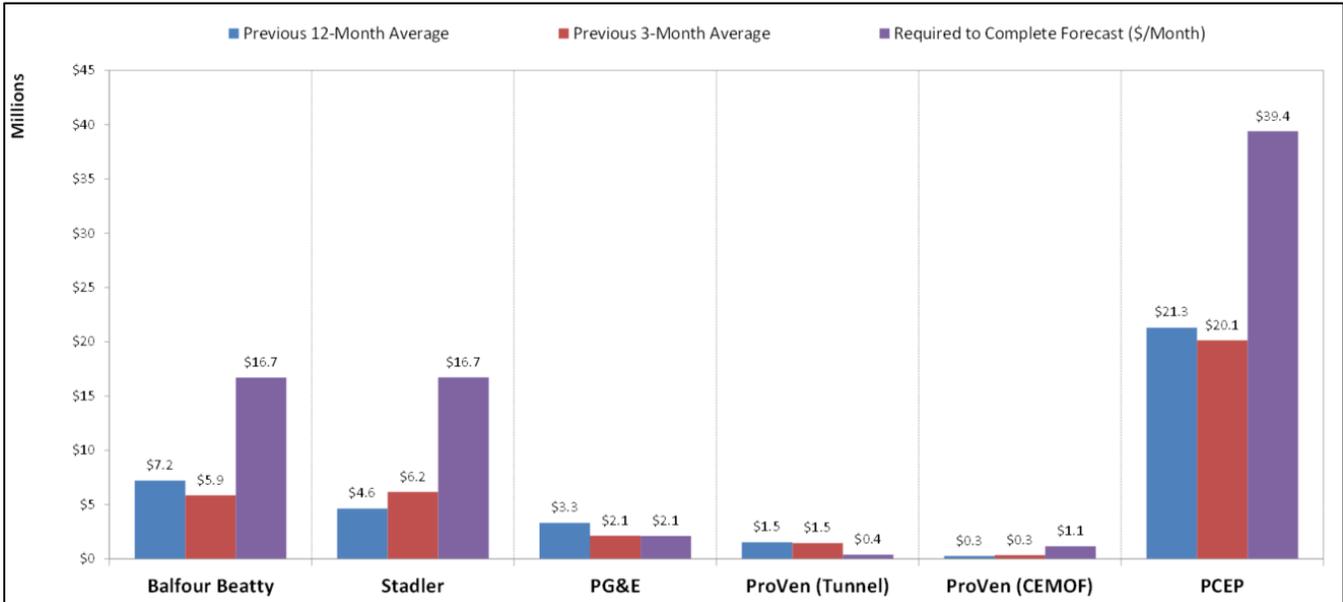


Figure 2-4 Construction Contract Budgets

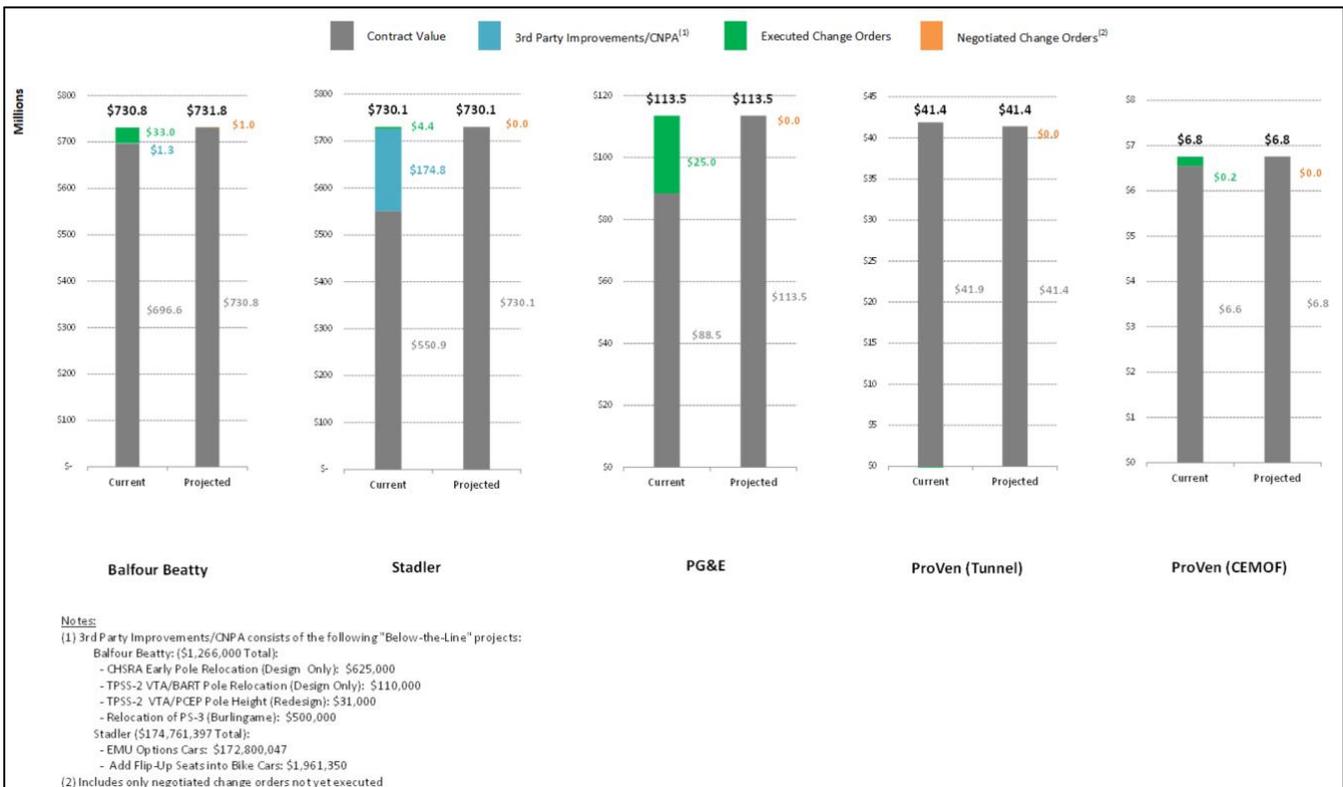


Figure 2-5 OCS Foundation Production


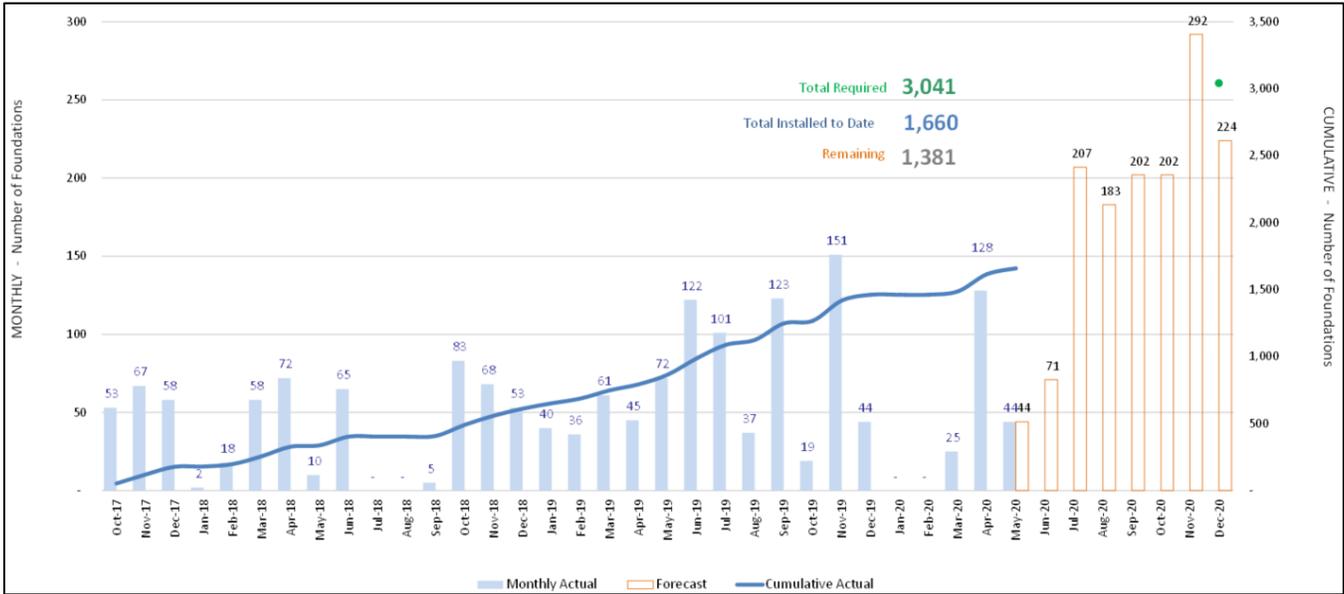


Figure 2-6 Contractor Completion Schedule

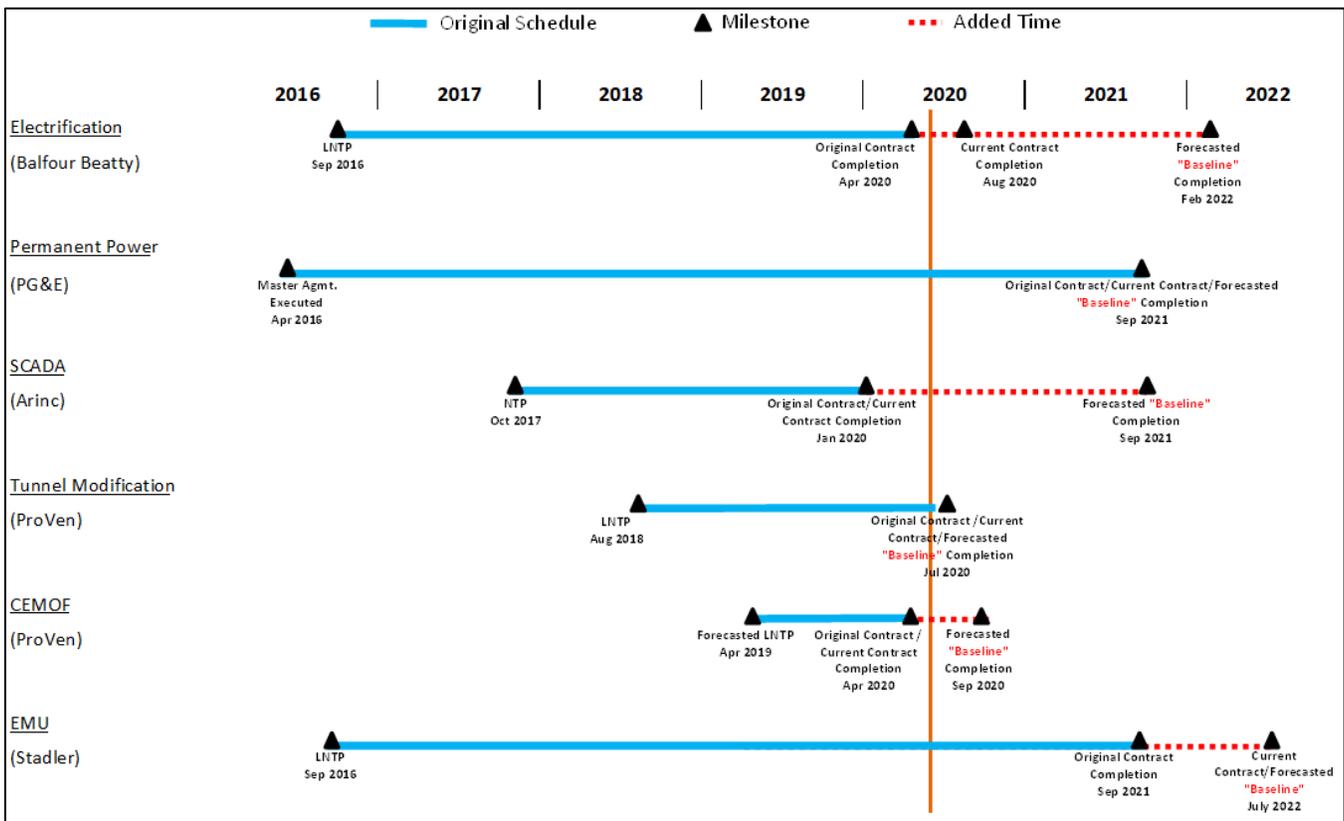

2.2. Funding Partners Participation in PCEP

The PCEP has a series of weekly, biweekly, monthly and quarterly meetings to coordinate all aspects of the program. The meetings are attended by project staff with participation by our funding partners in accordance with the Funding Partners Oversight Protocol. A summary of funding partner meetings and invitees can be found in Appendix B.

This section of the report provides a summary of the discussions and decisions made at the meetings and a list of funding partners who attended the meetings.

Electrification – Weekly Discipline-Specific Meetings

Purpose: To replace the previous weekly Engineering Meeting with three discipline-specific meetings for the three major categories of work under the Electrification Design Build (DB) contract: Overhead Contact System (OCS) Foundation, Traction Power Facilities (TPF), and Signals. Each meeting will focus on the status, resolution and tracking of Balfour Beatty Infrastructure, Inc. (BBII) and Electrification design- and construction-related issues.

Activity this Month

OCS Foundation Meeting

Funding Partners: None

- Review of upcoming foundation design and installation schedule
- Discussion of open issues impacting foundations design and installation
- Discussion of outstanding Requests for Information (RFI)
- Review of foundation designs that potentially impact Right of Way (ROW)
- Review of outstanding Field Orders or Change Notices required for work to continue

TPF Meeting

Funding Partners: None

- Review of outstanding items as they relate to the design and construction of the PG&E Interconnection
- Review of status of long-lead material procurement
- Review of PG&E Interconnection schedule
- Discuss progress and next steps for the Single-Phase Study
- Discuss outstanding comments on the interconnection agreement
- Review and resolve open issues on the construction and design of the TPFs (paralleling stations, traction power substations, switching station)

Signal Meeting

Funding Partners: None

- Discussion of design, installation and testing of the signal and communication modifications to the Caltrain system
- Discussion of outstanding comments and responses to comments on signal and communication design packages
- Review of schedule for signal and communication cutover plans
- Discuss and resolve RFIs

PCEP Delivery Coordination Meeting – Bi-Weekly

Purpose: To facilitate high-level coordination and information sharing between cross-functional groups regarding the status of the work for which they are responsible.

Activity this Month

Funding Partners: VTA: Edwin Castillo; SFCTA: Luis Zurinaga

The Project Management Oversight Consultant (PMOC) held a virtual monitoring visit with staff on May 19-20. A bi-annual presentation on the progress of the project to the San Francisco County Transportation Authority (SFCTA) Board of Supervisors is scheduled in June. In environmental and planning, a Notice of Construction was filed with the California Public Utilities Commission (CPUC) for the PG&E interconnection work. In contracts and procurement, two sole-source contract amendments have been approved by the JPB Finance Committee and the Change Management Board (CMB). Both will be presented to the June Board for final approval. For EMU design and manufacturing, truck frame production in Winterthur and carshell production in Altenrhein are running on schedule. Testing and commissioning on Trainset 1 in Salt Lake City has limited progress due to engineer travel restrictions to the U.S. Shoring work for the CEMOF facility is nearly complete and form work is projected to start within the next couple of weeks. In design build activities, steel cages for Segment 3 are projected to arrive on May 20 and will follow with steel plates and foundations installation. There will be coordination with the South San Francisco Project team for the work on the temporary platform at TPS-1.

Systems Integration Meeting – Bi-Weekly

Purpose: To discuss and resolve issues with inter-system interfaces and to identify and assign Action Item Owners for interface points that have yet to be addressed.

Activity this Month

Funding Partners: None

Bi-weekly PCEP interface meetings are held to monitor and determine appropriate resolution for systems integration issues. All information from the systems integration database was recovered, is now in an Excel spreadsheet and individual items are being updated. The Action Items spreadsheet is the primary tracking method while review and System Integration matrix updates are in progress. The Systems Integration Lead also

maintains contact with the EMU procurement team. The Traction Power SCADA team also holds bi-weekly status meetings. Coordination with the EMU procurement, PTC and Caltrain Capital Project managers responsible for delivery of the 25th Avenue Grade Separation Project, Marin Napoleon Bridge Rehabilitation Project, and the South San Francisco Station Project is ongoing. There is coordination with the Tunnel Modification Project, PG&E construction of the Interconnection to TPS-2, and the CEMOF upgrades as well. Progress on activities including systems integration testing activities, FRA, FTA and safety certification are being tracked. An effort is being undertaken to re-focus Systems Integration to avoid task overlap with the JPB Rail Activation Committee. A smaller “breakout” group is meeting to determine and track what testing and with which resources will need to be coordinated among the various contracts and suppliers. This “Testing & Commissioning Meeting” is the primary interface to the PCEP Design-Build Team at this time. This group will report back to the System Integration meeting group with their findings.

Master Program Schedule (MPS) Meeting – Monthly

Purpose: To review the status of the MPS and discuss the status of major milestones, critical and near-critical paths, upcoming Board review items, and progress with the contracts, among others.

Activity this Month

Funding Partners: Metropolitan Transportation Commission (MTC): Trish Stoops; VTA: Manolo Gonzalez-Estay, SFCTA: Luis Zurinaga

The program critical path continues to run through the manufacturing and testing of EMU trainsets. Due to COVID-19 impacts on the Stadler vehicle schedule, the forecasted Revenue Service Date (RSD) has been adjusted from May 2022 to July 2022. This has resulted in the drawdown of 77 days of contingency. Thirty one days of contingency remain to support an RSD of August 2022. As the COVID-19 pandemic is a force majeure event, the JPB is reviewing its Full Funding Grant Agreement (FFGA) RSD obligation.

Risk Assessment Meeting – Monthly

Purpose: To identify risks and corresponding mitigation measures. For each risk on the risk register, mitigation measures have been identified and are being implemented. Progress in mitigating these risks is confirmed at the ongoing risk monitoring and monthly risk assessment meetings.

Activity this Month

Funding Partners: SFCTA: Luis Zurinaga; MTC: Trish Stoops

A Risk Assessment Committee Meeting was held on May 6. Nine risks were retired, two risks were regraded, and three new risks were added to the risk register.

Change Management Board (CMB) – Monthly

Purpose: To review, evaluate and authorize proposed changes to PCEP over \$200,000. The CMB discusses major topics including potential changes to PCEP contracts,

contingency usage, track access delays and Differing Site Conditions (DSC) field order updates. Potential contract changes will follow the PCEP Change Order Procedure. Once approved changes are executed, they will be reported in the Change Management section (Section 9) of this report.

Activity this Month

The CMB meeting occurred on April 7.

Funding Partners: CHSRA: Boris Lipkin; VTA: Edwin Castillo; SFCTA: Luis Zurinaga and Anna Harvey; SMCTA: Joe Hurley; MTC: Kenneth Folan, Trish Stoops, and S. Wolfe

BBII Contract

Four changes were approved.

CEMOF Contract

No changes were identified for consideration.

Stadler Contract

One change was approved.

SCADA Contract

No changes were identified for consideration

Tunnel Modification Contract

No changes were identified for consideration.

Amtrak Contract

No changes were identified for consideration.

Other

No changes were identified for consideration.

2.3. Schedule

The program critical path continues to run through the manufacturing and testing of EMU trainsets by Stadler. Stadler reported an overall schedule delay due to the impact of COVID-19 travel restrictions on trainset testing. As a result, the forecasted Revenue Service Date (RSD) has been delayed from May 2022 to July 2022. Since the COVID-19 pandemic is a force majeure event, the JPB is reviewing the possibility of extending its FFGA Revenue Service obligation.

BBII continues to report an overall delay to substantial completion. JPB is working with BBII on the issue and is urging BBII to accelerate resolution.

Table 2-1 indicates major milestone dates for the MPS.

Table 2-1 Schedule Status

Milestones	Program Plan	Progress Schedule (May 2020) ¹
Arrival of First Vehicle in Pueblo, CO	N/A	11/20/2020 ²
Arrival of First Vehicle at JPB (after Pueblo Testing)	N/A	04/02/2021 ²
Segment 4 Completion	11/21/2019	03/25/2021
o Interconnection from PG&E Substation to Traction Power Substation (TPS)	N/A	12/10/2020
PG&E Provides Permanent Power	09/09/2021	09/09/2021
Electrification Substantial Completion	08/10/2020	02/26/2022 ²
Start Phased Revenue Service	N/A	02/27/2022 ²
RSD (w/o Risk Contingency)	12/09/2021	07/22/2022 ²
FFGA RSD (w/ Risk Contingency)	08/22/2022	08/22/2022

Note:

1. Dates may shift slightly as the update of this month's Progress Schedule is still in process.
2. See "Notable Variances" in Section 7 for explanation on date shift.

2.4. Budget

A summary of the overall budget and expenditure status for the PCEP is provided in Table 2-2 below.

Table 2-2 Budget and Expenditure Status

Description of Work	Budget (A)	Current Budget (B) ¹	Cost This Month (C) ²	Cost To Date (D) ³	Estimate To Complete (E)	Estimate At Completion (F) = (D) + (E)
Electrification Subtotal	\$1,316,125,208	\$1,316,125,208	\$10,451,707	\$735,097,431	\$581,027,777	\$1,316,125,208
EMU Subtotal	\$664,127,325	\$664,127,325	\$5,786,544	\$221,215,638	\$442,911,686	\$664,127,325
PCEP TOTAL	\$1,980,252,533	\$1,980,252,533	\$16,238,251	\$956,313,069	\$1,023,939,464	\$1,980,252,533

Notes regarding tables above:

1. Column B "Current Budget" includes executed change orders and awarded contracts.
2. Column C "Cost This Month" represents the cost of work performed this month.
3. Column D "Cost To Date" includes actuals (amount paid) and accruals (amount of work performed) to date.

2.5. Board Actions

- None

Future anticipated board actions include:

- Shunt wire construction
- EMU Pantograph Inspection & Monitoring System contract
- On-call program management and electrification support services contract amendments

2.6. Government and Community Affairs

There was one outreach event this month.

3.0 ELECTRIFICATION – INFRASTRUCTURE

This section reports on the progress of the Electrification, SCADA, and Tunnel Modification components. A brief description on each of the components is provided below.

3.1. Electrification

The Electrification component of the PCEP includes installation of 138 miles of wire and overhead catenary system (OCS) for the distribution of electrical power to the EMUs. The OCS will be powered from a 25 kilovolt (kV), 60-Hertz, single phase, alternating current supply system consisting of two traction power substations (TPS), one switching station (SWS), and seven paralleling stations (PS). Electrification infrastructure will be constructed using a DB delivery method.

Activity This Month

- Continued to install on-track and off-track foundations in Segment 3.
- Strung OCS feeder and static wires in Segment 2.
- Potholed at proposed OCS locations and utility locations in all Segments in advance of foundation installation. BBII and PCEP also continued to resolve conflicts found during the potholing process, such as loose concrete, asphalt, and other debris, and continued designing solutions for those conflicts that cannot be avoided. The conflicts must be resolved before installation of foundations at those locations.
- Relocated signal cables and remove abandoned facilities found in conflict with planned OCS foundations as conflicts were identified.
- Removed asbestos found in conflict with OCS foundations.
- Continued to install ductbank and manholes, drainage, and form and rebar work at TPS-1.
- Continued civil work and ductbank installation, and installed gantry foundations at PS-4.
- Continued site work and utility removal at PS-5.
- Continued to install signal ductbank, conduits, and cables in Segment 2.
- Continued to install signal ductbank, conduits, and cables in Segment 4.
- Performed cable termination at CP Michael.
- Installed cables at Luther Junction.
- Set signal houses at 45.21 and 45.57.
- Continued drilling of rails for impedance bond connections in Segments 1, 2, 3 and 4 at various control points and crossings.
- Continued installation of insulated joints (IJs) in Segment 3.
- Performed switch isolation in Segment 3.
- Install overhead bridge attachments at various locations in Segment 2 and 3.

Peninsula Corridor Electrification Project
Monthly Progress Report

- Progressed the OCS design with BBII in all segments, which included submittal and review of Design Change Notices for revised foundation locations.
- Coordinated design review with local jurisdictions for the OCS, traction power facilities, and bridge attachments design, including responses to comments from jurisdictions.
- Continued to review and coordinate signal and communication design submittals with BBII.
- Continued discussions with FRA and CPUC on grade crossing design.
- Continued to progress the TPS interconnection design for TPS-1 and TPS-2. Received Issued for Construction Design (IFC) for TPS-2 and continued to progress TPS-1 interconnection design towards IFC.
- Executed amendment to Supplemental Agreement No. 2 with PG&E for construction of interconnections at TPS-1 and 2.
- Worked with BBII through Site Specific Work Plans (SSWP) for upcoming field work.
- Continued to work with PG&E and Silicon Valley Power (SVP) for the finalization of single-phase studies. Continued data conversion and model validation.
- PG&E continued work at East Grand and FMC substations.

A summary of the work progress by segment is provided in Table 3-1 below.

Table 3-1 Work Progress by Segment

Segment	Work Area	Foundations			Poles		
		Required ^{abc}	Completed this Month	Completed to Date	Required ^{ab}	Completed this Month	Completed to Date ^{de}
1	Tunnels	32	0	32	32	0	32
	A	309	0	0	259	0	0
	B	237	0	0	177	0	0
2	5	244	0	184	209	0	160
	4	314	0	239	254	0	190
	3	174	0	63	141	0	36
	2	247	0	78	205	0	60
	1	207	0	79	154	0	33
3	2	510	44	382	443	23	137
	1	391	0	360	310	9	230
4	A	241	0	156	177	0	107
	B	139	0	87	123	0	70
	CEMOF	95	0	0	81	0	0
Total		3,140	44	1,660	2,565	32	1055

Note:

- Foundations required do not match poles required as guy foundations are needed in some locations for extra support.
- The number of required poles and foundations fluctuate due to design changes.
- 55 foundations in S2WA5 will be installed by South San Francisco and 64 foundations in S2WA3 will be installed by 25th Avenue.
- Installation of one additional pole in S3WA1 was unreported during December 2019.
- Installation of three additional poles in S2WA4 were unreported during May 2019.

Activity Next Month

- Continue foundation installation in Segment 3, both on-track and off-track.
- Continue resolution of DSCs.
- Continue to install protective steel plates for protection of utilities during foundation installation.
- Continue to install OCS poles and assemblies in all Segments where available.
- Continue wire installation in Segments 3 and 4.
- Continue work with BBII on field investigation activities and designs, which will include the progression of the OCS, traction power, bonding and grounding, signal systems, and other civil infrastructure such as overhead bridge protections.
- Pothole and clear obstructions at proposed OCS locations. Potholing will concentrate in Segments 3 and 4, as well areas of potential ROW needs in Segments 1 and 2.
- Continue construction at TPS-1 and TPS-2.
- Continue construction at PS-7, PS-5, PS-4, PS-6, and the Switching Station.
- Continue to install conduit and foundations for signal and wayside power cubicle (WPC) units in Segment 4 and Segment 2.
- Continue to install impedance bond connections.
- Continue to install IJs.
- Continue to install bridge attachments.
- Continue to coordinate with stakeholders on the consistent warning time solution and advance location-specific design.
- Continue to progress location-specific design for grade crossing system.
- Continue planning process for signal cutovers.
- Review BBII work plans for upcoming construction activities.
- Complete review of TPS-2 IFC and progress TPS-1 to IFC.
- Coordinate with PG&E on final design and construction for PG&E infrastructure.
- Coordinate with local jurisdictions to review designs.
- Continue tree pruning and removals.

3.2. Supervisory Control and Data Acquisition

SCADA is a system that monitors and controls field devices for electrification, including traction power substations (TPS), wayside power cubicles (WPC), and the OCS. SCADA will be integrated with the base operating system for Caltrain Operations and Control, which is the Rail Operations Center System. A separate control console will be established for the Power Director.

Activity This Month

- Submitted formal schedule for review and Monthly Progress Report.
- All Test Procedures have been completed and received Statement of No Objection (SONO) or SONO with Comments.
- ARINC delivered FAT database for MACRO to review as a Pre-FAT activity

Activity Next Month

- Prepare and deliver the Monthly Report and the Monthly Schedule Update.
- Attend project status meetings (virtually).
- Support ongoing discussions concerning RFIs.
- Complete Installation and Cutover Plan
- Complete Operations User Manual
- Complete Training Manual
- Deliver Installation Plan and complete pre-FAT at 95%.

3.3. Tunnel Modification

Tunnel modifications will be required on the four tunnels located in San Francisco. This effort is needed to accommodate the required clearance for the OCS to support electrification of the corridor. Outside of the PCEP scope, Caltrain Engineering has requested the PCEP team to manage completion of design and construction for the Tunnel 1 and Tunnel 4 Drainage and Track Rehabilitation Project. The Tunnel Drainage and Track Rehabilitation Project is funded separately from PCEP.

Activity This Month

- Continued review of and prepared responses for submittals and RFIs.
- Completed Installation of fencing at Tunnels 1 through 4.
- Completed Conductor Rail installation.
- Completed Right of Way (ROW) fence signage.
- Feeder installation completed.
- Completed installation of Post insulator.

Activity Next Month

- Review and respond to submittals, RFIs, and SSWPs as needed.
- Terminate feeder wire, contact wire, and conductor rail.
- Install signage inside all tunnels.
- Prepare OCS testing plan.
- Review Spare Parts transmittal.
- Punch List items.

3.4. Interconnection Construction

The PCEP will require a 115-kV interconnection to supply power from the PG&E substations to the Caltrain substations in San Jose and South San Francisco. Construction of the interconnections will be performed by PG&E under an amendment to Supplemental Agreement No. 2.

Activity This Month

- Review and respond to submittals.
- Review RFP for TPS-2.
- Review Change Orders.
- Pre-Bid Walk for FMC.

Activity Next Month

- Continue reviewing and responding to submittals.

THIS PAGE INTENTIONALLY LEFT BLANK

4.0 ELECTRIC MULTIPLE UNITS

This section reports on the progress of the Electric Multiple Units (EMU) procurement and the Centralized Equipment Maintenance and Operations Facility (CEMOF) modifications.

4.1. Electric Multiple Units

The procurement of EMUs, or trainsets, from Stadler consists of a Base Order of 96 railcars, plus an Option Order of an additional 37 railcars, for a total of 133 railcars. The cars from these two orders will be combined and delivered as 19 seven-car Trainsets. The Base Order is funded from PCEP, and Option Order funded by a Transit and Intercity Rail Capital Program (TIRCP) grant. One more Option for additional cars is available.

Activity This Month

- COVID-19 preventive actions continued for the third month causing mixed disruptions to Stadler's activities:
 - Switzerland-based management, administrative and engineering personnel are back in their offices.
 - Switzerland-based production continued to operate near normal. Car shells and truck frames shipments are on schedule.
 - Salt Lake City-based management, administrative and engineering personnel are back in their offices.
 - Salt Lake City-based 'Type Testing' of Trainset No. 1 continues to be on hold since key Stadler and sub-supplier personnel cannot travel to the United States. The current delay in testing is estimated at one day for each day of COVID-19 travel restrictions.
 - Stadler has material for about three trainsets, but the disrupted supply chain will likely create shortages and production delays.
 - Stadler is in the process of determining possible delays to trainset deliveries to Caltrain.
 - PCEP oversight and administration of Project is unaffected.
 - PCEP QA representatives are onsite in Altenrhein and Salt Lake City facilities.
- Final Design Reviews remain to be completed for three systems. These software-based systems include 'Train Control,' 'Monitoring and Diagnostics,' and 'Car Control.' Completion is scheduled for mid-2020 and must be performed prior to the commencement of Type Testing.
- First Article Inspections (FAI) continue to have their paperwork formalized and closed out.
- 37 car shells have been shipped from Stadler – Switzerland, with 28 onsite in Stadler's Salt Lake City facility.

- The requested waiver from the FRA pertaining to use of an 'Alternative Vehicle Technology' (AVT) approach for crashworthiness design has been approved by the FRA. This is a major accomplishment and milestone for the Project.
- The requested waiver from the FRA pertaining to passenger activated manual emergency door opening has been denied by the FRA. This pertains only to the high-level doors that are now being plugged. Caltrain's will provide an FRA-compliant design.
- Quality Assurance audits of USA-based sub-suppliers were halted in mid-March due to COVID-19 travel restriction. Audits will commence when sub-suppliers reopen.
- PCEP, FRA and Caltrain Management meeting in Salt Lake City postponed to July 8 and 9.

Activity Next Month

- Continue to close out system level FDRs and FAls.
- Add two staff members in Salt Lake City. One as a test witnesser for the exhaustive engineering Type Tests, and the other as a witnesser of Routine Tests conducted on all 133 cars, and 19 completed trainsets.
- Re-baseline Stadler trainset delivery and testing schedule on Caltrain property.
- Continue to support system integration and rail startup activation activities

4.2. Centralized Equipment Maintenance and Operations Facility Modifications

The CEMOF Modifications Project will provide work areas to perform maintenance on new EMUs.

Activity This Month

- Continued processing submittals, RFIs, and SSWPs.
- Completed installation of conduit and wire inside the maintenance building near Track 5.
- Started shoring for the catch basins at the maintenance pit and installed catch basins at the north pit.
- Completed installation of storm drain line including the 22-inch sleeve and pipe.

Activity Next Month

- Continue north pit shoring activity.
- Delivery of the Parts Storage Warehouse building.
- Design of the shoring for the shallow fire sprinkler line.
- Removal and off-haul of ballast at Track 5.
- Removal and off-haul of Class II soil from Track 5 area.

5.0 SAFETY

Safety and Security requirements and plans are necessary to comply with applicable laws and regulations related to safety, security, and emergency response activities. Safety staff coordinates with contractors to review and plan the implementation of contract program safety requirements. Safety project coordination meetings continue to be conducted on a monthly basis to promote a clear understanding of project safety requirements as defined in contract provisions and program safety documents.

Activity This Month

- Project staff provided input and continued its participation in the BBII contractor workforce safety meetings. Project incidents continue to be reviewed with project staff to reinforce the application of recommended safety mitigation measures.
- Conducted 2020 monthly employee injury reviews for BBII and its subcontractors.
- Continued to provide input and oversight of the contractor SSWP safety provisions and ongoing safety construction oversight and inspections.
- Continued the reviews with the contractor of the updated project Preliminary Hazard Analysis (PHA), Threat & Vulnerability Assessment (TVA), Safety & Security Certification Plan (SSCP), and System Safety Plan (SSP).
- Conducted the monthly project Safety and Security Certification and Fire/Life Safety Meetings.
- Performed reviews and provided comments on the BBII Safety and Security Certification Design Criteria Conformance Checklists (DCCC) submittals.
- Participated with internal stakeholders in Rail Activation Committee meetings.
- Investigated project incident occurrences and worked with the contractor representatives to identify incident root causes and develop and implement safety and security mitigation measures.
- Conducted ongoing safety inspections of contractor field activities and performed pre-work site hazards assessment walks with BBII and subcontractor staff.
- Participated in weekly project coordination meetings with the contractor to review open issues and recommended action items.
- Provided project safety and security updates to PMOC staff and provided requested documents to be reviewed by the PMOC.
- Continued to coordinate with JPB Safety and the project contractors with the application of mitigation measures in response to the evolving COVID-19 virus.

Activity Next Month

- Monthly virtual safety communication meetings continue to be scheduled for the Project Safety and Security Certification Committee, Fire/Life Safety Committee, Rail Activation Committee, and other project-related contractor and JPB safety meetings to discuss safety priorities.
- Continue focus on performing site safety inspections on the OCS foundations, pole installations, potholing, Tunnel, and CEMOF work to assess safety work practices and identify additional opportunities for improvement. Conduct contractor equipment inspections as needed.

Peninsula Corridor Electrification Project
Monthly Progress Report

- Continue to meet with the PCEP contractors, JPB safety, and TransitAmerica Services, Inc. (TASI) to identify opportunities to further improve project safety performance and continue to reinforce lessons learned safety mitigation recommendations resulting from prior project incidents.
- Reinforce the ongoing application of recommended mitigation measures in response to the evolving COVID-19 virus.

6.0 QUALITY ASSURANCE

The Quality Assurance (QA) staff performs technical reviews for planning, implementing, evaluating, and maintaining an effective program to verify that all equipment, structures, components, systems, and facilities are designed, procured, constructed, installed, and maintained in accordance with established criteria and applicable codes and standards throughout the design, construction, startup and commissioning of the PCEP.

Activity This Month

- Staff meetings with BBII QA/Quality Control (QC) management representatives continue weekly.
- Continued review of BBII-generated Nonconformance Reports (NCR) and Construction Discrepancy Reports for proper discrepancy condition, cause, disposition, corrective and preventive action and verification of closure.
- Continued review and approval of Design Variance Requests for BBII and PGH Wong for QA/QC and inspection issues/concerns.
- Continued review of BBII QC Inspectors Daily Reports, Construction QC Reports and Surveillance Reports for work scope, performance of required duties, adequacy, non-conformances, test/inspection results, follow-up on unresolved issues, and preciseness.
- Continued review of BBII Material Receipt Reports, Certificates of Conformance, Certified Tests Reports, and Certificates of Analysis to ensure delivered project materials conform to specifications, and that contractually required quality and test support documents are adequate and reflect concise conditions per the purchase order requirements.
- Continued regularly scheduled design reviews and surveillances on project design packages.
- Completed second shift BBII audit of the modernization of switch machines with no Findings.

Table 6-1 below provides details on the status of audits performed through the reporting period.

Table 6-1 Quality Assurance Audit Summary

Quality Assurance Activity	This Reporting Period	Total to Date
Audits Conducted	1	116
Audit Findings		
Audit Findings Issued	0	68
Audit Findings Open	0	0
Audit Findings Closed	0	68
Non-Conformances		
Non-Conformances Issued	0	10
Non-Conformances Open	0	1
Non-Conformances Closed	0	9

Activity Next Month

- Conduct audits of two PGH Wong design packages.
- Conduct field surveillances at TPS-1.
- Conduct audit of the CEMOF contractor, ProVen.

7.0 SCHEDULE

The program critical path continues to run through the manufacturing and testing of EMU trainsets by Stadler. Stadler reported an overall schedule delay due to the impact of COVID-19 travel restrictions on trainset testing. As a result, the forecasted Revenue Service Date (RSD) has been delayed from May 2022 to July 2022. Since the COVID-19 pandemic is a force majeure event, the JPB is reviewing the possibility of extending its FFGA Revenue Service obligation.

Shown below, Table 7-1 indicates major milestone dates for the MPS.

Table 7-1 Schedule Status

Milestones	Program Plan	Progress Schedule (May 2020) ¹
Arrival of First Vehicle in Pueblo, CO	N/A	11/20/2020 ²
Arrival of First Vehicle at JPB (after Pueblo testing)	N/A	04/02/2021 ²
Segment 4 Completion	11/21/2019	03/25/2021
o Interconnection from PG&E Substation to Traction Power Substation (TPS)	N/A	12/10/2020
PG&E Provides Permanent Power	09/09/2021	09/09/2021
Electrification Substantial Completion	08/10/2020	02/26/2022 ²
Start Phased Revenue Service	N/A	02/27/2022 ²
RSD (w/o Risk Contingency)	12/09/2021	07/22/2022 ²
FFGA RSD (w/ Risk Contingency)	08/22/2022	08/22/2022

Note:

1. Dates may shift slightly as the update of this month's Progress Schedule is still in process.
2. See "Notable Variances" for explanation on date shift.

Notable Variances

BBII continues to report an overall delay to substantial completion. JPB is working with BBII on the issue and is urging BBII to accelerate resolution. While BBII works to resolve its schedule delays, the JPB continues to evaluate the BBII schedule and has determined that BBII's substantial completion has been delayed from January 2022 to February 2022. This results in a delay to the start of Phased Revenue Service, from February 1, 2022 to February 27, 2022.

Within the month of May, the variances relative to the BBII schedule are due to signal design progressing slower than the progress assumed in the baseline schedule, slow progress on Traction Power Facilities design and construction, and slow progress on OCS foundation design resolution and installation.

Peninsula Corridor Electrification Project
Monthly Progress Report

Additionally, the vehicle schedule has been updated to reflect COVID-19 impacts. These impacts affect the assembly and test of all trainsets, most notably the following milestones:

1. Arrival of the first trainset in Pueblo, CO is delayed from September 2020 to November 2020
2. Arrival of the first trainset on JPB property is delayed from February 2021 to April 2021
3. Conditional acceptance of the 14th trainset is delayed from May 6, 2022 to July 22, 2022

The JPB will continue to monitor the impact of COVID-19 on these milestones.

The COVID-19 impact on Stadler's schedule has also caused a delay on program completion. The RSD has been delayed from May 6, 2022 to July 22, 2022. This has resulted in a contingency drawdown of 77 days; decreasing overall schedule contingency from 108 days to 31 days.

Items listed in Table 7-2 reflect the critical path activities/milestones for the PCEP.

Table 7-2 Critical Path Summary

Activity	Start	Finish
Manufacturing, Testing & Acceptance of Trainsets 1 - 14	08/13/2018	07/22/2022
RSD w/out Risk Contingency	05/06/2022	07/22/2022
FFGA RSD w/ Risk Contingency	08/22/2022	08/22/2022

Schedule Hold Points

Schedule Hold Points (SHP) represent key milestones on or near a schedule's critical path that are used as measurement points with respect to contingency drawdown. Delays to these key milestones have the potential to require a program to utilize available contingency. Table 7-3 below reflects the SHPs for the PCEP program schedule. The dates indicated reflect the planned completion dates for each SHP.

Table 7-3 Schedule Hold Points

Schedule Hold Point (SHP)	Date
FTA/PMOC Risk Refresh	08/30/2016 (A)
Begin EMU Manufacturing	12/04/2017 (A)
Arrival of 1 st Trainset in Salt Lake City	02/04/2019 (A)
Arrival of 1 st Trainset in Pueblo, CO	11/20/2020
Arrival of 1 st Trainset at JPB	04/02/2021
Segment 4 Completion	03/25/2021
Conditional Acceptance of 1 st Trainset	12/03/2021
System Electrified	02/26/2022
Begin Phased Revenue Service	02/27/2022
Conditional Acceptance of 14th Trainset	07/22/2022
FFGA RSD w/ Risk Contingency	08/22/2022

Note: "(A)" denotes an actual completion

THIS PAGE INTENTIONALLY LEFT BLANK

8.0 BUDGET AND EXPENDITURES

The summary of overall budget and expenditure status for the PCEP and Third-Party Improvements is shown in the following tables. Table 8-1 reflects the Electrification budget, Table 8-2 the EMU budget, Table 8-3 the overall PCEP budget, and Table 8-4 Third Party Improvements budget. Table 8-5 summarizes the budget transfers of contingency completed this month.

Table 8-1 Electrification Budget & Expenditure Status

Description of Work	Budget (A)	Current Budget (B) ¹	Cost This Month (C) ²	Cost To Date (D) ³	Estimate To Complete (E)	Estimate At Completion (F) = (D) + (E)
ELECTRIFICATION						
Electrification ⁽⁴⁾	\$696,610,558	\$729,574,261	\$3,275,755	\$395,269,983	\$334,304,278	\$729,574,261
SCADA	\$0	\$3,446,917	\$0	\$1,934,371	\$1,512,546	\$3,446,917
Tunnel Modifications	\$11,029,649	\$41,408,610	\$150,630	\$41,023,975	\$384,635	\$41,408,610
Real Estate	\$28,503,369	\$28,503,369	\$55,104	\$21,214,779	\$7,288,590	\$28,503,369
Private Utilities	\$63,515,298	\$117,451,380	\$3,352,560	\$85,699,500	\$31,751,880	\$117,451,380
Management Oversight ⁽⁵⁾	\$141,506,257	\$150,143,604	\$1,939,703	\$139,264,575	\$10,879,029	\$150,143,604
Executive Management	\$7,452,866	\$9,214,226	\$107,050	\$8,338,927	\$875,300	\$9,214,226
Planning	\$7,281,997	\$6,281,997	\$7,802	\$5,812,042	\$469,955	\$6,281,997
Community Relations	\$2,789,663	\$1,789,663	\$6,319	\$1,576,567	\$213,095	\$1,789,663
Safety & Security	\$2,421,783	\$3,691,387	\$104,411	\$3,421,055	\$270,332	\$3,691,387
Project Management Services	\$19,807,994	\$16,807,994	\$181,017	\$12,958,018	\$3,849,976	\$16,807,994
Engineering & Construction	\$11,805,793	\$12,372,460	\$199,925	\$10,681,489	\$1,690,972	\$12,372,460
Electrification Eng & Mgmt	\$50,461,707	\$50,461,707	\$575,403	\$48,462,588	\$1,999,120	\$50,461,707
Construction Management	\$0	\$4,499,776	\$470,552	\$4,222,606	\$277,171	\$4,499,776
IT Support	\$312,080	\$407,170	\$0	\$407,170	\$0	\$407,170
Operations Support	\$1,445,867	\$2,380,632	\$43,178	\$2,702,152	(\$321,520)	\$2,380,632
General Support	\$4,166,577	\$5,566,577	\$69,263	\$5,631,546	(\$64,968)	\$5,566,577
Budget / Grants / Finance	\$1,229,345	\$1,429,345	\$356	\$1,353,426	\$75,919	\$1,429,345
Legal	\$2,445,646	\$4,755,731	\$106,758	\$4,616,542	\$139,190	\$4,755,731
Other Direct Costs	\$5,177,060	\$5,777,060	\$67,669	\$4,372,572	\$1,404,487	\$5,777,060
Prior Costs 2002 - 2013	\$24,707,878	\$24,707,878	\$0	\$24,707,878	\$0	\$24,707,878
TASI Support	\$55,275,084	\$57,475,084	\$1,651,178	\$40,582,426	\$16,892,658	\$57,475,084
Insurance	\$3,500,000	\$4,543,588	\$0	\$4,543,588	\$0	\$4,543,588
Environmental Mitigations	\$15,798,320	\$14,972,644	\$0	\$756,777	\$14,215,868	\$14,972,644
Required Projects	\$17,337,378	\$14,253,335	\$7,083	\$917,539	\$13,335,796	\$14,253,335
Maintenance Training	\$1,021,808	\$1,021,808	\$0	\$0	\$1,021,808	\$1,021,808
Finance Charges	\$5,056,838	\$6,137,156	\$19,693	\$3,889,916	\$2,247,240	\$6,137,156
Contingency	\$276,970,649	\$147,193,450	N/A	N/A	\$72,747,601	\$72,747,601
Forecasted Costs and Changes	\$0	\$0	N/A	N/A	\$74,445,850	\$74,445,850
ELECTRIFICATION SUBTOTAL	\$1,316,125,208	\$1,316,125,208	\$10,451,707	\$735,097,431	\$581,027,777	\$1,316,125,208

Notes regarding tables above:

1. Column B "Current Budget" includes executed change orders and awarded contracts.
2. Column C "Cost This Month" represents the cost of work performed this month.
3. Column D "Cost To Date" includes actuals (amount paid) and accruals (amount of work performed) to date.
4. Cost To Date for "Electrification" includes 5% for Contractor's retention until authorization of retention release.
5. The agency labor is actual through April 2020 and accrued for May 2020.

Peninsula Corridor Electrification Project
Monthly Progress Report

Table 8-2 EMU Budget & Expenditure Status

Description of Work	Budget (A)	Current Budget (B) ¹	Cost This Month (C) ²	Cost To Date (D) ³	Estimate To Complete (E)	Estimate At Completion (F) = (D) + (E)
EMU						
EMU	\$550,899,459	\$555,292,618	\$4,753,440	\$170,705,002	\$384,587,616	\$555,292,618
CEMOF Modifications	\$1,344,000	\$6,756,604	\$310,499	\$3,309,931	\$3,446,672	\$6,756,604
Management Oversight ⁽⁴⁾	\$64,139,103	\$62,557,957	\$692,829	\$44,079,616	\$18,478,341	\$62,557,957
Executive Management	\$5,022,302	\$6,263,136	\$64,646	\$5,150,261	\$1,112,875	\$6,263,136
Community Relations	\$1,685,614	\$985,614	\$200	\$653,647	\$331,967	\$985,614
Safety & Security	\$556,067	\$765,296	\$13,178	\$563,666	\$201,630	\$765,296
Project Mgmt Services	\$13,275,280	\$11,275,280	\$105,839	\$8,374,113	\$2,901,167	\$11,275,280
Eng & Construction	\$89,113	\$89,113	\$0	\$23,817	\$65,296	\$89,113
EMU Eng & Mgmt	\$32,082,556	\$29,981,014	\$352,756	\$20,378,886	\$9,602,127	\$29,981,014
Construction Management	\$0	\$1,501,543	\$62,001	\$701,965	\$799,578	\$1,501,543
IT Support	\$1,027,272	\$952,089	\$11,107	\$625,853	\$326,236	\$952,089
Operations Support	\$1,878,589	\$1,878,589	\$8,210	\$393,550	\$1,485,038	\$1,878,589
General Support	\$2,599,547	\$2,599,547	\$33,354	\$2,429,317	\$170,230	\$2,599,547
Budget / Grants / Finance	\$712,123	\$1,012,123	(\$83)	\$899,348	\$112,775	\$1,012,123
Legal	\$1,207,500	\$1,251,473	\$654	\$1,234,874	\$16,599	\$1,251,473
Other Direct Costs	\$4,003,139	\$4,003,139	\$40,967	\$2,650,318	\$1,352,821	\$4,003,139
TASI Support	\$2,740,000	\$2,789,493	\$17,705	\$160,404	\$2,629,089	\$2,789,493
Insurance	\$0	\$38,263	\$0	\$38,263	\$0	\$38,263
Required Projects	\$4,500,000	\$3,927,821	\$0	\$538,280	\$3,389,541	\$3,927,821
Finance Charges	\$1,941,800	\$3,761,482	\$12,070	\$2,384,142	\$1,377,340	\$3,761,482
Contingency	\$38,562,962	\$29,003,087	N/A	N/A	\$25,720,176	\$25,720,176
Forecasted Costs and Changes	\$0	\$0	N/A	N/A	\$3,282,911	\$3,282,911
EMU SUBTOTAL	\$664,127,325	\$664,127,325	\$5,786,544	\$221,215,638	\$442,911,686	\$664,127,325

Notes regarding tables above:

1. Column B "Current Budget" includes executed change orders and awarded contracts.
2. Column C "Cost This Month" represents the cost of work performed this month.
3. Column D "Cost To Date" includes actuals (amount paid) and accruals (amount of work performed) to date.
4. The agency labor is actual through April 2020 and accrued for May 2020.

Table 8-3 PCEP Budget & Expenditure Status

Description of Work	Budget (A)	Current Budget (B) ¹	Cost This Month (C) ²	Cost To Date (D) ³	Estimate To Complete (E)	Estimate At Completion (F) = (D) + (E)
Electrification Subtotal	\$1,316,125,208	\$1,316,125,208	\$10,451,707	\$735,097,431	\$581,027,777	\$1,316,125,208
EMU Subtotal	\$664,127,325	\$664,127,325	\$5,786,544	\$221,215,638	\$442,911,686	\$664,127,325
PCEP TOTAL	\$1,980,252,533	\$1,980,252,533	\$16,238,251	\$956,313,069	\$1,023,939,464	\$1,980,252,533

Notes regarding tables above:

1. Column B "Current Budget" includes executed change orders and awarded contracts.
2. Column C "Cost This Month" represents the cost of work performed this month.
3. Column D "Cost To Date" includes actuals (amount paid) and accruals (amount of work performed) to date.

Table 8-4 Third Party Improvements/CNPA Budget & Expenditure Status

Description of Work	Budget (A)	Current Budget (B) ¹	Cost This Month (C) ²	Cost To Date (D) ³	Estimate To Complete (E)	Estimate At Completion (F) = (D) + (E)
CHSRA Early Pole Relocation	\$1,000,000	\$1,000,000	\$0	\$941,706	\$58,294	\$1,000,000
PS-3 Relocation (Design)	\$500,000	\$500,000	\$0	\$150,000	\$350,000	\$500,000
TPSS-2 VTA/PCEP Pole Relocation (Design)	\$110,000	\$110,000	\$0	\$93,500	\$16,500	\$110,000
TPSS-2 VTA/PCEP Pole Height (Redesign)	\$31,000	\$31,000	\$0	\$0	\$31,000	\$31,000
EMU Option Cars	\$172,800,047	\$172,800,047	\$0	\$53,292,490	\$119,507,557	\$172,800,047
Add Flip-Up Seats into Bike Cars	\$1,961,350	\$1,961,350	\$0	\$980,675	\$980,675	\$1,961,350
CNPA TOTAL	\$176,402,397	\$176,402,397	\$0	\$55,458,372	\$120,944,025	\$176,402,397

Notes regarding tables above:

1. Column B "Current Budget" includes executed change orders and awarded contracts.
2. Column C "Cost This Month" represents the cost of work paid this month.
3. Column D "Cost To Date" includes actuals (amount paid) to date.

Table 8-4 shows improvements outside of the scope of PCEP that are funded with non-PCEP funds. These improvements are implemented through the PCEP contracts. In FTA terminology, these efforts are categorized as Concurrent Non-Project Activities (CNPA).

CHSRA Early Pole Relocation: Relocation of 196 OCS poles as part of PCEP. Implementing these pole relocations minimizes future cost and construction impacts. This scope is funded by the CHSRA.

PS-3 Relocation (Design): Relocate PS-3 (Burlingame) as part of PCEP to avoid a future conflict with the Broadway Grade Separation Project (BGSP). This scope is funded by the BGSP.

TPSS-2 VTA/PCEP Pole Relocation and Height (Design): Design changes due to the relocation of VTA/BART Pole at TPSS-2 location and pole height redesign for live line clearances. This scope is funded by the VTA.

EMU Option Cars: Exercise Stadler Contract Option for 37 additional EMUs. This scope is funded with a combination of TIRCP and matching local funds.

Add Flip-Up Seats into Bike Cars: Stadler contract change order to add four additional flip-up seats in each of the two unpowered (bike) cars per trainset (eight total per trainset). This scope is funded by Caltrain outside of the PCEP.

Table 8-5 Budget Transfers of Contingency

Transfer	Description	Contingency¹
ELECTRIFICATION		
BBI-053-CCO-050	Switch Machine Isolation - Credit	(\$277,430)
BBI-053-CCO-092A	Signal Cable Relocation (Field Order No. 340)	\$106,773
BBI-053-CCO-093A	Signal Cable Relocation (Field Order No. 340)	\$90,765
BBI-053-CCO-101	Asbestos Pipe Abatement at 46.3-07/08	\$21,037
	ELECTRIFICATION SUBTOTAL	(\$58,856)
EMU		
STA-056-CCO-023	Deferral of Wheelchair Lifts	\$632,703
PROV-071-CCO-022	Deletion of Concrete Pad and Double Plywood Floor at PSW	(\$1,409)
PROV-071-CCO-023	Flashing at Overflow Drain at Component Test Room	\$2,981
PROV-071-CCO-024	Parts Storage Warehouse Power Feed	\$16,412
PROV-071-CCO-025	Removal of Hazardous Soil from PSW Subgrade Excavation	\$43,444
PROV-071-CCO-026A	Removal of Hazardous Soil from PSW Footing Excavation	\$35,808
PROV-071-CCO-027	480 Volt Duct Bank and Wire Removal	\$5,015
	EMU SUBTOTAL	\$734,954
	PCEP TOTAL	\$676,098

Notes regarding tables above:

¹. Budget amount transferred from project contingency. A negative amount represents a credit to contingency.

Table 8-5 shows budget transfers of project contingency implemented during the current monthly reporting period. This table includes contingency transfers for both executed contract change orders as covered under Section 9.0 and uses of contingency for Program budget line items outside the five PCEP contracts.

Appendix D includes costs broken down by Standard Cost Code (SCC) format. This format is required for reporting of costs to the FTA. The overall project total in the SCC format is lower than the project costs in table 8-3. This is due to the exclusion of costs incurred prior to the project entering the Project Development phase.

9.0 CHANGE MANAGEMENT

The change management process establishes a formal administrative work process associated with the initiation, documentation, coordination, review, approval and implementation of changes that occur during the design, construction or manufacturing of the PCEP. The change management process accounts for impacts of the changes and ensures prudent use of contingency.

Currently the PCEP contracts are BBII, CEMOF, Stadler, SCADA, Tunnel Modifications, and Amtrak.

A log of all executed change orders can be found in Appendix E.

Executed Contract Change Orders (CCO) This Month

Electrification Contract

Change Order Authority (5% of BBII Contract)			5% x \$696,610,558 = \$34,830,528
Date	Change Number	Description	CCO Amount
5/1/2020	BBI-053-CCO-050	Switch Machine Isolation - Credit	(\$277,430)
5/19/2020	BBI-053-CCO-092A	Signal Cable Relocation (Field Order No. 340)	\$106,773
5/19/2020	BBI-053-CCO-093A	Signal Cable Relocation (Field Order No. 340)	\$90,765
5/27/2020	BBI-053-CCO-101	Asbestos Pipe Abatement at 46.3-07/08	\$21,037
			Total
			(\$58,885)

¹ (When indicated) Change approved by the Board of Directors – not counted against the Executive Director’s Change Order Authority.

EMU Contract

Change Order Authority (5% of Stadler Contract)			5% x \$550,899,459 = \$27,544,973
Date	Change Number	Description	CCO Amount
5/6/2020	STA-056-CCO-023	Deferral of Wheelchair Lifts	\$632,703
			Total
			\$632,703

¹ (When indicated) Change approved by the Board of Directors – not counted against the Executive Director’s Change Order Authority.

SCADA Contract

Change Order Authority (15% of ARINC Contract)			15% x \$3,446,917 = \$517,038
Date	Change Number	Description	CCO Amount
	None		\$0
			Total
			\$0

¹ (When indicated) Change approved by the Board of Directors – not counted against the Executive Director’s Change Order Authority.

Peninsula Corridor Electrification Project
Monthly Progress Report

Tunnel Modification Contract

Change Order Authority (10% of ProVen Contract)²

10% x \$38,477,777 = \$3,847,778

Date	Change Number	Description	CCO Amount
5/11/2020	PROV-070-CCO-025	NOPC #1 CWR (CNPA - Drainage \$660,000.00)	\$660,000
Total			\$660,000

¹ (When indicated) Change approved by the Board of Directors – not counted against the Executive Director's Change Order Authority.

² Tunnel modification contract (\$38,477,777) includes: Notching (\$25,281,170) and Drainage (\$13,196,607).

³ Third Party Improvements/CNPA Projects that are funded with non-PCEP funds.

CEMOF Contract

Change Order Authority (10% of ProVen Contract)

10% x \$6,550,777 = \$655,078

Date	Change Number	Description	CCO Amount
4/8/2020	PROV-071-CCO-022	Deletion of Concrete Pad and Double Plywood Floor at PSW	(\$1,409)
4/8/2020	PROV-071-CCO-023	Flashing at Overflow Drain at Component Test Room	\$2,981
4/9/2020	PROV-071-CCO-024	Parts Storage Warehouse Power Feed	\$16,412
4/22/2020	PROV-071-CCO-025	Removal of Hazardous Soil from PSW Subgrade Excavation	\$43,444
4/22/2020	PROV-071-CCO-026A	Removal of Hazardous Soil from PSW Footing Excavation	\$35,808
4/27/2020	PROV-071-CCO-027	480 Volt Duct Bank and Wire Removal	\$5,015
Total			\$102,251

¹ (When indicated) Change approved by the Board of Directors – not counted against the Executive Director's Change Order Authority.

Amtrak AEM-7 Contract

Change Order Authority (Lump Sum)

Up to \$150,000

Date	Change Number	Description	CCO Amount
	None		\$0
Total			\$0


Notes:

¹ When the threshold of 75% is reached, staff may return to the Board to request additional authority.

10.0 FUNDING

Figure 10-1 depicts a summary of the funding plan for the PCEP. It provides a breakdown of the funding partners as well as the allocated funds. In the last month, FTA awarded \$97 million in Section 5307 funding for the project. Staff are now working with FTA to award the next \$100 million in Core Capacity funding for the project.

Figure 10-1 Funding Plan

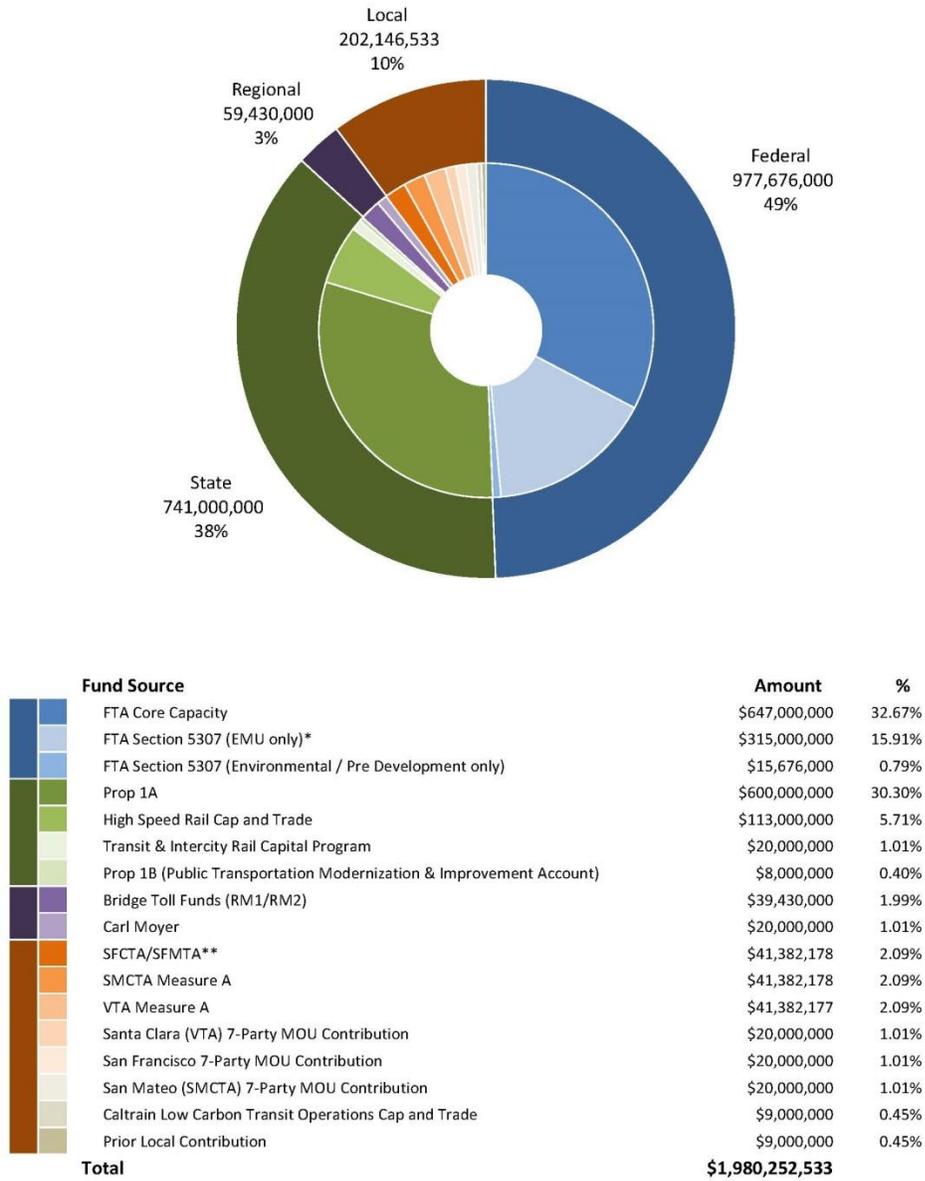

Notes:

*Includes necessary fund transfer with SMCTA

**Includes \$4M CMAQ Transfer considered part of SF local contribution

THIS PAGE INTENTIONALLY LEFT BLANK

11.0 RISK MANAGEMENT

The risk management process is conducted in an iterative fashion throughout the life of the project. During this process, new risks are identified, other risks are resolved or managed, and potential impacts and severity modified based on the current situation. The Risk Management team's progress report includes a summary on the effectiveness of the Risk Management Plan, any unanticipated effects, and any correction needed to handle the risk appropriately.

The Risk Management team meets monthly to identify risks and corresponding mitigation measures. Each risk is graded based on the potential cost and schedule impacts they could have on the project. This collection of risks has the greatest potential to affect the outcome of the project and consequently is monitored most closely. For each of the noted risks, as well as for all risks on the risk register, mitigation measures have been identified and are being implemented. Progress in mitigating these risks is confirmed at monthly risk assessment meetings attended by project team management and through continuous monitoring of the Risk Management Lead.

The team has identified the following items as top risks for the project (see Appendix F for the complete Risk Table):

1. The contractor may not complete and install signal design including two-speed check (2SC) modifications within budget and schedule.
2. Extent of differing site conditions and associated redesign efforts results in delays to the completion of the electrification contract and increases program costs.
3. Sub-optimal contractor sequencing when progressing design and clearing foundation locations may result in construction inefficiencies.
4. Additional property acquisition is necessitated by change in design.
5. Potential for Stadler's sub-suppliers to fall behind schedule or delays in parts supply chain result in late completion of vehicles.
6. TASI may not have sufficient number of signal maintainers for testing.
7. Contractor generates hazardous materials that necessitate proper removal and disposal in excess of contract allowances and expectations.
8. Rejection of Design Variance Request for Automatic Transformer Feeder and static wires results in cost and schedule impacts to PCEP.
9. Major program elements may not be successfully integrated with existing operations and infrastructure in advance of revenue service.
10. Property not acquired in time for contractor to do work.
11. Collaboration across multiple disciplines to develop a customized rail activation program may fail to comprehensively address the full scope of issues required to operate and maintain an electrified railroad and decommission the current diesel fleet.

Activity This Month


- Updated risk descriptions, effects, and mitigations based upon weekly input from risk owners. Monthly cycle of risk updating was completed based on schedules established in the Risk Identification and Mitigation Plan.

Peninsula Corridor Electrification Project
Monthly Progress Report

- Updated risk retirement dates based upon revisions to the project schedule and input from risk owners.
- Continued weekly monitoring of risk mitigation actions and publishing of the risk register.
- The Risk Management team attended Project Delivery, Traction Power, and Systems Integration meetings to monitor developments associated with risks and to identify new risks.
- Summarized cost of risk analysis in draft summary document.
- Developed risk register formulated by Rail Activation Committee.


Figures 11-1 and 11-2 show the risks identified for the program. Risks are categorized as top risk, upcoming risk, and all other risks. The categories are based on a rating scale composed of schedule and cost factors. Top risks are considered to have a significantly higher than average risk grade. Upcoming risks are risks for which mitigating action must be taken within 60 days. All other risks are risks not falling into other categories.

Figure 11-1 Monthly Status of Risks

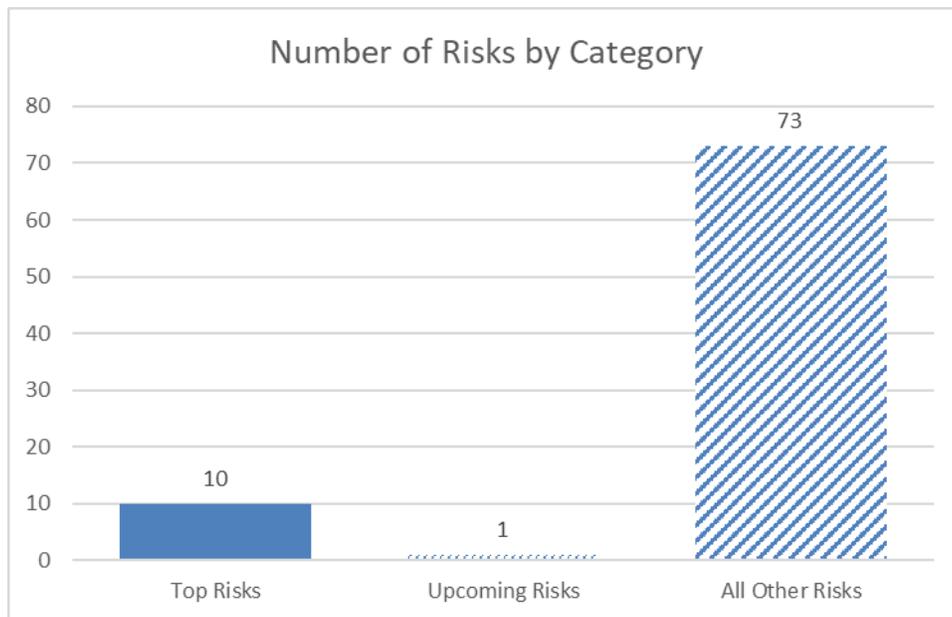

Total Number of Active Risks = 84

Figure 11-2 Risk Classification

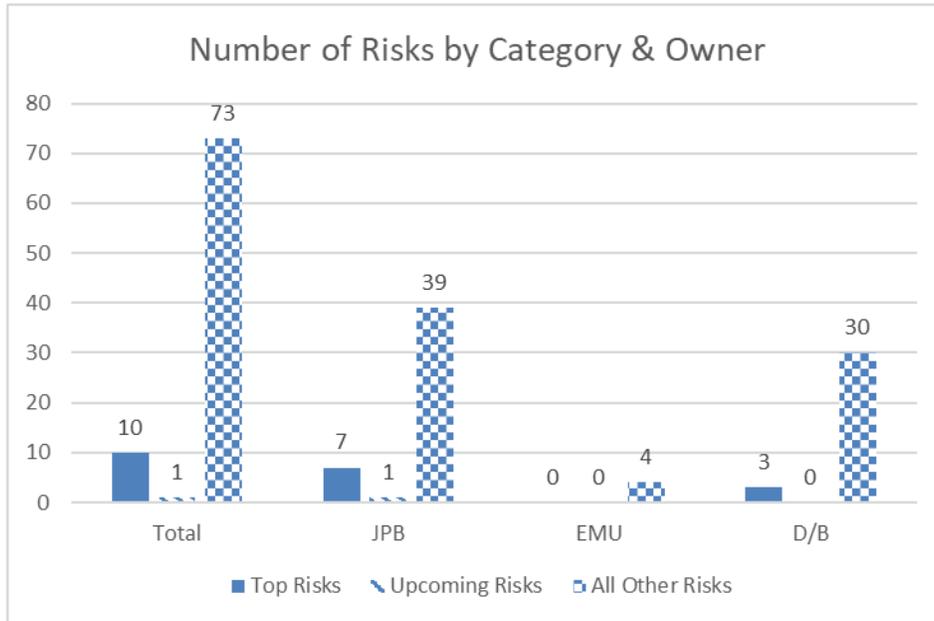

Total Number of Active Risks = 84

Activity Next Month

- Conduct weekly monitoring of risk mitigation actions and continue publishing risk register.
- Update risk descriptions, effects, mitigations and retirement dates based on weekly monitoring and attendance at key project meetings.
- Convene Risk Assessment Committee meeting.
- Complete risk analysis summary report.
- Complete work on Rail Activation risk register.

THIS PAGE INTENTIONALLY LEFT BLANK

12.0 ENVIRONMENTAL

12.1. Permits

The PCEP has obtained the required environmental permits from the following agencies/federal regulations: Section 106 of the National Historic Preservation Act of 1966 (NHPA), Section 7 of the Endangered Species Act (ESA), United States Army Corps of Engineers, San Francisco Bay Regional Water Quality Control Board (SFWQCB), the California Department of Fish and Wildlife, and the San Francisco Bay Conservation Development Commission.

Activity This Month

- None

Activity Next Month

- None

12.2. Mitigation Monitoring and Reporting Program (MMRP)

The California Environmental Quality Act (CEQA) requires that a Lead Agency establish a program to monitor and report on mitigation measures that it has adopted as part of the environmental review process. The PCEP team has prepared a MMRP to ensure that mitigation measures identified in the PCEP Environmental Impact Report are fully implemented during project implementation. PCEP will implement the mitigation measures through its own actions, those of the DB contractor and actions taken in cooperation with other agencies and entities. The status of each mitigation measure in the MMRP is included in Appendix G.

Activity This Month

- Environmental compliance monitors were present during project activities (OCS pole foundation installation, potholing for utility location, grading, tree trimming/removal, conduit installation, abandoned signal cable removal) occurring in areas that required environmental compliance monitoring. The monitoring was conducted in accordance with measures in the MMRP in an effort to minimize potential impacts on sensitive environmental resources.
- Noise and vibration monitoring also occurred during project activities, and non-hazardous soil was removed from the right of way (ROW).
- Environmentally Sensitive Area (ESA) delineation (staking and/or fencing) occurred to delineate jurisdictional waterways and other potentially sensitive areas that should be avoided during upcoming construction activities. Pre-construction nesting bird surveys during the nesting bird season continued (nesting bird season is defined as February 1 through September 15), and protocol-level surveys for a sensitive avian species continued at previously identified potential habitat locations. Wildlife exclusion fencing installation and monitoring occurred adjacent to portions of the alignment designated for wildlife exclusion fencing. Protocol-level surveys for a sensitive avian species were initiated at previously identified potential habitat locations.

Peninsula Corridor Electrification Project

Monthly Progress Report

- Best management practices (BMPs) installation and maintenance (e.g., silt fencing, straw wattles with no monofilament netting per wildlife agency permit requirements, soil covers, etc.) occurred at equipment staging areas and other work areas throughout the alignment in accordance with the project-specific Stormwater Pollution Prevention Plan (SWPPP). In addition, an asbestos pipe was safely removed and disposed of by a certified asbestos contractor, under the supervision of a certified asbestos consultant.

Activity Next Month

- Environmental compliance monitors will continue to monitor project activities (OCS pole foundation installation, pot holing for utility location, tree trimming/removal, conduit installation, utility removal, abandoned signal cable removal, etc.) occurring in areas that require environmental compliance monitoring in an effort to minimize potential impacts on sensitive environmental resources in accordance with the MMRP.
- Noise and vibration monitoring of project activities will continue to occur and non-hazardous soil will continue to be removed.
- Biological surveyors will continue to conduct pre-construction surveys for sensitive wildlife species ahead of project activities. Pre-construction nesting bird surveys during the nesting bird season will continue (nesting bird season is defined as February 1 through September 15), and protocol-level surveys for sensitive avian species will continue for the 2020 breeding season at previously identified potential habitat locations. BMPs.
- BMPs installation will continue in accordance with the project-specific SWPPP, and ESA staking and fencing will continue to occur, to delineate jurisdictional waterways, and other potentially sensitive areas, that should be avoided during upcoming project activities.
- Wildlife exclusion fencing will continue to be installed and maintained prior to upcoming construction activities adjacent to potentially suitable habitat for sensitive wildlife species.
- In accordance with the specifications provided by a certified Asbestos Consultant during the previous reporting periods, the removal and disposal of subsurface piping by a certified Asbestos Contractor, as well as the associated monitoring by the certified Asbestos Consultant, is anticipated to occur next reporting period.

13.0 UTILITY RELOCATION

Implementation of the PCEP requires relocation or rerouting of both public and private utility lines and/or facilities. Utility relocation will require coordination with many entities, including regulatory agencies, public safety agencies, federal, state, and local government agencies, private and public utilities, and other transportation agencies and companies. This section describes the progress specific to the utility relocation process.

Activity This Month

- Worked with all utilities on review of overhead utility line relocations based on the current design.
- Coordinated with individual utility companies on relocation plans and schedule for incorporation with Master Program Schedule.
- Coordinated work with communications utilities on review of relocation design and prioritization of relocations.
- Continued to coordinate relocation work for SVP and Palo Alto Power facilities. Palo Alto has issued bids for their relocation and is still projecting to complete their relocations by September 2020. Any temporary shutdowns required by PCEP prior to that date will be coordinated with Palo Alto.
- Continued to coordinate relocation by communication cable owners such as AT&T and Comcast.
- Conducted utility coordination meeting to discuss overall status and areas of potential concern from the utilities.

Activity Next Month

- Coordinate with individual utility owners on the next steps of relocations, including support of any required design information.
- Update the relocation schedule as information becomes available from the utility owners.
- Continue to review relocation design SVP, Palo Alto Power, and communications companies and coordinate relocation field work.
- Continue communication relocations in all Segments.
- Continue SVP and Palo Alto Power relocations in Segment 3.

THIS PAGE INTENTIONALLY LEFT BLANK

14.0 REAL ESTATE

The PCEP requires the acquisition of a limited amount of real estate. In general, Caltrain uses existing Right of Way (ROW) for the PCEP, but in certain locations, will need to acquire small portions of additional real estate to expand the ROW to accommodate installation of OCS supports (fee acquisitions or railroad easements) and associated Electrical Safety Zones (ESZ) (easements). There are two larger full acquisition areas required for wayside facilities. The PCEP Real Estate team manages the acquisition of all property rights. Caltrain does not need to acquire real estate to complete the EMU procurement portion of the PCEP.

Of the parcels identified at the beginning of the project, there remain only five owners from whom the agency requires possession.

The Real Estate team's current focus is working to identify new parcels and acquire them in conjunction with the project schedule.

- Staff has defined a process to ensure that BBII conveys new needs as soon as possible.
 - BBII must justify and JPB must approve all new parcels.
- Design needs to progress to enable BBII to identify exact acquisition areas.
- Staff is conducting pre-acquisition activities as appropriate.
- JPB has approved four new parcels to date.

Activity This Month

- Reached settlement agreement with Willowbend Apartment's legal counsel. Staff is reviewing purchase agreement comments.
- Staff continues to review potential new pole locations and providing feedback to the design team.
- Staff engaged internal signal team and BBII signal team to determine potential Real Estate interests.
- Review of proposed ESZs from BBII.
- Preparation of First Written Offer package for KB Homes. Reviewed ESZ requirements for KB Homes to confirm acquisitions.
- Through the Real Estate weekly meetings and the BBII bi-weekly meetings, the need for additional acquisition on the Sonora Gray parcel were eliminated.
- Reviewing parcel acquisition options for Marchese parcel with Santa Clara Valley Water District.
- Finalized design for Diridon Hospitality.
- Staff is actively working with PG&E and VTA to gain access to their properties for potholing. Submitted acquisition information package/plan to PG&E for their review and started appraisal of PG&E property based on revised design from BBII.
- Finalizing appraisal map for Britannia Gateway, which requires PG&E approval.

Activity Next Month

- Continue to negotiate for all open parcels.
- Make First Written Offer to KB Homes.
- Work with attorney for Willowbend to close escrow.
- Continue review of ESZ needs submitted by BBII compared to direction from contract.
- Continue to meet with internal signal team and BBII signal team to determine potential Real Estate needs.
- Finalize appraisals for PG&E parcel, Google parcel, and South San Francisco parcel and make offers.
- Send updated Grant Deeds to Stephens reflecting the new legal descriptions.
- Safety group to coordinate with VTA safety to comply with their permitting requirements.
- Adopt Resolution of Necessity for Diridon Hospitality.
- Continue to work with Segment 3 and 4 owners for early access to pothole.
- Make offers on the parcel for which appraisals have been completed.
- Actively participate in Foundation/Pothole and Gannett Fleming weekly meetings.
- Continue to work with project team to identify and analyze new potential parcels.
- Map newly identified parcels.

15.0 THIRD PARTY AGREEMENTS

Third-party coordination is necessary for work impacting public infrastructure, utilities, ROW acquisitions, and others. Table 15-1 below outlines the status of necessary agreements for the PCEP.

Table 15-1 Third-Party Agreement Status

Type	Agreement	Third-Party	Status
Governmental Jurisdictions	Construction & Maintenance ¹	City & County of San Francisco	Executed
		City of Brisbane	Executed
		City of South San Francisco	Executed
		City of San Bruno	Executed
		City of Millbrae	Executed
		City of Burlingame	Executed
		City of San Mateo	Executed
		City of Belmont	Executed
		City of San Carlos	Executed
		City of Redwood City	Executed
		City of Atherton	In Process
		County of San Mateo	Executed
		City of Menlo Park	Executed
		City of Palo Alto	Executed
		City of Mountain View	Executed
		City of Sunnyvale	Executed
		City of Santa Clara	Executed
	County of Santa Clara	Executed	
	City of San Jose	Executed	
	Condemnation Authority	San Francisco	In Process
San Mateo		Executed	
Santa Clara		Executed	
Utilities	Infrastructure	PG&E	Executed
	Operating Rules	CPUC	Executed
Transportation & Railroad	Construction & Maintenance	Bay Area Rapid Transit	Executed ²
	Construction & Maintenance	California Dept. of Transportation (Caltrans)	Not needed ³
	Trackage Rights	UPRR	Executed ²

Notes regarding table above:

1. Agreements memorialize the parties' consultation and cooperation, designate respective rights and obligations and ensure cooperation between the JPB and the 17 cities and three counties along the Caltrain ROW and within the PCEP limits in connection with the design and construction of the PCEP.
2. Utilizing existing agreements.
3. Caltrans Peer Process utilized. Formal agreement not needed.

THIS PAGE INTENTIONALLY LEFT BLANK

16.0 GOVERNMENT AND COMMUNITY AFFAIRS

The Community Relations and Outreach team coordinates all issues with all jurisdictions, partner agencies, government organizations, businesses, labor organizations, local agencies, residents, community members, other interested parties, and the media. In addition, the team oversees the BBII's effectiveness in implementing its Public Involvement Program. The following PCEP-related external affairs meetings took place this month:

Presentations/Meetings

- Caltrain Citizen's Advisory Committee

Third Party/Stakeholder Actions

- None

THIS PAGE INTENTIONALLY LEFT BLANK

17.0 DISADVANTAGED BUSINESS ENTERPRISE (DBE) PARTICIPATION AND LABOR STATISTICS


BBII proposed that 5.2% (\$36,223,749) of the total DB base contract value (\$696,610,558) would be subcontracted to DBEs.

Activity This Month

As expressed in Figure 17-1 below, to date BBII reports:

- **\$37,498,279** has been paid to DBE subcontractors.
- \$38.51 million of DBE contracts have been awarded (to be verified).
- **5.38%** has been achieved.

Figure 17-1 DBE Participation

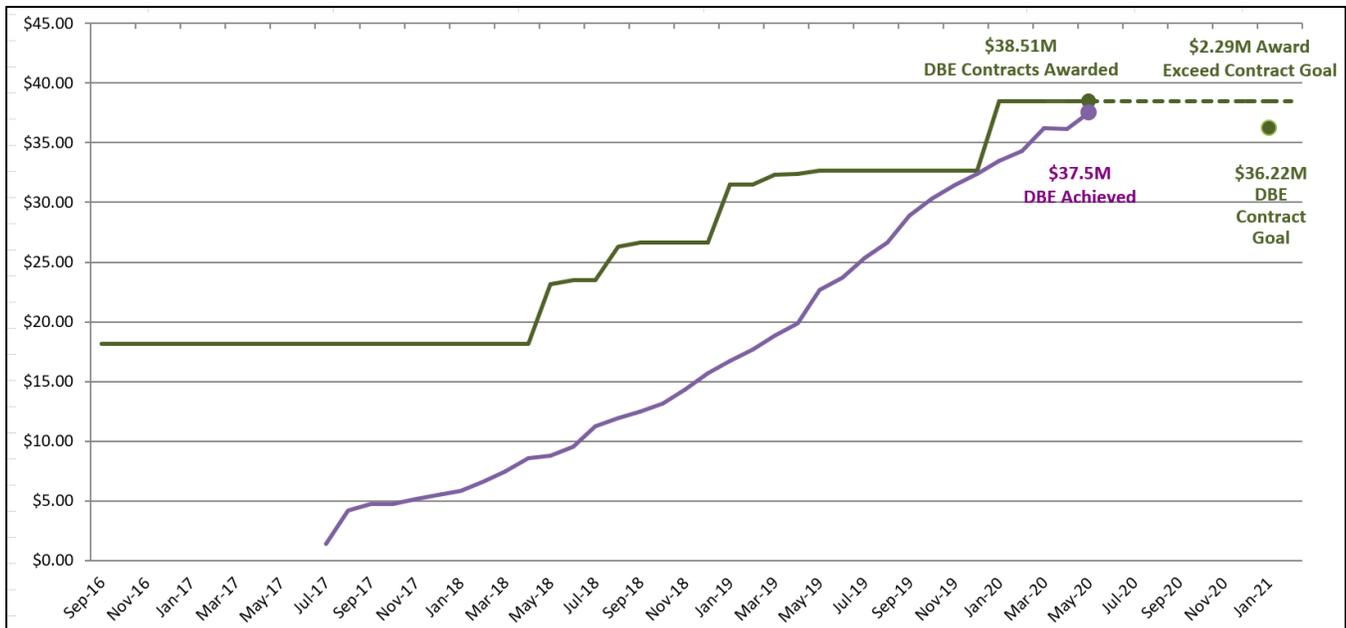

Activity Next Month

BBII has proposed the following key actions:

“In the month of June, 2020, we continue to anticipate increasing our DBE commitments to firms who we are currently negotiating pricing on proposed work or Professional Services Agreements. We are optimistic about the prospect of making future awards to DBE firms. We also anticipate that the existing project work will increase resulting in expanded work for current DBE subcontractors.”

THIS PAGE INTENTIONALLY LEFT BLANK

18.0 PROCUREMENT

Invitation for Bids (IFB)/Request for Quotes (RFQ)/ Request for Proposals (RFP) Issued this Month:

- None

Bids, Quotes, Proposals in Response to IFB/RFQ/RFP Received this Month:

- None

Contract Awards this Month:

- None

Work Directive (WD)/Purchase Order (PO) Awards & Amendments this Month:

- Multiple WDs & POs issued to support the program needs

In Process IFB/RFQ/RFP/Contract Amendments:

- None

Upcoming Contract Awards/Contract Amendments:

- Contract Amendment – On-Call Program Management Services for CalMod
- Contract Amendment – On-Call Electrification Support Services for CalMod

Upcoming IFB/RFQ/RFP to be Issued:

- RFQ – Scissor Lift Work Platform

Existing Contracts Amendments Issued:

- None

THIS PAGE INTENTIONALLY LEFT BLANK

19.0 TIMELINE OF MAJOR PROJECT ACCOMPLISHMENTS

Below is a timeline showing major project accomplishments from 2001 to 2017:

Date	Milestone
2001	Began federal National Environmental Policy Act (NEPA) Environmental Assessment (EA) / state EIR clearance process
2002	Conceptual Design completed
2004	Draft NEPA EA/EIR
2008	35% design complete
2009	Final NEPA EA/EIR and Finding of No Significant Impact (FONSI)
2014	RFQ for electrification RFI for EMU
2015	JPB approves final CEQA EIR JPB approves issuance of RFP for electrification JPB approves issuance of RFP for EMU Receipt of proposal for electrification FTA approval of Core Capacity Project Development
2016	JPB approves EIR Addendum #1: PS-7 FTA re-evaluation of 2009 FONSI Receipt of electrification best and final offers Receipt of EMU proposal Application for entry to engineering to FTA Completed the EMU Buy America Pre-Award Audit and Certification Negotiations completed with Stadler for EMU vehicles Negotiations completed with BBII, the apparent best-value electrification firm JPB approves contract award (LNTP) to BBII JPB approves contract award (LNTP) to Stadler FTA approval of entry into engineering for the Core Capacity Program Application for FFGA
2017	FTA finalized the FFGA for \$647 million in Core Capacity funding, met all regulatory requirements including end of Congressional Review Period (February) FTA FFGA executed, committing \$647 million to the project (May) JPB approves \$1.98 billion budget for PCEP (June) Issued NTP for EMUs to Stadler (June 1) Issued NTP for electrification contract to BBII (June 19) Construction began (August) EMU manufacturing began (October) Issued NTP for SCADA to Rockwell Collins (ARINC) (October) Issued NTP for CEMOF Facility Upgrades to HNTB (November)

Peninsula Corridor Electrification Project
Monthly Progress Report

Date	Milestone
2018	Completed all PG&E agreements JPB approves contract award to Mitsui for the purchase of electric locomotives and Amtrak for overhaul services, storage, acceptance testing, training, and shipment of locomotive to CEMOF JPB approves authorization for the Executive Director to negotiate final contract award to ProVen for tunnel modifications and track rehabilitation project JPB approves contract award (LNTP) to ProVen for tunnel modifications Issued NTP to ProVen for tunnel modifications (October) Amended contract with ProVen to include OCS in the tunnels (November)
2019	JPB approves contract award to ProVen for CEMOF modifications (February) JPB approves LNTP to ProVen for CEMOF modifications (April) JPB approves NTP to ProVen for CEMOF modifications (September)
2020	JPB approves agreement amendment to PG&E for interconnection construction JPB executes agreement with PG&E for interconnection construction (May) FRA approved the waiver for Alternative Vehicle Technology regarding crashworthiness of EMU cars.

APPENDICES

THIS PAGE INTENTIONALLY LEFT BLANK

Appendix A – Acronyms

THIS PAGE INTENTIONALLY LEFT BLANK

AIM	Advanced Information Management	EA	Environmental Assessment
ARINC	Aeronautical Radio, Inc.	EAC	Estimate at Completion
BAAQMD	Bay Area Air Quality Management District	EIR	Environmental Impact Report
BBII	Balfour Beatty Infrastructure, Inc.	EOR	Engineer of Record
CAISO	California Independent System Operator	EMU	Electric Multiple Unit
CalMod	Caltrain Modernization Program	ESA	Endangered Species Act
Caltrans	California Department of Transportation	ESA	Environmental Site Assessments
CDFW	California Department of Fish and Wildlife	FAI	First Article Inspection
CEMOF	Centralized Equipment Maintenance and Operations Facility	FEIR	Final Environmental Impact Report
CEQA	California Environmental Quality Act (State)	FNTP	Full Notice to Proceed
CHSRA	California High-Speed Rail Authority	FFGA	Full Funding Grant Agreement
CIP	Capital Improvement Plan	FONSI	Finding of No Significant Impact
CNPA	Concurrent Non-Project Activity	FRA	Federal Railroad Administration
CPUC	California Public Utilities Commission	FTA	Federal Transit Administration
CTC	Centralized Traffic Control	GO	General Order
DB	Design-Build	HSR	High Speed Rail
DBB	Design-Bid-Build	ICD	Interface Control Document
DBE	Disadvantaged Business Enterprise	IFC	Issued for Construction
DEMP	Design, Engineering, and Management Planning	ITS	Intelligent Transportation System
		JPB	Peninsula Corridor Joint Powers Board
		LNTP	Limited Notice to Proceed

Peninsula Corridor Electrification Project
Monthly Progress Report

MMRP	Mitigation, Monitoring, and Reporting Program	RFI	Request for Information
		RFP	Request for Proposals
MOU	Memorandum of Understanding	RFQ	Request for Qualifications
MPS	Master Program Schedule	ROCS	Rail Operations Center System
NCR	Non Conformance Report	ROW	Right of Way
NEPA	National Environmental Policy Act (Federal)	RRP	Railroad Protective Liability
NHPA	National Historic Preservation Act	RSD	Revenue Service Date
NMFS	National Marine Fisheries Service	RWP	Roadway Worker Protection
NTP	Notice to Proceed	SamTrans	San Mateo County Transit District
OCS	Overhead Contact System	SCADA	Supervisory Control and Data Acquisition
PCEP	Peninsula Corridor Electrification Project	SCC	Standard Cost Code
PCJPB	Peninsula Corridor Joint Powers Board	SPUR	San Francisco Bay Area Planning and Urban Research Association
PG&E	Pacific Gas and Electric	SFBCDC	San Francisco Bay Conservation Development Commission
PHA	Preliminary Hazard Analysis	SFCTA	San Francisco County Transportation Authority
PMOC	Project Management Oversight Contractor	SFMTA	San Francisco Municipal Transportation Authority
PS	Paralleling Station	SFRWQCB	San Francisco Regional Water Quality Control Board
PTC	Positive Train Control	SOGR	State of Good Repair
QA	Quality Assurance	SSCP	Safety and Security Certification Plan
QC	Quality Control	SSMP	Safety and Security Management Plan
QMP	Quality Management Plan	SSWP	Site Specific Work Plan
QMS	Quality Management System		
RAMP	Real Estate Acquisition Management Plan		
RE	Real Estate		

SWS	Switching Station
TASI	TransitAmerica Services Inc.
TBD	To Be Determined
TPS	Traction Power Substation
TVA	Threat and Vulnerability Assessment
UPRR	Union Pacific Railroad
USACE	United States Army Corp of Engineers
USFWS	U.S. Fish and Wildlife Service
VTA	Santa Clara Valley Transportation Authority

THIS PAGE INTENTIONALLY LEFT BLANK

Appendix B – Funding Partner Meetings

THIS PAGE INTENTIONALLY LEFT BLANK

Funding Partner Meeting Representatives
Updated April 21, 2020

Agency	CHSRA	MTC	SFCTA/SFMTA/CCSF	SMCTA	VTA
FTA Quarterly Meeting	<ul style="list-style-type: none"> • Boris Lipkin • Simon Whitehorn • Wai Siu (info only) 	<ul style="list-style-type: none"> • Anne Richman 	<ul style="list-style-type: none"> • Luis Zurinaga 	<ul style="list-style-type: none"> • April Chan • Peter Skinner 	<ul style="list-style-type: none"> • Jim Lawson
Funding Partners Quarterly Meeting	<ul style="list-style-type: none"> • Boris Lipkin • Simon Whitehorn • John Popoff 	<ul style="list-style-type: none"> • Trish Stoops 	<ul style="list-style-type: none"> • Luis Zurinaga 	<ul style="list-style-type: none"> • April Chan • Peter Skinner 	<ul style="list-style-type: none"> • Krishna Davey • Edwin Castillo • Franklin Wong
Funding Oversight (monthly)	<ul style="list-style-type: none"> • Kelly Doyle 	<ul style="list-style-type: none"> • Anne Richman • Kenneth Folan 	<ul style="list-style-type: none"> • Anna LaForte • Maria Lombardo • Luis Zurinaga • Monique Webster • Ariel Espiritu Santo 	<ul style="list-style-type: none"> • April Chan • Peter Skinner 	<ul style="list-style-type: none"> • Jim Lawson • Marcella Rensi • Michael Smith
Change Management Board (monthly)	<ul style="list-style-type: none"> • Bruce Armistead • Boris Lipkin • Simon Whitehorn 	<ul style="list-style-type: none"> • Trish Stoops • Kenneth Folan 	<ul style="list-style-type: none"> • Luis Zurinaga • Tilly Chang (info only) 	<ul style="list-style-type: none"> • Joe Hurley 	<ul style="list-style-type: none"> • Krishna Davey • Edwin Castillo • Franklin Wong • Jim Lawson • Nuria Fernandez (info only)
Master Program Schedule Update (monthly)	<ul style="list-style-type: none"> • Wai Siu 	<ul style="list-style-type: none"> • Trish Stoops 	<ul style="list-style-type: none"> • Luis Zurinaga 	<ul style="list-style-type: none"> • Joe Hurley 	<ul style="list-style-type: none"> • Jim Lawson
Risk Assessment Committee (monthly)	<ul style="list-style-type: none"> • Wai Siu 	<ul style="list-style-type: none"> • Trish Stoops 	<ul style="list-style-type: none"> • Luis Zurinaga 	<ul style="list-style-type: none"> • Joe Hurley 	<ul style="list-style-type: none"> • Krishna Davey • Edwin Castillo • Franklin Wong
PCEP Delivery Coordination Meeting (bi-weekly)	<ul style="list-style-type: none"> • Wai Siu 	<ul style="list-style-type: none"> • Trish Stoops 	<ul style="list-style-type: none"> • Luis Zurinaga 	<ul style="list-style-type: none"> • Joe Hurley 	<ul style="list-style-type: none"> • Krishna Davey • Edwin Castillo • Franklin Wong
Systems Integration Meeting (bi-weekly)	<ul style="list-style-type: none"> • Wai Siu 	<ul style="list-style-type: none"> • Trish Stoops 	<ul style="list-style-type: none"> • Luis Zurinaga 	<ul style="list-style-type: none"> • Joe Hurley 	<ul style="list-style-type: none"> • Krishna Davey • Edwin Castillo • Franklin Wong

THIS PAGE INTENTIONALLY LEFT BLANK

Appendix C – Schedule

THIS PAGE INTENTIONALLY LEFT BLANK

Appendix D – Standard Cost Codes

THIS PAGE INTENTIONALLY LEFT BLANK

Peninsula Corridor Electrification Project Monthly Progress Report

Description of Work	FFGA Baseline Budget (A)	Approved Budget (B)	Cost This Month (C)	Cost To Date (D)	Estimate To Complete (E)	Estimate At Completion (F) = (D) + (E)
10 - GUIDEWAY & TRACK ELEMENTS	\$14,256,739	\$27,308,610	\$9,601	\$24,946,946	\$2,854,053	\$27,800,999
10.02 Guideway: At-grade semi-exclusive (allows cross-traffic)	\$2,500,000	\$2,500,000	\$9,601	\$139,054	\$2,360,946	\$2,500,000
10.07 Guideway: Underground tunnel	\$8,110,649	\$24,808,610	\$0	\$24,807,892	\$493,107	\$25,300,999
10.07 Allocated Contingency	\$3,646,090	\$0	\$0	\$0	\$0	\$0
30 - SUPPORT FACILITIES: YARDS, SHOPS, ADMIN. BLDGS	\$2,265,200	\$6,756,604	\$310,499	\$3,309,931	\$4,785,606	\$8,095,538
30.03 Heavy Maintenance Facility	\$1,344,000	\$6,756,604	\$310,499	\$3,309,931	\$4,785,606	\$8,095,538
30.03 Allocated Contingency	\$421,200	\$0	\$0	\$0	\$0	\$0
30.05 Yard and Yard Track	\$500,000	\$0	\$0	\$0	\$0	\$0
40 - SITEWORK & SPECIAL CONDITIONS	\$255,072,402	\$270,749,520	\$4,319,610	\$176,419,505	\$97,552,673	\$273,972,177
40.01 Demolition, Clearing, Earthwork	\$3,077,685	\$3,077,685	(\$762,500)	\$4,567,500	(\$1,489,815)	\$3,077,685
40.02 Site Utilities, Utility Relocation	\$62,192,517	\$93,328,599	\$3,375,705	\$85,304,433	\$9,024,166	\$94,328,599
40.02 Allocated Contingency	\$25,862,000	(\$0)	\$0	\$0	(\$0)	(\$0)
40.03 Haz. mat'l, contam'd soil removal/mitigation, ground water treatments	\$2,200,000	\$4,944,961	\$145,872	\$6,523,924	(\$1,578,963)	\$4,944,961
40.04 Environmental mitigation, e.g. wetlands, historic/archeologic, parks	\$32,579,208	\$32,954,208	\$126,375	\$2,069,745	\$30,884,463	\$32,954,208
40.05 Site structures including retaining walls, sound walls	\$568,188	\$568,188	\$0	\$0	\$568,188	\$568,188
40.06 Pedestrian / bike access and accommodation, landscaping	\$804,933	\$764,933	\$0	\$0	\$764,933	\$764,933
40.07 Automobile, bus, van accessways including roads, parking lots	\$284,094	\$284,094	\$0	\$0	\$284,094	\$284,094
40.08 Temporary Facilities and other indirect costs during construction	\$107,343,777	\$114,216,852	\$1,434,158	\$77,953,903	\$39,656,653	\$117,610,556
40.08 Allocated Contingency	\$20,160,000	\$20,610,000	\$0	\$0	\$19,438,953	\$19,438,953
50 - SYSTEMS	\$504,445,419	\$523,118,617	\$3,523,096	\$167,748,816	\$371,785,803	\$539,534,620
50.01 Train control and signals	\$97,589,149	\$100,749,268	(\$1,413,643)	\$30,180,943	\$71,824,862	\$102,005,805
50.01 Allocated Contingency	\$1,651,000	\$0	\$0	\$0	\$0	\$0
50.02 Traffic signals and crossing protection	\$23,879,905	\$23,879,905	\$0	\$0	\$23,879,905	\$23,879,905
50.02 Allocated Contingency	\$1,140,000	\$1,140,000	\$0	\$0	\$1,140,000	\$1,140,000
50.03 Traction power supply: substations	\$69,120,009	\$97,744,787	(\$8,733)	\$34,619,024	\$63,387,788	\$98,006,812
50.03 Allocated Contingency	\$31,755,013	\$2,990,895	\$0	\$0	\$2,763,958	\$2,763,958
50.04 Traction power distribution: catenary and third rail	\$253,683,045	\$276,373,056	\$4,945,471	\$102,890,860	\$201,124,861	\$304,015,721
50.04 Allocated Contingency	\$18,064,000	\$12,677,408	\$0	\$0	\$159,120	\$159,120
50.05 Communications	\$5,455,000	\$5,455,000	\$0	\$57,989	\$5,397,011	\$5,455,000
50.07 Central Control	\$2,090,298	\$2,090,298	\$0	\$0	\$2,090,298	\$2,090,298
50.07 Allocated Contingency	\$18,000	\$18,000	\$0	\$0	\$18,000	\$18,000
60 - ROW, LAND, EXISTING IMPROVEMENTS	\$35,675,084	\$35,675,084	\$55,104	\$19,055,444	\$16,619,640	\$35,675,084
60.01 Purchase or lease of real estate	\$25,927,074	\$25,927,074	\$55,104	\$18,926,870	\$7,080,205	\$26,007,074
60.01 Allocated Contingency	\$8,748,010	\$8,748,010	\$0	\$0	\$8,668,010	\$8,668,010
60.02 Relocation of existing households and businesses	\$1,000,000	\$1,000,000	\$0	\$128,574	\$871,426	\$1,000,000
70 - VEHICLES (96)	\$625,544,147	\$624,682,944	\$5,286,462	\$208,212,818	\$415,013,473	\$623,226,291
70.03 Commuter Rail	\$589,167,291	\$592,028,797	\$5,286,462	\$207,674,538	\$386,298,236	\$593,972,774
70.03 Allocated Contingency	\$9,472,924	\$5,822,395	\$0	\$0	\$2,421,765	\$2,421,765
70.06 Non-revenue vehicles	\$8,140,000	\$8,067,821	\$0	\$538,280	\$7,529,541	\$8,067,821
70.07 Spare parts	\$18,763,931	\$18,763,931	\$0	\$0	\$18,763,931	\$18,763,931
80 - PROFESSIONAL SERVICES (applies to Cats. 10-50)	\$323,793,010	\$333,280,065	\$2,702,116	\$300,763,953	\$53,655,034	\$354,418,986
80.01 Project Development	\$130,350	\$130,350	\$0	\$280,180	(\$149,830)	\$130,350
80.02 Engineering (not applicable to Small Starts)	\$180,227,311	\$187,751,436	\$735,308	\$196,403,760	(\$3,970,151)	\$192,433,609
80.02 Allocated Contingency	\$1,866,000	\$202,474	\$0	\$0	\$21,942	\$21,942
80.03 Project Management for Design and Construction	\$72,029,265	\$74,932,188	\$1,149,725	\$76,507,634	\$21,716,917	\$98,224,551
80.03 Allocated Contingency	\$9,388,080	\$8,000,396	\$0	\$0	(\$0)	(\$0)
80.04 Construction Administration & Management	\$23,677,949	\$27,056,839	\$712,842	\$17,742,087	\$20,313,433	\$38,055,520
80.04 Allocated Contingency	\$19,537,000	\$16,158,109	\$0	\$0	\$5,159,428	\$5,159,428
80.05 Professional Liability and other Non-Construction Insurance	\$3,500,000	\$4,581,851	\$0	\$4,581,851	\$0	\$4,581,851
80.06 Legal; Permits; Review Fees by other agencies, cities, etc.	\$7,167,275	\$8,651,684	\$106,758	\$5,211,099	\$4,785,897	\$9,996,996
80.06 Allocated Contingency	\$556,000	\$0	\$0	\$0	\$0	\$0
80.07 Surveys, Testing, Investigation, Inspection	\$3,287,824	\$3,388,781	(\$2,518)	\$37,341	\$3,351,440	\$3,388,781
80.08 Start up	\$1,797,957	\$1,797,957	\$0	\$0	\$1,797,957	\$1,797,957
80.08 Allocated Contingency	\$628,000	\$628,000	\$0	\$0	\$628,000	\$628,000
Subtotal (10 - 80)	\$1,761,052,001	\$1,821,571,445	\$16,206,487	\$900,457,412	\$962,266,282	\$1,862,723,695
90 - UNALLOCATED CONTINGENCY	\$162,620,295	\$99,200,850	\$0	\$0	\$58,048,601	\$58,048,601
Subtotal (10 - 90)	\$1,923,672,296	\$1,920,772,296	\$16,206,487	\$900,457,412	\$1,020,314,884	\$1,920,772,296
100 - FINANCE CHARGES	\$6,998,638	\$9,898,638	\$31,763	\$6,274,058	\$3,624,580	\$9,898,638
Total Project Cost (10 - 100)	\$1,930,670,934	\$1,930,670,934	\$16,238,251	\$906,731,470	\$1,023,939,464	\$1,930,670,934

THIS PAGE INTENTIONALLY LEFT BLANK

Appendix E – Change Order Logs

THIS PAGE INTENTIONALLY LEFT BLANK

**Peninsula Corridor Electrification Project
Monthly Progress Report**

Change Order Logs

Electrification Contract

Change Order Authority (5% of BBII Contract)

5% x \$696,610,558 = \$34,830,528

Date	Change Number	Description	CCO Amount	Change Order Authority Usage ¹	Remaining Authority
08/31/17	BBI-053-CCO-001	Track Access Delays Q4 2016	\$85,472	0.25%	\$34,745,056
02/28/18	BBI-053-CCO-003	Deletion of Signal Cable Meggering (Testing)	(\$800,000)	(2.30%)	\$35,545,056
02/21/18	BBI-053-CCO-004	Field Order for Differing Site Condition Work Performed on 6/19/17	\$59,965	0.17%	\$35,485,091
03/12/18	BBI-053-CCO-006	Track Access Delays for Calendar Quarter 1 2017	\$288,741	0.83%	\$35,196,350
04/24/18	BBI-053-CCO-002	Time Impact 01 Associated with Delayed NTP	\$9,702,667	0.00% ²	-
04/24/18	BBI-053-CCO-008	2016 Incentives (Safety, Quality, and Public Outreach)	\$750,000	0.00% ²	-
05/31/18	BBI-053-CCO-009	16th St. Grade Crossing Work Removal from BBII Contract	(\$685,198)	(1.97%)	\$35,881,548
05/31/18	BBI-053-CCO-012	2017 Incentives (Safety, Quality, and Public Outreach)	\$1,025,000	0.00% ²	-
06/25/18	BBI-053-CCO-010	Pothole Change Of Shift	\$300,000	0.86%	\$35,581,548
06/25/18	BBI-053-CCO-013	Field Order for Signal Cable Relocation (FO# 31)	\$95,892	0.28%	\$35,485,656
06/25/18	BBI-053-CCO-015	TASI Pilot Transportation 2017	\$67,345	0.19%	\$35,418,311
06/26/18	BBI-053-CCO-005	Field Orders for Signal Cable Relocation (FO#s 26, 30)	\$191,836	0.55%	\$35,226,475
06/28/18	BBI-053-CCO-014	Field Orders for Signal Cable Relocation (FO-36 & FO-38)	\$145,694	0.42%	\$35,080,781
06/29/18	BBI-053-CCO-007	Track Access Delays for Calendar Quarter 2 2017	\$297,512	0.85%	\$34,783,269
06/29/18	BBI-053-CCO-011	Field Orders for Differing Site Condition (FO#s Partial 07A , 08-14)	\$181,013	0.52%	\$34,602,256
06/29/18	BBI-053-CCO-017	Field Order for NorCal Utility Potholing (FO# 27)	\$93,073	0.27%	\$34,509,183
06/29/18	BBI-053-CCO-018	Field Order for NorCal Utility Potholing (FO# 29)	\$76,197	0.22%	\$34,432,986
06/29/18	BBI-053-CCO-020	Field Orders for Differing Site Condition (FO#s 15-19)	\$118,364	0.34%	\$34,314,622
7/19/2018	BBI-053-CCO-019	Field Order for NorCal Utility Potholing (FO-032)	\$88,956	0.26 %	\$34,225,666
7/19/2018	BBI-053-CCO-021	As In-Service (AIS) Drawings for Segment 2 and 4 Signal Design (CN-009)	\$105,000	0.30 %	\$34,120,666
7/25/2018	BBI-053-CCO-022	CEMOF Yard Traction Power Feed (CN-008)	\$332,700	0.96 %	\$33,787,966
7/31/2018	BBI-053-CCO-028	Sonic Echo Impulse Testing	\$4,541	0.01 %	\$33,783,425
7/31/2018	BBI-053-CCO-026	TASI Pilot Transportation 2018 (CNC-0022)	\$50,409	0.14%	\$33,733,016
7/31/2018	BBI-053-CCO-027	Signal Cable Relocation (FOs-040 & 051)	\$196,114	0.56%	\$33,536,902
9/27/2018	BBI-053-CCO-030	Delete Spare 115k Disconnect Switches	(\$19,000)	(0.05)%	\$33,555,902
9/28/2018	BBI-053-CCO-031	Bldg A HVAC and FOB Card Reader Systems	\$76,500	0.22 %	\$33,479,402
9/28/2018	BBI-053-CCO-025A	Addition of Shunt Wire at Transverse Utility Crossing Locations - Design	\$925,000	2.66 %	\$32,554,402
9/28/2018	BBI-053-CCO-016A	UPRR MT-1 Pole Relocation - Design Changes	\$903,000	0.00% ²	-
9/28/2018	BBI-053-CCO-024A	PG&E Utility Feed Connection to TPS#1 and TPS#2 (Design Only)	\$727,000	0.00% ²	-
12/17/2018	BBI-053-CCO-032	PS-2 Site Relocation (Design Only)	\$291,446	0.84%	\$32,262,956
1/17/2019	BBI-053-CCO-023	Insulated Rail Joints	\$2,694,519	0.00% ²	-
1/17/2019	BBI-053-CCO-029	CHSRA Early Pole Relocation (Design Only)	\$625,000	0.00% ^{2,3}	-
2/5/2019	BBI-053-CCO-040A	Increase in Potholing Quantity (unit price contract bid item by 25%)	\$1,662,500	4.77 %	\$30,600,456

Peninsula Corridor Electrification Project
Monthly Progress Report

Change Order Authority (5% of BBII Contract)

5% x \$696,610,558 = \$34,830,528

Date	Change Number	Description	CCO Amount	Change Order Authority Usage ¹	Remaining Authority
3/5/2019	BBI-053-CCO-042A	TPSS-2 VTA/BART Pole Relocation (Design Only) (CNPA funded by VTA)	\$110,000	0.32% ³	\$30,490,456
3/11/2019	BBI-053-CCO-036	Field Order for Signal Cable Relocation (FO-064)	\$86,538	0.25%	\$30,403,918
3/20/2019	BBI-053-CCO-035	Millbrae Avenue Existing Overhead Barrier	(\$40,000)	(0.11)%	\$30,443,918
3/19/2019	BBI-053-CCO-046	Training in Design Software and Potholing	\$136,611	0.39%	\$30,307,307
4/8/2019	BBI-053-CCO-041	Grade Crossing Warning System (CN59) – 5 mph Speed Check	\$446,982	1.28%	\$29,860,325
5/30/2019	BBI-053-CCO-044	Additional Daytime Potholing (Increase Quantity by 500 in Segment 4)	\$150,000	0.43 %	\$29,710,325
6/6/2019	BBI-053-CCO-048	Power Metering Devices	\$101,908	0.29 %	\$29,608,417
6/13/2019	BBI-053-CCO-045	Incentive Payment for 2018	\$1,025,000	0.00% ²	-
6/13/2019	BBI-053-CCO-024B	PG&E Utility Feed Connection to TPS #1 and TPS#2 (Material On Hand)	\$1,600,000	4.59 %	\$28,008,417
6/24/2019	BBI-053-CCO-043	PS-5 Site Relocation (Design Only)	\$348,000	1.00 %	\$27,660,417
6/24/2019	BBI-053-CCO-054	Change Design Sequence for OCS Foundations	\$37,500	0.11%	\$27,622,917
7/1/2019	BBI-053-CCO-040B	Increase Quantity for Utilities Potholing (Bid Item #9)	\$1,867,700	5.36 %	\$25,755,217
7/10/2019	BBI-053-CCO-033A	Relocation of PS3 (Design) (CNPA funded by BGSP)	\$500,000	1.44 % ³	\$25,255,217
8/15/2019	BBI-053-CCO-047	CEMOF Slot Drains (Design Only)	\$69,000	0.20%	\$25,186,217
8/16/2019	BBI-053-CCO-055	Sheriff's Deputy in Segment 4B	\$4,644	0.01%	\$25,181,573
9/3/2019	BBI-053-CCO-037	Field Orders for Signal Cable Relocation (FO-053 & FO-059)	\$184,576	0.53%	\$24,996,997
9/7/2019	BBI-053-CCO-057	Mediator with Technical Expertise	\$0	0.00%	\$24,996,997
9/27/2019	BBI-053-CCO-061	Interconnect Renaming of Circuit Numbers	\$58,058	0.17%	\$24,938,939
9/27/2019	BBI-053-CCO-063A	Track Access Delays - Quarter 1 2018 (Partial)	\$343,496	0.99%	\$24,595,443
10/21/2019	BBI-053-CCO-064	TPS-2 VTA Pole Height Redesign (CNPA funded by VTA)	\$31,000	0.09% ³	\$24,564,443
11/15/2019	BBI-053-CCO-038	Field Order for Signal Cable Relocation (FO-079 & FO-085)	\$187,764	0.54 %	\$24,376,680
11/26/2019	BBI-053-CCO-025B	Addition of OCS Shunt Wires in Segments 2 & 4 - Wire Assembly Materials Only	\$144,370	0.41 %	\$24,232,310
12/11/2019	BBI-053-CCO-065A	Foundation Inefficiencies S2WA5	\$401,501	1.15%	\$23,830,809
12/17/2019	BBI-053-CCO-025C	Addition of OCS Shunt Wires in Segments 2 & 4 – Pole Assembly Materials Only	\$884,500	2.54 %	\$22,946,309
1/7/2020	BBI-053-CCO-066A	Increase Quantity for Contaminated Soils (Bid Unit Price Item #1)	\$950,000	2.73 %	\$21,996,309
2/5/2020	BBI-053-CCO-023B	Insulated Rail Joints De-stressing	\$890,600	2.56 %	\$21,105,709
3/18/2020	BBI-053-CCO-072A	SVP Requirements for Joint SIS & SPS (Task 1)	\$80,000	0.23 %	\$21,025,709
3/19/2020	BBI-053-CCO-023C	Portec Insulated Rail Joints	\$375,000	1.08 %	\$20,650,709
3/26/2020	BBI-053-CCO-076	Asbestos Pipe Abatement at CP Shark	\$145,872	0.42 %	\$20,504,837
3/31/2020	BBI-053-CCO-075	Norcal Utility Potholing (FO#39)	\$98,105	0.28 %	\$20,406,733
4/21/2020	BBI-053-CCO-077A	Contaminated Soil (Class 1) at TPS-1	\$701,780	2.01 %	\$19,704,953
4/27/2020	BBI-053-CCO-066B	Increase Quantity for Contaminated Soils (Bid Item #1)	\$926,273	2.66 %	\$18,778,680
4/27/2020	BBI-053-CCO-090A	Signal Cable Relocation (Field Order No. 340)	\$47,258	0.14 %	\$18,731,423
4/27/2020	BBI-053-CCO-091A	Signal Cable Relocation (Field Order No. 340)	\$131,663	0.38 %	\$18,599,759
4/29/2020	BBI-053-CCO-080A	Steel Plates to Protect Utilities (DTDS)	\$135,128	0.39 %	\$18,464,631

**Peninsula Corridor Electrification Project
Monthly Progress Report**

Change Order Authority (5% of BBII Contract)

5% x \$696,610,558 = \$34,830,528

Date	Change Number	Description	CCO Amount	Change Order Authority Usage ¹	Remaining Authority
4/29/2020	BBI-053-CCO-081A	Steel Plates to Protect Utilities (DTDS)	\$95,474	0.27 %	\$18,369,157
4/29/2020	BBI-053-CCO-071	Increase Quantity for Tree Pruning (Bid Unit Price Item #4d)	\$375,000	1.08 %	\$17,994,157
5/1/2020	BBI-053-CCO-050	Switch Machine Isolation - Credit	(\$277,430)	(0.80)%	\$18,271,586
5/19/2020	BBI-053-CCO-092A	Signal Cable Relocation (Field Order No. 340)	\$106,773	0.31 %	\$18,164,814
5/19/2020	BBI-053-CCO-093A	Signal Cable Relocation (Field Order No. 340)	\$90,765	0.26 %	\$18,074,049
5/27/2020	BBI-053-CCO-101	Asbestos Pipe Abatement at 46.3-07/08	\$21,037	0.06 %	\$18,053,012
Total			\$34,229,702	48.17 %	\$18,053,012

Notes:

- ¹ When the threshold of 75% is reached, staff may return to the Board to request additional authority.
- ² Change approved by the Board of Directors – not counted against the Executive Director's Change Order Authority.
- ³ Third party improvements/CNPA projects that are funded with non-PCEP funds.

EMU Contract

Change Order Authority (5% of Stadler Contract)

5% x \$550,899,459 = \$27,544,973

Date	Change Number	Description	CCO Amount	Change Order Authority Usage ¹	Remaining Authority
09/22/2017	STA-056-CCO 001	Contract General Specification and Special Provision Clean-up	\$0	0.00%	-
10/27/2017	STA-056-CCO 002	Prototype Seats and Special Colors	\$55,000	0.20%	\$27,489,973
11/02/2017	STA-056-CCO 003	Car Level Water Tightness Test	\$0	0.00%	-
12/05/2017	STA-056-CCO-004	Onboard Wheelchair Lift 800 Pound Capacity Provisions	\$848,000	3.08%	\$26,641,973
11/03/2017	STA-056-CCO 005	Design Progression (multiple)	\$0	0.00%	-
12/12/2017	STA-056-CCO 006	Prototype Seats and Special Colors	(\$27,500)	(0.10%)	\$26,669,473
01/17/2018	STA-056-CCO 007	Multi-Color Destination Signs	\$130,760	0.47%	\$26,538,713
02/09/2018	STA-056-CCO-008	Adjustment to Delivery and LDs due to delayed FNTP	\$490,000	0.00% ²	-
02/12/2018	STA-056-CCO-009	Ship Cab Mock-up to Caltrain	\$53,400	0.19%	\$26,485,313
04/17/2018	STA-056-CCO-010	Onboard Wheelchair Lift Locations	(\$1,885,050)	(6.84%)	\$28,370,363
04/17/2018	STA-056-CCO-011	Multiple Change Group 3 and Scale Models	\$0	0.00%	-
10/29/2018	STA-056-CCO-012	Multiple Change Group 4	\$0	0.00%	-
10/29/2018	STA-056-CCO-013	Wheelchair Lift Installation Redesign	\$228,400	0.83%	\$28,141,963
12/14/2018	STA-056-CCO-014	PTC System Change	\$0	0.00%	-
12/22/2018	STA-056-CCO-015	EMU Option Cars	\$172,800,047	0.00% ^{2,3}	-
6/26/2019	STA-056-CCO-016	Testing at TTCL (Pueblo Facility) - First Trainset	\$3,106,428	11.28 %	\$25,035,535
8/27/2019	STA-056-CCO-017	Virtual Reality Experience	\$400,000	1.45 %	\$24,635,535
8/21/2019	STA-056-CCO-018	EMI Conducted Emissions Limits	\$0	0.00%	\$24,635,535
8/8/2019	STA-056-CCO-019	Option Car Payment Milestones	\$0	0.00%	\$24,635,535
8/21/2019	STA-056-CCO-020	Multiple No Cost No Schedule Impact Changes Group 5	\$0	0.00%	\$24,635,535
10/28/2019	STA-056-CCO-021	Plugging of High-Level Doorways	\$736,013	2.67%	\$23,899,523
11/13/2019	STA-056-CCO-022	Add Flip-Up Seats into Bike Cars (CNPA: \$1.96M funded by Non-PCEP)	\$1,961,350	7.12% ³	\$21,938,173

Peninsula Corridor Electrification Project
Monthly Progress Report

Change Order Authority (5% of Stadler Contract)				5% x \$550,899,459 = \$27,544,973	
Date	Change Number	Description	CCO Amount	Change Order Authority Usage¹	Remaining Authority
4/21/2020	STA-056-CCO-025	Removal of Vandal Film from Windows	(\$374,994)	(1.36)%	\$22,313,167
5/6/2020	STA-056-CCO-023	Deferral of Wheelchair Lifts	\$632,703	2.30 %	\$21,680,464
Total			\$179,154,556	21.29 %	\$21,680,464

Notes:

1. When the threshold of 75% is reached, staff may return to the Board to request additional authority.
2. Change approved by the Board of Directors – not counted against the Executive Director's Change Order Authority.
3. Third party improvements/CNPA projects that are funded with non-PCEP funds.

SCADA Contract

Change Order Authority (15% of ARINC Contract)				15% x \$3,446,917 = \$517,038	
Date	Change Number	Description	CCO Amount	Change Order Authority Usage¹	Remaining Authority
None to date					
Total			\$0	0.00%	\$517,038

Notes:

1. When the threshold of 75% is reached, staff may return to the Board to request additional authority.
2. Change approved by the Board of Directors – not counted against the Executive Director's Change Order Authority.

Tunnel Modifications Contract

Change Order Authority (10% of ProVen Contract¹)				10% x \$55,077,777 = \$5,507,778	
Date	Change Number	Description	CCO Amount	Change Order Authority Usage²	Remaining Authority
3/27/2019	PROV-070-CCO-003	Track Access Delay	\$25,350	0.46 %	\$5,482,428
3/27/2019	PROV-070-CCO-004	Additional OCS Potholing Due to Conflict with Existing Utilities	\$70,935	1.29 %	\$5,411,493
3/27/2019	PROV-070-CCO-005	Install Tie Backs and Piles in Boulders at Tunnel 4	\$29,478	0.54 %	\$5,382,015
3/28/2019	PROV-070-CCO-001	Partnering Meetings (50% PCEP)	\$14,443	0.26 % ⁴	\$5,367,572
4/25/2019	PROV-070-CCO-002	Furnish Galvanized E-clips	\$37,239	0.68 %	\$5,330,333
4/30/2019	PROV-070-CCO-006	Additional Rock Bolts and Testing	\$22,549	0.41 %	\$5,307,784
5/23/2019	PROV-070-CCO-013	Late Removal of Leaky Feeder Tunnel 4 (T-4)	\$21,225	0.39 %	\$5,286,559
5/28/2019	PROV-070-CCO-014	OCS Piles Utility Conflict at Tunnel-1 South (T-1S)	\$16,275	0.30 %	\$5,270,284
5/29/2019	PROV-070-CCO-012	OCS Piles Utility Conflict at T-4S	\$6,871	0.12 %	\$5,263,413
5/31/2019	PROV-070-CCO-016A	Portal Structure Detailing Changes	\$84,331	1.53 %	\$5,179,082
6/18/2019	PROV-070-CCO-009	Creosote Ties Covering (CNPA - Drainage \$3,116.00)	\$3,116	0.06 % ⁴	\$5,175,966
6/28/2019	PROV-070-CCO-008	Micropiles at South Tunnel-2 South (T-2S)	\$41,322	0.75 %	\$5,134,644
6/28/2019	PROV-070-CCO-010	Salvage Transition Panels (CNPA - Drainage \$6,144.00)	\$6,144	0.11 % ⁴	\$5,128,500
6/28/2019	PROV-070-CCO-011	Demo PVC and Plug Tunnel-1 South (T-1S) (CNPA - Drainage \$4,035.00)	\$4,035	0.07 % ⁴	\$5,124,465
6/28/2019	PROV-070-CCO-020	Unidentified SD Conflict with Junction Inlet (CNPA - Drainage \$1,976.00)	\$1,976	0.04 % ⁴	\$5,122,489
9/26/2019	PROV-070-CCO-007	Canopy Tube Drilling	\$89,787	1.63%	\$5,032,702
9/26/2019	PROV-070-CCO-023	Over-excavate Trapezoidal Ditch at T-1N (CNPA - Drainage \$46,914.00)	\$46,914	0.85% ⁴	\$4,985,788

**Peninsula Corridor Electrification Project
Monthly Progress Report**

Change Order Authority (10% of ProVen Contract¹)

10% x \$55,077,777 = \$5,507,778

Date	Change Number	Description	CCO Amount	Change Order Authority Usage ²	Remaining Authority
10/4/2019	PROV-070-CCO-029	Additional DryFix Pins	\$105,000	1.91%	\$4,880,788
10/4/2019	PROV-070-CCO-021	Out of Sequence Piles	\$185,857	3.37 %	\$4,694,931
10/30/2019	PROV-070-CCO-017	Hard Piping in T-4 (CNPA - Drainage \$2,200.00)	\$2,200	0.04 % ⁴	\$4,692,731
1/25/2020	PROV-070-CCO-027	Grout Quantity Underrun	(\$1,216,000)	(22.08)%	\$5,908,731
1/29/2020	PROV-070-CCO-026	HMAC Quantity Overrun (CNPA - Drainage \$160,000.00)	\$160,000	2.9 % ⁴	\$5,748,731
5/11/2020	PROV-070-CCO-025	NOPC #1 CWR (CNPA - Drainage \$660,000.00)	\$660,000	11.98 % ⁴	\$5,088,731
Total			\$419,047	7.61 %	\$5,088,731

Notes:

- ¹ Tunnel modifications contract (\$55,077,777) includes: Notching (\$25,281,170), Drainage (\$13,196,607) and OCS Installation (\$16,600,000).
- ² When the threshold of 75% is reached, staff may return to the Board to request additional authority.
- ³ Change approved by the Board of Directors – not counted against the Executive Director’s Change Order Authority.
- ⁴ Third Party Improvements/CNPA Projects that are funded with non-PCEP funds.

CEMOF Modifications Contract

Change Order Authority (10% of ProVen Contract)

10% x \$6,550,777 = \$655,078

Date	Change Number	Description	CCO Amount	Change Order Authority Usage ¹	Remaining Authority
1/16/2020	PROV-071-CCO-001	Change Casing Size of Siphon Line to Schedule 80 PVC Pipe	\$3,849	0.59 %	\$651,229
1/13/2020	PROV-071-CCO-002	Leakage test for IW line	\$1,339	0.20 %	\$649,890
1/15/2020	PROV-071-CCO-003	Roughen surface of existing concrete	\$3,159	0.48 %	\$646,731
1/9/2020	PROV-071-CCO-004	Change Catch Basin Size from 24"X24" to 36" Round	\$14,415	2.20 %	\$632,316
1/15/2020	PROV-071-CCO-005	Hand Dig around Communication Lines	\$906	0.14 %	\$631,410
1/17/2020	PROV-071-CCO-008	Change Storm Drain Line A Material from 12-inch RCP Pipe to 12-inch PVC Pipe	\$3,583	0.55 %	\$627,827
1/16/2020	PROV-071-CCO-009	Demolition of Existing Exterior Light	\$1,558	0.24 %	\$626,269
2/13/2020	PROV-071-CCO-010	Deletion of Plastic Bollards Around New Inspection Pit	(\$3,324)	(0.51)%	\$629,593
2/13/2020	PROV-071-CCO-011	Fixing Broken Conduit in Concrete Slab North of Maintenance Building	\$4,286	0.65 %	\$625,307
2/13/2020	PROV-071-CCO-012	Epoxy Dowels at New Stairwells	\$3,526	0.54 %	\$621,781
2/13/2020	PROV-071-CCO-013	Deletion of the Removal and Replacement of Pump Disconnect Switches	(\$7,007)	(1.07)%	\$628,788
2/13/2020	PROV-071-CCO-014	Recycled Base Rock for Backfill at Pressurized Water Line at Parts Storage Warehouse	\$1,411	0.22 %	\$627,377
2/20/2020	PROV-071-CCO-015	Cut and Cap Oil Line	\$1,002	0.15 %	\$626,375
2/25/2020	PROV-071-CCO-016	Installation of Homerun Conduit	\$27,404	4.18 %	\$598,971
2/25/2020	PROV-071-CCO-017	Potholing for Boosted Water Line	\$18,476	2.82 %	\$580,495
2/28/2020	PROV-071-CCO-018	Cap Compressed Air Line	\$9,519	1.45 %	\$570,976
2/28/2020	PROV-071-CCO-019	Acoustic Ceiling Removal at Component Test Room	\$4,253	0.65 %	\$566,723
3/5/2020	PROV-071-CCO-020	Ground Wire Relocation	\$14,117	2.16 %	\$552,606
3/13/2020	PROV-071-CCO-021	Zurn Drain Assembly in Lieu of Fibrelyte	\$1,104	0.17 %	\$551,502
4/8/2020	PROV-071-CCO-022	Deletion of Concrete Pad and Double Plywood Floor at PSW	(\$1,409)	(0.22)%	\$552,911

Peninsula Corridor Electrification Project
Monthly Progress Report

Change Order Authority (10% of ProVen Contract)

10% x \$6,550,777 = \$655,078

Date	Change Number	Description	CCO Amount	Change Order Authority Usage ¹	Remaining Authority
4/8/2020	PROV-071-CCO-023	Flashing at Overflow Drain at Component Test Room	\$2,981	0.46 %	\$549,930
4/9/2020	PROV-071-CCO-024	Parts Storage Warehouse Power Feed	\$16,412	2.51 %	\$533,518
4/22/2020	PROV-071-CCO-025	Removal of Hazardous Soil from PSW Subgrade Excavation	\$43,444	6.63 %	\$490,073
4/22/2020	PROV-071-CCO-026A	Removal of Hazardous Soil from PSW Footing Excavation	\$35,808	5.47 %	\$454,266
4/27/2020	PROV-071-CCO-027	480 Volt Duct Bank and Wire Removal	\$5,015	0.77 %	\$449,251
Total			\$205,827	31.42 %	\$449,251

Notes:

1. When the threshold of 75% is reached, staff may return to the Board to request additional authority.
2. Change approved by the Board of Directors – not counted against the Executive Director’s Change Order Authority.

AMTRAK AEM-7 Contract

Change Order Authority (Lump Sum)

Up to \$150,000

Date	Change Number	Description	CCO Amount	Change Order Authority Usage ¹	Remaining Authority
10/25/2019	AMTK-066-CCO-001	Change to Amtrak Contract for Test Locomotives	(72,179)	(48.12%)	222,179
Total			(72,179)	(48.12%)	\$222,179

Notes:

1. When the threshold of 75% is reached, staff may return to the Board to request additional authority.

Appendix F – Risk Table

THIS PAGE INTENTIONALLY LEFT BLANK

Listing of PCEP Risks and Effects in Order of Severity

ID	RISK DESCRIPTION	EFFECT(S)
314	The contractor may not complete and install signal design including Two-speed check (2SC) modifications within budget and schedule.	Delay and additional cost for rework.
303	Extent of differing site conditions and associated redesign efforts results in delays to the completion of the electrification contract and increases program costs.	<p>Extends construction of design-build contract with associated increase in project costs</p> <ul style="list-style-type: none"> • DSC design cost • Inefficiencies • Construction costs related to DSCs (i.e., larger foundations) • Additional potholing
313	Sub-optimal contractor sequencing, when progressing design and clearing foundation locations may result in construction inefficiencies	Contractor claims for increase in construction and design costs, and reduced production rates extending construction duration
267	Additional property acquisition is necessitated by change in design.	New project costs and delays to schedule.
010	Potential for Stadler's sub-suppliers to fall behind schedule or delays in parts supply chain result in late completion of vehicles.	<ul style="list-style-type: none"> • Delay in obtaining parts / components. • Cost increases. (See Owner for allocation of costs) • Schedule increase - 3 months (See Owner for allocation of damages associated with this Risk)
209	TASI may not have sufficient number of signal maintainers for testing.	<ul style="list-style-type: none"> • Delays to construction/testing. • Delays to completion of infrastructure may delay acceptance of vehicles
273	Contractor generates hazardous materials, that necessitates proper removal and disposal in excess of contract allowances and expectations.	Delay to construction while removing and disposing of hazardous materials resulting in schedule delay, increased construction costs, and schedule delay costs.
308	Rejection of DVR for ATF and static wires results in cost and schedule impacts to PCEP.	Delay and delay claims
223	Major program elements may not be successfully integrated with existing operations and infrastructure in advance of revenue service.	<p>Proposed changes resulting from electrification may not be fully and properly integrated into existing system.</p> <p>Rework resulting in cost increases and schedule delays</p>

Peninsula Corridor Electrification Project
Monthly Progress Report

ID	RISK DESCRIPTION	EFFECT(S)
240	<p>Property not acquired in time for contractor to do work.</p> <p>Property Acquisition not complete per contractor availability date</p> <p><>Fee</p> <p><>Easement</p> <p><>Contract stipulates that if parcels are not available by contract date, there is only a delay if parcels are not available by the time contractor completes the Segment</p>	<ul style="list-style-type: none"> • Potential delays in construction schedule
263	<p>Collaboration across multiple disciplines to develop a customized rail activation program may fail to comprehensively address the full scope of issues required to operate and maintain an electrified railroad and decommission the current diesel fleet.</p>	<p>Delay in testing of EMUs. Delay in Revenue Service Date. Additional costs for Stadler and BBII due to overall schedule delays.</p>
318	<p>Change of vehicle suppliers results in additional first article inspections at cost to JPB</p>	<p>PCEP incurs additional cost to validate supplier and product, including repeat FAIs as needed</p>
011	<p>Risks in achieving acceptable vehicle operations performance:</p> <p><> software problems</p> <p><> electrical system problems</p> <p><> mechanical problems</p> <p><> systems integration problems</p> <p><> interoperability with diesel equipment</p> <p>Increased issues lately with vehicles regarding system integration and compatibility.</p>	<p>Cost increase.</p> <p>Delays vehicle acceptance</p> <p>Potential spill-over to other program elements</p>
244	<p>Delays to completion of Segment 4 and then the entire alignment would create storage issues and impede the ability to exercise (power up and move) EMUs and delay testing of the delivered EMUs.</p>	<p>Delay claims from the EMU contractor (Stadler) and expiration of the EMU 2 year warranty before putting significant mileage on the EMUs. Inability to exercise EMUs</p>
296	<p>PG&E needs to complete interconnection to be sufficiently complete to accept interim power</p>	<p>Delay in testing and increased costs</p>
319	<p>Failure of BBI to order cages in advance results in delays to foundation installation</p>	<p>Delays in installation of catenary system and additional cost for track protection and oversight.</p>

ID	RISK DESCRIPTION	EFFECT(S)
322	BBII needs to complete traction power substations to be sufficiently complete to accept interim power	Delay in testing and increased costs
013	Vehicle manufacturer could default.	Prolonged delay to resolve issues (up to 12 months) Increase in legal expenses Potential price increase to resolve contract issue
067	Relocation of overhead utilities must precede installation of catenary wire and connections to TPSs. Relocation work will be performed by others and may not be completed to meet BBII's construction schedule.	Delay in progress of catenary installation resulting in claims and schedule delay
242	Track access does not comply with contract-stipulated work windows.	Contractor claims for delays, schedule delays and associated costs to owner's representative staff.
253	Permits for bridges may not be issued in a timely manner.	Delays to issuance of permit for construction while negotiating and executing an operation and maintenance agreement for equipment installed on bridges; existing bridge deficiencies could result in additional costs to PCEP.
261	Although EMUs meets their electromagnetic emissions limits and wayside signal system track circuits meet their susceptibility requirements there are still compatibility issues leading to improper signal system operation	Changes on the EMU and/or signal system require additional design and installation time and expense.
285	Potential for inflation, (except with respect to Maintenance Option) to increase contractor costs.	Higher cost
286	Potential for wage escalation, (except for Maintenance Option) to increase contractor costs.	Higher cost
309	Potential that vehicles will not receive timely notification from FRA of compliance with acceptable alternate crash management standards	Delays to completion of construction and additional cost to changes in design.
056	Lack of operations personnel for testing.	<ul style="list-style-type: none"> • Testing delayed. • Change order for extended vehicle acceptance.

Peninsula Corridor Electrification Project
Monthly Progress Report

ID	RISK DESCRIPTION	EFFECT(S)
115	Other capital improvement program projects compete with PCEP for track access allocation and requires design coordination (design, coordination, integration).	Schedule delay as resources are allocated elsewhere, won't get track time, sequencing requirements may delay PCEP construction, track access requirements must be coordinated.
321	Single Phase Study and interconnection agreement may be delayed preventing energization of Segment 4 for milestone 1	
082	Unexpected restrictions could affect construction progress: <> night work <> noise <> local roads <> local ordinances	<ul style="list-style-type: none"> • Reduced production rates. • Delay
270	OCS poles or structures as designed by Contractor fall outside of JPB row	Additional ROW Take, additional cost and time
012	Potential for electromagnetic interference (EMI) to private facilities with sensitive electronic equipment caused by vehicles.	<ul style="list-style-type: none"> • Increased cost due to mitigation • Potential delay due to public protests or environmental challenge.
014	Contractor's proposal on stakeholder requested changes to the vehicles (e.g., High Level Doors in lieu of windows as emergency exits) may significantly exceed JPB authorized amount.	Schedule delay. Cost increase.
078	Need for unanticipated, additional ROW for new signal enclosures.	Delay while procuring ROW and additional ROW costs.
087	Unanticipated HazMat or contaminated hot spots encountered during foundation excavations for poles, TPSS, work at the yards.	Increased cost for clean-up and handling of materials and delay to schedule due to HazMat procedures.
088	Construction safety program fails to sufficiently maintain safe performance.	Work stoppages due to safety incidents resulting in schedule delay and additional labor costs.
171	Electrification facilities could be damaged during testing.	Delay in commencing electrified operations.
247	Timely resolution of 3rd party design review comments to achieve timely approvals	Delay to completion of design and associated additional labor costs.
251	Subcontractor and supplier performance to meet aggressive schedule <>Potential issue meeting Buy America requirements	Delay to production schedule resulting in increased soft costs and overall project schedule delay.
272	Final design based upon actual Geotech conditions	Could require changes

ID	RISK DESCRIPTION	EFFECT(S)
287	Design changes may necessitate additional implementation of environmental mitigations not previously budgeted.	Increased cost for environmental measures and delays to construct and overall delay in construction schedule
289	Coordination and delivery of permanent power for power drops for everything except traction power substations along alignment	Can't test resulting in delays to schedule and associated additional project costs.
291	Order/manufacture of long lead items prior to 100% IFC design document that proves to be incorrect	Design change and/or delays
292	Potential that UPS will not fit in the spaces allotted to communications work within the buildings.	Requisite backup capacity units under design criteria could result in the need for larger unit than originally planned resulting in design and fabrication changes and associated schedule delays and costs.
304	Solution to FRA concerns over bike storage impeding path to emergency exit windows path results in increased costs and potential rework.	Protracted negotiations with FRA to achieve original design
317	JPB may not make timely acquisition of resources to staff rail activation plan with key personnel.	Delay in operating electrified railroad - delay of RSD.
323	FRA concerns require re-design	
027	Vehicle power consumption may not meet requirements. <>System impact study and load flow show no issues	Issue with PG&E. Can't run full acceleration.
031	New cars possibly not reliable enough to be put into service as scheduled	Operating plan negatively impacted
042	Full complement of EMUs not available upon initiation of electrified revenue service	Late delivery impacts revenue service date.
101	PG&E may not be able to deliver permanent power for the project within the existing budget and in accordance with the project schedule	Additional project costs; potential delay to revenue service date
150	Number of OCS pole installation is significant. Any breakdown in sequencing of operations or coordination of multiple crews will have a substantial effect on the project.	Delay.

Peninsula Corridor Electrification Project
Monthly Progress Report

ID	RISK DESCRIPTION	EFFECT(S)
245	Failure of BBI to submit quality design and technical submittals in accordance with contract requirements <ul style="list-style-type: none"> • \$3-\$5M/month burn rate for Owner's team during peak 	Delays to project schedule and additional costs for preparation and review of submittals.
252	Failure of BBI to order/manufacture long lead items prior to 100% IFC design document approval by JPB	Delays to project schedule and additional cost for contractor and JPB staff time.
271	Need for additional construction easements beyond that which has been provided for Contractor proposed access and staging	Additional cost and time
306	Possible legal challenge and injunction to any changes in PCEP requiring subsequent CEQA or NEPA environmental clearance documentation/actions.	Worst case: a judge issues an injunction, which would prohibit any work ONLY on the project scope of the environmental document. Impact to the project from cost and schedule impact depends on if work is on the critical or becomes on the critical path.
008	Requests for change orders after vehicles are in production	Delays to manufacturing of vehicles and additional design and manufacturing costs.
023	Manufacturer cannot control vehicle weight to meet specifications.	Increased operating cost.
025	Potential that vehicles cannot meet requirements for "Mean Time to Repair" (MTTR).	Increased maintenance cost.
032	Failure to come up to speed on stakeholder safety requirements: <ul style="list-style-type: none"> <> FTA <> FRA <> CPUC 	Takes longer than expected to gain FRA/FTA concurrence on waiver and/or level boarding requirements.
053	Failure to meet Buy America requirements. (Contractor definition of component v. sub-component may not be accepted by Caltrain / FTA.)	Potential need for negotiations that might lead to delay of project award. (BA is not negotiable)
054	Infrastructure not ready for vehicles (OCS, TPS, Commissioning site / facility).	Increases cost if done off property

ID	RISK DESCRIPTION	EFFECT(S)
069	<p>Potential need for additional construction easements. Especially for access and laydown areas.</p> <p>Contractor could claim project is not constructible and needs more easements after award.</p>	<p>Increased cost</p> <p>Delay</p>
106	<p>Potential that DB contractor will have insufficient field resources (personnel or equipment) to maintain aggressive schedule.</p> <p>Multiple segments will need to be under design simultaneously.</p> <p>Labor pool issue. 32 qualified linemen will be needed. Potential there is not enough available. Big storm damage anywhere in US will draw from the pool to make line repairs.</p> <p>Possible shortages with other specialty crafts as well.</p>	<p>Delay.</p>
151	<p>Public could raise negative concerns regarding wheel/rail noise.</p>	<p>Increased cost to mitigate: <> grind rails <> reprofile wheels <> sound walls</p>
161	<p>Unanticipated costs to provide alternate service (bus bridges, etc.) during rail service disruptions.</p>	<p>Cost increase.</p>

Peninsula Corridor Electrification Project
Monthly Progress Report

ID	RISK DESCRIPTION	EFFECT(S)
182	<p>Compliance with Buy America requirements for 3rd party utility relocations.</p> <p><>Utility relocations covered under existing Caltrain agreements that require utilities to move that will not have effect on project cost - will not be Buy America</p> <p><>Installation of new equipment inside PG&E substations that will provide all PG&E customers, about 1/6 of that provides power to our system - is upgrade that benefits all customers subject to Buy America requirements, is it 1/6th, or 100%</p> <p><>Risk is substation not relocations</p> <p><>Substation equipment is available domestically, has 6 month longer lead time and increased cost of 20%</p>	<ul style="list-style-type: none"> • Increased cost • Delay
192	<p>Environmental compliance during construction.</p> <ul style="list-style-type: none"> - Potential impact to advancing construction within the vicinity of any cultural finds that are excavated. - Failure to meet the commitments contained within the PCEP EA, FEIR and permit conditions 	<ul style="list-style-type: none"> • Delay • Cost increase
195	<p>Introduction of electrified train service will require training of first responders in working in and around the rail corridor. The new vehicles will be considerably quieter than the existing fleet and the presence of high voltage power lines will require new procedures for emergency response. A new training program will need to be developed and disseminated for:</p> <ul style="list-style-type: none"> • Fire, police, and first responders • Local communities • Schools 	<p>Safety hazards resulting in incidents that delay construction and increase labor cost. Delays in RSD until training is completed as requirement of safety certification process.</p>

ID	RISK DESCRIPTION	EFFECT(S)
237	JPB needs an agreement with each city in which catenary will be strung over an existing grade crossing (17 in all) under GO 88 (grade crossings). These agreements must be executed subsequent to installing overhead catenary. JPB is preparing a response to CPUC while working with the cities. Delays in reaching agreement could have impacts on schedule and budget.	Not completing the grade crossing diagnostics and getting agreement from the cities on the results can result in delays to necessary approvals for the project and revenue service.
248	3rd party coordination <>Jurisdictions, Utilities, UP, Contractors <>D/B needs to provide timely information to facilitate 3rd party coordination <>Risk is for construction	Delays in approvals resulting in project schedule delays and associated costs.
250	Potential for municipalities to request betterments as part of the electrification project.	Delay to project schedule in negotiating betterments as part of the construction within municipalities and associated increased cost to the project as no betterments were included in the project budget.
254	Potential that bridge clearance data are inaccurate and that clearances are not sufficient for installation of catenary.	Results in additional design and construction to create sufficient clearance.
266	Verizon poles in conflict with OCS may not be removed in advance of OCS installation.	Delay in progress of catenary installation resulting in claims and schedule delay
274	JPB as-built drawings and existing infrastructure to be used as basis of final design and construction is not correct	Additional cleanup of as-builts after PCEP construction
275	DB fails to verify as-built drawings and existing infrastructure	Additional cleanup of as-builts after PCEP construction
278	Failure of D/B contractor and subcontractors and suppliers to meet Buy America requirements	Delays while acceptable materials are procured and additional costs for delays and purchase of duplicative equipment.
282	Failure to maintain dynamic envelope and existing track clearances consistent with requirements.	Redesign entailing cost and schedule impacts.
284	Compliance with project labor agreement could result in inefficiencies in staffing of construction.	Increase in labor costs and less efficient construction resulting in schedule delays.
290	Delays in agreement and acceptance of initial VVSC requirements database.	Delay to design acceptance
293	Readiness of 115kV interconnect for temporary power to support testing	Delay in testing

Peninsula Corridor Electrification Project
Monthly Progress Report

ID	RISK DESCRIPTION	EFFECT(S)
311	Although project recordable injuries remain below the industry average, there have been numerous small impact incidents occurring that could potentially lead to a more serious event occurring.	The occurrence of a high impact safety event could result in project rework, construction delays, and increased project costs.
325	EMU production delay. Possible that there are quality issues, failed factory tests, poor integration / control of suppliers.	Schedule Increase
326	EMU production delay. Possible that there are failed factory tests	Schedule Increase
327	EMU production delay. Possible that there is poor integration / control of suppliers.	Schedule Increase

Appendix G – MMRP Status Log

THIS PAGE INTENTIONALLY LEFT BLANK

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
AES-2a: Minimize OCS construction activity on residential and park areas outside the Caltrain ROW.	X	X			Ongoing	The OCS proposed construction schedule has been provided to the JPB. OCS construction began the week of October 2, 2017. The D-B has utilized the potholing process to assist in locating conflicts in the 35% design and attempting to relocate OCS pole locations within the ROW.
AES-2b: Aesthetic treatments for OCS poles, TPFs in sensitive visual locations, and Overbridge Protection Barriers.	X				Ongoing	The design requirements indicated in the measure have been implemented as described, and coordination with the specific jurisdictions regarding pole colors and design is ongoing. Coordination with the JPB & local jurisdiction regarding Overbridge Protection Barriers and TPFs is ongoing.
AES-4a: Minimize spillover light during nighttime construction.		X			Ongoing	OCS construction began the week of October 2, 2017; and the BBI community relations lead has notified nearby residents of upcoming construction. During construction, lighting is faced inward, towards the railroad tracks, and any complaints will be documented and addressed by the BBI community relations lead.
AES-4b: Minimize light spillover at TPFs.	X				Upcoming	The design requirements indicated in the measure are being utilized in the design and construction process.
AQ-2a: Implement BAAQMD basic and additional construction mitigation measures to reduce construction-related dust.	X	X			Ongoing	The Dust Mitigation Plan was submitted to the JPB and approved. The requirements in the Dust Mitigation Plan will be implemented throughout the construction period and documented in daily reports.

Peninsula Corridor Electrification Project
Monthly Progress Report

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
AQ-2b: Implement BAAQMD basic and additional construction mitigation measures to control construction-related ROG and NOX emissions.	X	X			Ongoing	The Equipment Emissions Control Plan was submitted to the JPB and approved. The requirements in the Equipment Emissions Control Plan will be implemented throughout the construction period and documented in daily reports.
AQ-2c: Utilize clean diesel-powered equipment during construction to control construction-related ROG and NOX emissions.	X	X			Ongoing	The Equipment Emissions Control Plan was submitted to the JPB and approved. The requirements in the Equipment Emissions Control Plan will be implemented throughout the construction period and documented in daily reports.
BIO-1a: Implement general biological impact avoidance measures.	X	X			Ongoing	Worker Environmental Awareness Training is provided to all project-related personnel before they work on the project. All measures as described will be implemented throughout the construction period and documented in daily reports.
BIO-1b: Implement special-status plant species avoidance and revegetation measures.	X	X	X		Complete	Not applicable. Subsequent habitat assessment and avoidance of Communication Hill eliminated any potential to affect special-status plant species. The measure is not needed.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
BIO-1c: Implement California red-legged frog and San Francisco garter snake avoidance measures.	X	X			Ongoing	Pre-construction surveys are occurring no more than 7 days prior to the initiation of construction activities nearby/adjacent to potential habitat for CRLF and SFGS. The Wildlife Exclusion Fencing Plans for Segments 1 and 4 were submitted and approved by the wildlife agencies, and installation and monitoring of wildlife exclusion fencing is ongoing. No CRLF / SFGS or sign of each species has been observed to date on the Project.
BIO-1d: Implement western pond turtle avoidance measures.	X	X			Ongoing	Pre-construction surveys are occurring no more than 7 days prior to the initiation of construction activities nearby/adjacent to potential habitat for WPT. No WPT or WPT sign have been observed to date on the Project.
BIO-1e: Implement Townsend’s big-eared bat, pallid bat, hoary bat, and fringed myotis avoidance measures.	X	X			Ongoing	Pre-construction surveys are occurring no more than 7 days prior to the initiation of construction activities with the potential to disturb bats or their habitat. No special-status bats or sign have been observed to date on the Project.
BIO-1f: Implement western burrowing owl avoidance measures.	X	X			Ongoing	Protocol surveys for Western Burrowing Owl have been conducted from April–July, in 2017, 2018, and 2019, at previously identified potentially suitable habitat locations. Note that all of these locations are in Construction Segment 4 (southern Santa Clara and San Jose). No Burrowing Owls have been observed during the 2017-2019 surveys. Survey reports for the 2017, 2018, and 2019 surveys have been submitted to the JPB for the project

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
						record. In addition, pre-construction surveys of the potential BUOW habitat areas in Segment 4 are ongoing, as needed, and if required, they occur no more than 7 days prior to the onset of new ground-disturbing of construction activities. Surveys for the 2020 breeding season will commenced in March 2020. On March 24, 2020, two burrowing owls were observed adjacent to the Caltrain ROW, near MP 44.6. The owls were located approximately 150 feet away from the Caltrain ROW. A 200-meter no-disturbance buffer has been continued to be implemented during the reporting period. Any future work scheduled to occur within the 200-meter buffer will be coordinated with the Qualified Biologist, in consultation with the JPB and the CDFW, as needed.
BIO-1g: Implement northern harrier, white-tailed kite, American peregrine falcon, saltmarsh common yellowthroat, purple martin, and other nesting bird avoidance measures.	X	X			Ongoing	Nesting Bird and raptor surveys were conducted from February 1 through September 15, in 2017, 2018 and 2019, prior to project-related activities with the potential to impact nesting birds. Nesting Bird Surveys recommenced on February 1, 2020 for the 2020 nesting season (February 1, 2020). During this reporting period, a 250-foot buffer continued to be implemented around the active Cooper's hawk (COHA) nest in a tree adjacent to the tracks near MP 33.5. Any work that occurred within the buffer area was monitored full-time by a qualified biologist. No impacts to the nest were observed during this reporting period. It is anticipated the nestling(s)

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
						will fledge during the next reporting period.
BIO-1h: Conduct biological resource survey of future contractor-determined staging areas.	X	X			Ongoing	The agency-approved Qualified Biologist has conducted surveys of the staging areas currently being used for construction activities. No special-status species or other potentially sensitive biological resources were observed. The agency-approved Qualified Biologist will continue to survey ahead of the initiation of activities at planned staging areas as the Project moves into new construction areas.
BIO-1i: Minimize impacts on Monarch butterfly overwintering sites.	X	X			Ongoing	The agency-approved Qualified Biologist has periodically monitored the project limits to evaluate the presence of Monarch butterfly overwintering sites. No Monarch butterfly overwintering sites have been observed on the Project to date.
BIO-1j: Avoid nesting birds and bats during vegetation maintenance.				X	Upcoming	To be completed during Project operation.
BIO-2: Implement serpentine bunchgrass avoidance and revegetation measures.	X	X	X		Complete	Not applicable. Subsequent habitat assessment and avoidance of Communication Hill eliminated any potential to affect serpentine bunchgrass. This measure is no longer needed.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
BIO-3: Avoid or compensate for impacts on wetlands and waters.	X	X	X		Complete	The JPB has compensated for unavoidable wetland impacts by purchasing adequate credits from a wetlands mitigation bank approved by USACE and SFRWQCB.
BIO-5: Implement Tree Avoidance, Minimization, and Replacement Plan.	X	X	X		Ongoing	Tree removal and pruning activities were initiated in August 2017, and are ongoing, under the guidance of the BBI Arborist, and in accordance with the Tree Avoidance, Minimization, and Replacement Plan. Tree Removal and Pruning status is provided to the JPB on a regular basis.
BIO-6: Pay <i>Santa Clara Valley Habitat Plan</i> land cover fee (if necessary).	X				Complete	Not applicable. The SCVHP does not apply to the Project because TPS2, Option 1 was not selected and OCS does not extend to Communication Hill. This measure is not needed.
CUL-1a: Evaluate and minimize impacts on structural integrity of historic tunnels.	X				Upcoming	To be implemented prior to construction in tunnels.
CUL-1b: Minimize impacts on historic decorative tunnel material.	X				Upcoming	To be implemented prior to construction in tunnels. Historic American Engineering Record (HAER) documentation was completed in October 2018, pursuant to this measure.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
CUL-1c: Install project facilities in a way that minimizes impacts on historic tunnel interiors.	X				Upcoming	To be implemented prior to construction in tunnels.
CUL-1d: Implement design commitments at historic railroad stations	X				Complete	The Qualified Architectural Historian completed and submitted the HABS Level III documents to the JPB for all seven of the historic stations. Pole placement has been designed to minimize the visual impact to historic stations and all design changes are reviewed by the Environmental Compliance Lead to ensure the mitigation measure is being implemented as the design of the project progresses.
CUL-1e: Implement specific tree mitigation considerations at two potentially historic properties and landscape recordation, as necessary.	X	X			Complete	It was determined that the project is not acquiring any ROW at either of the subject properties so all tree effects would be within the JPB ROW. Therefore, the APE does not include these two historic properties. This measure is no longer needed.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
CUL-1f: Implement historic bridge and underpass design requirements.	X				Ongoing	This measure is being implemented as described during the design process and will be incorporated into the final design. The four bridges that are included in the MMRP are rail bridges crossing over another feature. Design of the OCS system is taking into account that there are requirements that restrict the design. Thus far, the designs for Construction Segments 2 & 4 are in process and designs are not yet complete. The D-B will forward to the Architectural Historian once complete.
CUL-2a: Conduct an archaeological resource survey and/or monitoring of the removal of pavement or other obstructions to determine if historical resources under CEQA or unique archaeological resources under PRC 21083.2 are present.	X				Ongoing	Periodic inspections of ground surface areas along the alignment, in conjunction with cultural monitoring as-needed of project activities in culturally sensitive areas are ongoing. The Archaeological Final Report will be provided at the conclusion of construction activities.
CUL-2b: Conduct exploratory trenching or coring of areas where subsurface project disturbance is planned in those areas with “high” or “very high” potential for buried site.	X				Ongoing	Exploratory trenching and subsurface testing of all potentially culturally sensitive areas occurred prior to the initiation of construction activities in those areas. The results will be included in the Archaeological Final Report. No cultural resources requiring the development of a treatment plan were observed. A Native American monitor has been present for all exploratory trenching and subsurface testing work.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
CUL-2c: Conduct limited subsurface testing before performing ground-disturbing work within 50 meters of a known archaeological site.	X				Ongoing	Exploratory trenching and subsurface testing of all potentially culturally sensitive areas occurred prior to the initiation of construction activities in those areas. The results will be included in the Archaeological Final Report. No cultural resources requiring the development of a treatment plan were observed. A Native American monitor has been present for all exploratory trenching and subsurface testing work.
CUL-2d: Conduct exploratory trenching or coring of areas within the three zones of special sensitivity where subsurface project disturbance is planned.	X				Ongoing	Exploratory trenching and subsurface testing of all potentially culturally sensitive areas occurred prior to the initiation of construction activities in those areas. The results will be included in the Archaeological Final Report. No cultural resources requiring the development of a treatment plan were observed. A Native American monitor has been present for all exploratory trenching and subsurface testing work.
CUL-2e: Stop work if cultural resources are encountered during ground-disturbing activities.	X	X			Ongoing	No prehistoric or historic-period cultural materials have been observed during cultural monitoring.
CUL-2f: Conduct archaeological monitoring of ground-disturbing activities in areas as determined by JPB and SHPO.		X			Ongoing	Cultural monitoring as-needed of project activities in culturally sensitive areas is ongoing. The Archaeological Final Report will be provided at the conclusion of construction activities.

Peninsula Corridor Electrification Project
Monthly Progress Report

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
CUL-3: Comply with state and county procedures for the treatment of human remains discoveries.		X			Ongoing	No human remains have been observed to date on the Project.
EMF-2: Minimize EMI effects during final design, Monitor EMI effects during testing, commission and operations, and Remediate Substantial Disruption of Sensitive Electrical Equipment.	X	X	X		Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. Designs are submitted and reviewed/commented on by JPB. Monitoring EMI effects will occur post construction.
GEO-1: Perform a site-specific geotechnical study for traction power facilities.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. Geotechnical studies are being conducted by Parikh under subcontract with PGH Wong. Studies and results are submitted to JPB as completed.
GEO-4a: Identification of expansive soils.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design by the D-B as described. Geotechnical studies are being conducted by Parikh under subcontract with PGH Wong. Studies and results are submitted to JPB as completed.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
GEO-4b: Mitigation of expansive soils.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design by the D-B as described. Geotechnical studies are being conducted by Parikh under subcontract with PGH Wong. Studies and results are submitted to JPB as completed.
HAZ-2a: Conduct a Phase II Environmental Site Assessment prior to construction.	X				Complete	A Phase II Environmental Assessment was completed prior to construction by the JPB consultant, and the results were provided to BBI, and the required mitigation is being implemented prior to the initiation of construction activities.
HAZ-2b: Implement engineering controls and best management practices during construction.	X	X			Ongoing	D-B field activities are being monitored daily for significant color changes or odors which may indicate contamination. In addition, assessments of existing subsurface pipes by a certified Asbestos Consultant are occurring as needed throughout the project as they are observed. Following the assessments, a specification describing the methods for removal and disposal are provided to the certified asbestos contractor. The removal and disposal work performed by the certified asbestos contractor is monitored by the certified asbestos consultant.
HYD-1: Implement construction dewatering treatment, if necessary.	X	X			Ongoing	Facilities & BMPs are in place to deal with this requirement should it arise in the OCS foundations.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
HYD-4: Minimize floodplain impacts by minimizing new impervious areas for TPFs or relocating these facilities.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. The TPFs in Construction Segments 2 & 4 are currently in final design and design for TPFs in Construction Segments 1 & 3 has begun. The design minimizes hardscape only to required structure foundations; yard areas are to receive a pervious material.
HYD-5: Provide for electrical safety at TPFs subject to periodic or potential flooding.	X			X	Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. The TPFs in Construction Segments 2 & 4 are currently in final design and design for TPFs in Construction Segments 1 & 3 has begun. The design plan currently raises the TPFs above the floodplain.
HYD-7: Implement sea level rise vulnerability assessment and adaptation plan.				X	Ongoing	The JPB has initiated this measure and preparation of the sea level rise vulnerability assessment and adaptation plan is underway.
NOI-1a: Implement Construction Noise Control Plan.	X	X			Ongoing	The Noise and Vibration Control Plan has been submitted and is being implemented. Field activity is monitored per the Plan. If allowable noise levels are near or exceed allowable noise levels, mitigation such as blankets are used from that point forward.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
NOI-1b: Conduct site-specific acoustical analysis of ancillary facilities based on the final mechanical equipment and site design and implement noise control treatments where required.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. PGH Wong has completed analysis and design and issued for JPB review.
NOI-2a: Implement Construction Vibration Control Plan.	X	X			Ongoing	The Noise and Vibration Control Plan has been submitted and is being implemented. Field activity is monitored per the Plan.
PSU-8a: Provide continuous coordination with all utility providers.	X	X			Ongoing	The design requirements indicated in the measure will be implemented through the final design as described. Coordination with utility providers is ongoing and there have not been any service interruptions thus far.
PSU-8b: Adjust OCS pole foundation locations.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design as described.
PSU-8c: Schedule and notify users about potential service interruptions.	X	X			Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. There have not been any service interruptions thus far.
PSU-9: Require application of relevant construction mitigation measures to utility relocation and transmission line construction by others.	X	X			Ongoing	JPB has initiated coordination with PG&E regarding transmission line construction. PG&E is currently raising overcrossing lines in Segment 2.

Peninsula Corridor Electrification Project
Monthly Progress Report

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
TRA-1a: Implement Construction Road Traffic Control Plan.	X	X			Ongoing	The D-B has begun traffic control design and permit applications with the City of Millbrae, Burlingame and San Mateo. Other communities will follow. Designs have been completed for all cross-over bridges in Segments 2 & 4 and submitted.
TRA-1c: Implement signal optimization and roadway geometry improvements at impacted intersections for the 2020 Project Condition.	X	X			Upcoming	This measure has not started
TRA-2a: Implement construction railway disruption control plan.	X	X			Ongoing	Minimization of railway disruption is being coordinated by the Site Specific Work Plan. A Construction Railway Disruption Control Plan was prepared to document the measures that are being implemented.
TRA-3b: In cooperation with the City and County of San Francisco, implement surface pedestrian facility improvements to address the Proposed Project's additional pedestrian movements at and immediately adjacent to the San Francisco 4th and King Station.	X	X	X		Upcoming	This measure has not started.
TRA-4b: Continue to improve bicycle facilities at Caltrain stations and partner with bike share programs where available following guidance in				X	Ongoing	The JPB adopted the Caltrain Bicycle Parking Management Plan in November 2017, and staff have been working to implement the Plan's recommendations to improve wayside bike parking facilities along

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
Caltrain's Bicycle Access and Parking Plan.						the corridor. Staff have also been coordinating with local jurisdictions that have launched bikeshare pilot programs to safely site bicycles near Caltrain stations.
NOI-CUMUL-1: Implement a phased program to reduce cumulative train noise along the Caltrain corridor as necessary to address future cumulative noise increases over FTA thresholds				X	Upcoming	This measure will be implemented during project operation.
NOI-CUMUL-2: Conduct project-level vibration analysis for Blended System operations and implement vibration reduction measures as necessary and appropriate for the Caltrain corridor				X	In Progress	CHSRA is conducting this analysis as part of the EIR/EIS for the San Francisco to San Jose section.
TRA-CUMUL-1: Implement a phased program to provide traffic improvements to reduce traffic delays near at-grade crossings and Caltrain stations				X	Upcoming	This measure will be implemented during project operation.
TRA-CUMUL-2: Implement technical solution to allow electric trolley bus transit across 16th Street without OCS conflicts in cooperation with SFMTA.	X				Complete	Not applicable. SFMTA has elected to not electrify the 16 th Street crossing. This measure no longer applies.
Mitigation Measure TRA-CUMUL-3: As warranted, Caltrain and freight operators will partner to provide Plate H clearance				X	Upcoming	This measure will be implemented during project operation.

Peninsula Corridor Electrification Project
Monthly Progress Report

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
as feasible between San Jose and Bayshore.						
AES-2a: Minimize OCS construction activity on residential and park areas outside the Caltrain ROW.	X	X			Ongoing	The OCS proposed construction schedule has been provided to the JPB. OCS construction began the week of October 2, 2017. The D-B has used the potholing process to assist in locating conflicts in the 35% design and attempting to relocate OCS pole locations within the ROW, thereby avoiding parks and residential areas.
AES-2b: Aesthetic treatments for OCS poles, TPFs in sensitive visual locations, and Overbridge Protection Barriers.	X				Ongoing	The design requirements indicated in the measure have been implemented as described, and coordination with the specific jurisdictions regarding pole colors and design, TPFs, and Overbridge Protection Barriers, is ongoing.
AES-4a: Minimize spillover light during nighttime construction.		X			Ongoing	OCS construction began the week of October 2, 2017. The BBI community relations lead has notified nearby residents of upcoming construction. During construction, lighting is faced inward, towards the railroad tracks, and any complaints will be documented and addressed by the BBI community relations lead.
AES-4b: Minimize light spillover at TPFs.	X				Upcoming	The design requirements indicated in the measure are being used in the design process of the TPFs.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
AQ-2a: Implement BAAQMD basic and additional construction mitigation measures to reduce construction-related dust.	X	X			Ongoing	The Dust Mitigation Plan was submitted to the JPB. The requirements in the Dust Mitigation Plan will be implemented throughout the construction period and documented in daily reports.
AQ-2b: Implement BAAQMD basic and additional construction mitigation measures to control construction-related ROG and NOX emissions.	X	X			Ongoing	The Equipment Emissions Control Plan was submitted to the JPB. The requirements in the Equipment Emissions Control Plan will be implemented throughout the construction period and documented in daily reports.
AQ-2c: Utilize clean diesel-powered equipment during construction to control construction-related ROG and NOX emissions.	X	X			Ongoing	The Equipment Emissions Control Plan was submitted to the JPB. The requirements in the Equipment Emissions Control Plan will be implemented throughout the construction period and documented in daily reports.
BIO-1a: Implement general biological impact avoidance measures.	X	X			Ongoing	Worker Environmental Awareness Training is provided to all project-related personnel before they work on the project. All measures as described will be implemented throughout the construction period and documented in daily reports.
BIO-1b: Implement special-status plant species avoidance and revegetation measures.	X	X	X		Complete	Not applicable. Subsequent habitat assessment and avoidance of Communication Hill eliminated any potential to affect special-status plant species. The measure is not needed.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
BIO-1c: Implement California red-legged frog and San Francisco garter snake avoidance measures.	X	X			Ongoing	Pre-construction surveys are occurring no more than 7 days prior to the initiation of construction activities nearby/adjacent to potential habitat for CRLF and SFGS. The Wildlife Exclusion Fencing Plan for Segments 2 and 4 was submitted and approved by the wildlife agencies, and installation and monitoring of wildlife exclusion fencing is ongoing. No CRLF / SFGS or sign of each species has been observed to date on the Project. A separate Wildlife Exclusion Fencing Plan will be submitted for Segments 1 and 3, prior to initiation of construction activities in those segments.
BIO-1d: Implement western pond turtle avoidance measures.	X	X			Ongoing	Pre-construction surveys are occurring no more than 7 days prior to the initiation of construction activities nearby/adjacent to potential habitat for WPT. No WPT or WPT sign have been observed to date on the Project.
BIO-1e: Implement Townsend's big-eared bat, pallid bat, hoary bat, and fringed myotis avoidance measures.	X	X			Ongoing	Pre-construction surveys are occurring no more than 7 days prior to the initiation of construction activities with the potential to disturb bats or their habitat. No special-status bats or sign have been observed to date on the Project.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
BIO-1f: Implement western burrowing owl avoidance measures.	X	X			Ongoing	Protocol surveys for Western Burrowing Owl were conducted from April 2017 through July 2017 at previously identified potentially suitable habitat locations. Note that all of these locations are in Construction Segment 4 (southern Santa Clara and San Jose). No Burrowing Owls were observed during the surveys. Construction in Segment 4 is anticipated to occur in 2018. Prior to construction activities in Segment 4, pre-construction surveys of the potential habitat areas will occur no more than 7 days prior to the onset of construction activities. In addition, protocol surveys were initiated in March 2018, and were completed in June 2018, at the previously identified potentially suitable habitat locations, which will allow work to occur during the 2019 breeding season, if necessary. No Burrowing Owls were observed during the 2018 surveys.
BIO-1g: Implement northern harrier, white-tailed kite, American peregrine falcon, saltmarsh common yellowthroat, purple martin, and other nesting bird avoidance measures.	X	X			Ongoing	Nesting Bird surveys were conducted from February 1 through September 15, 2017 prior to project-related activities with the potential to impact nesting birds. No active nests were observed during this reporting period. Nesting Bird surveys were initiated on February 1, 2018 and continued throughout the reporting period. Active nests were observed during this reporting period, and no-disturbance buffers were implemented to avoid any impacts to active nests, and all project activities which occurred nearby active nests

Peninsula Corridor Electrification Project
Monthly Progress Report

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
						were monitored by agency-approved biological monitors.
BIO-1h: Conduct biological resource survey of future contractor-determined staging areas.	X	X			Ongoing	The agency-approved Qualified Biologist has conducted surveys of the staging areas currently being used for construction activities. No special-status species or other potentially sensitive biological resources were observed. The agency-approved Qualified Biologist will continue to survey ahead of the initiation of activities at planned staging areas as the Project moves into new construction areas.
BIO-1i: Minimize impacts on Monarch butterfly overwintering sites.	X	X			Ongoing	The agency-approved Qualified Biologist has periodically monitored the project limits to evaluate the presence of Monarch butterfly overwintering sites. No Monarch butterfly overwintering sites have been observed on the Project to date.
BIO-1j: Avoid nesting birds and bats during vegetation maintenance.				X	Upcoming	To be completed during Project operation.
BIO-2: Implement serpentine bunchgrass avoidance and revegetation measures.	X	X	X		Complete	Not applicable. Subsequent habitat assessment and avoidance of Communication Hill eliminated any potential to affect serpentine bunchgrass. This measure is no longer needed.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
BIO-3: Avoid or compensate for impacts on wetlands and waters.	X	X	X		Complete	The JPB has compensated for unavoidable wetland impacts by purchasing adequate credits from a wetlands mitigation bank approved by USACE and SFRWQCB.
BIO-5: Implement Tree Avoidance, Minimization, and Replacement Plan.	X	X	X		Ongoing	Tree removal and pruning activities were initiated in August 2017, and are ongoing, under the guidance of the BBI Arborist, and in accordance with the Tree Avoidance, Minimization, and Replacement Plan. Tree Removal and Pruning status is provided to the JPB on a weekly basis.
BIO-6: Pay <i>Santa Clara Valley Habitat Plan</i> land cover fee (if necessary).	X				Complete	Not applicable. The SCVHP does not apply to the Project because TPS2, Option 1 was not selected and OCS does not extend to Communication Hill. This measure is not needed.
CUL-1a: Evaluate and minimize impacts on structural integrity of historic tunnels.	X				Upcoming	To be implemented prior to construction in tunnels.
CUL-1b: Minimize impacts on historic decorative tunnel material.	X				Upcoming	To be implemented prior to construction in tunnels.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
CUL-1c: Install project facilities in a way that minimizes impacts on historic tunnel interiors.	X				Upcoming	To be implemented prior to construction in tunnels.
CUL-1d: Implement design commitments at historic railroad stations	X				Complete	The Qualified Architectural Historian completed and submitted the HABS Level III documents to the JPB for all seven of the historic stations. Pole placement has been designed to minimize the visual impact to historic stations and all design changes are reviewed by the Environmental Compliance Lead to ensure the mitigation measure is being implemented as the design of the project progresses.
CUL-1e: Implement specific tree mitigation considerations at two potentially historic properties and landscape recordation, as necessary.	X	X			Complete	It was determined that the project is not acquiring any ROW at either of the subject properties so all tree effects would be within the JPB ROW. Therefore, the APE does not include these two historic properties. This measure is no longer needed.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
CUL-1f: Implement historic bridge and underpass design requirements.	X				Ongoing	This measure is being implemented as described during the design process and will be incorporated into the final design. The four bridges that are included in the MMRP are rail bridges crossing over another feature. Design of the OCS system is taking into account that there are requirements that restrict the design. Thus far, the designs for Construction Segments 2 & 4 are in process and designs are not yet complete. The D-B will forward to the Architectural Historian once complete.
CUL-2a: Conduct an archaeological resource survey and/or monitoring of the removal of pavement or other obstructions to determine if historical resources under CEQA or unique archaeological resources under PRC 21083.2 are present.	X				Ongoing	Periodic inspections of ground surface areas along the alignment, in conjunction with cultural monitoring as-needed of project activities in culturally sensitive areas are ongoing. The Archaeological Final Report will be provided at the conclusion of construction activities.
CUL-2b: Conduct exploratory trenching or coring of areas where subsurface project disturbance is planned in those areas with “high” or “very high” potential for buried site.	X				Ongoing	Exploratory trenching and subsurface testing of all potentially culturally sensitive areas occurred prior to the initiation of construction activities in those areas. The results will be included in the Archaeological Final Report. No cultural resources requiring the development of a treatment plan were observed. A Native American monitor has been present for all exploratory trenching and subsurface testing work.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
CUL-2c: Conduct limited subsurface testing before performing ground-disturbing work within 50 meters of a known archaeological site.	X				Ongoing	Exploratory trenching and subsurface testing of all potentially culturally sensitive areas occurred prior to the initiation of construction activities in those areas. The results will be included in the Archaeological Final Report. No cultural resources requiring the development of a treatment plan were observed. A Native American monitor has been present for all exploratory trenching and subsurface testing work.
CUL-2d: Conduct exploratory trenching or coring of areas within the three zones of special sensitivity where subsurface project disturbance is planned.	X				Ongoing	Exploratory trenching and subsurface testing of all potentially culturally sensitive areas occurred prior to the initiation of construction activities in those areas. The results will be included in the Archaeological Final Report. No cultural resources requiring the development of a treatment plan were observed. A Native American monitor has been present for all exploratory trenching and subsurface testing work.
CUL-2e: Stop work if cultural resources are encountered during ground-disturbing activities.	X	X			Ongoing	No prehistoric or historic-period cultural materials have been observed during cultural monitoring.
CUL-2f: Conduct archaeological monitoring of ground-disturbing activities in areas as determined by JPB and SHPO.		X			Ongoing	Cultural monitoring as-needed of project activities in culturally sensitive areas is ongoing. The Archaeological Final Report will be provided at the conclusion of construction activities.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
CUL-3: Comply with state and county procedures for the treatment of human remains discoveries.		X			Ongoing	No human remains have been observed to date on the Project.
EMF-2: Minimize EMI effects during final design, Monitor EMI effects during testing, commission and operations, and Remediate Substantial Disruption of Sensitive Electrical Equipment.	X	X	X		Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. Designs are submitted and reviewed/commented on by JPB. Monitoring EMI effects will occur post construction.
GEO-1: Perform a site-specific geotechnical study for traction power facilities.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. Geotechnical studies and results are submitted to JPB as completed.
GEO-4a: Identification of expansive soils.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. Geotechnical studies and results are submitted to JPB as completed.

Peninsula Corridor Electrification Project
Monthly Progress Report

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
GEO-4b: Mitigation of expansive soils.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. Geotechnical studies and results are submitted to JPB as completed.
HAZ-2a: Conduct a Phase II Environmental Site Assessment prior to construction.	X				Complete	A Phase II Environmental Assessment was completed prior to construction by the JPB consultant, and the results were provided to BBI, and the required mitigation is being implemented prior to the initiation of construction activities.
HAZ-2b: Implement engineering controls and best management practices during construction.	X	X			Ongoing	Field activities are being monitored daily for significant color changes or odors which may indicate contamination. In addition, an assessment of two existing subsurface pipes by a certified Asbestos Consultant occurred during this reporting period, and a specification describing the methods for removal and disposal is currently in progress.
HYD-1: Implement construction dewatering treatment, if necessary.	X	X			Ongoing	Facilities & BMPs are in place to deal with this requirement should it arise in the OCS foundations.
HYD-4: Minimize floodplain impacts by minimizing new impervious areas for TPFs or relocating these facilities.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. The TPFs in Construction Segments 2 & 4 are currently in final design and design for TPFs in Construction Segments 1 & 3 has begun. The design minimizes

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
						hardscape only to required structure foundations; yard areas are to receive a pervious material.
HYD-5: Provide for electrical safety at TPFs subject to periodic or potential flooding.	X			X	Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. The TPFs in Construction Segments 2 & 4 are currently in final design and design for TPFs in Construction Segments 1 & 3 has begun. The design plan currently raises the TPFs above the floodplain.
HYD-7: Implement sea level rise vulnerability assessment and adaptation plan.				X	Ongoing	The JPB has initiated this measure and preparation of the sea level rise vulnerability assessment and adaptation plan is underway.
NOI-1a: Implement Construction Noise Control Plan.	X	X			Ongoing	The Noise and Vibration Control Plan has been submitted and is being implemented. Field activity is monitored per the Plan. If allowable noise levels are near or exceed allowable noise levels, mitigation such as blankets are used from that point forward.
NOI-1b: Conduct site-specific acoustical analysis of ancillary facilities based on the final mechanical equipment and site design and implement noise control treatments where required.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. Design is still in process and a noise study is currently being performed.

Peninsula Corridor Electrification Project
Monthly Progress Report

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
NOI-2a: Implement Construction Vibration Control Plan.	X	X			Ongoing	The Noise and Vibration Control Plan has been submitted and is being implemented. Field activity is monitored per the Plan.
PSU-8a: Provide continuous coordination with all utility providers.	X	X			Ongoing	The design requirements indicated in the measure will be implemented through the final design as described. Coordination with utility providers is ongoing and there have not been any service interruptions thus far.
PSU-8b: Adjust OCS pole foundation locations.	X				Ongoing	The design requirements indicated in the measure are being implemented through the final design as described.
PSU-8c: Schedule and notify users about potential service interruptions.	X	X			Ongoing	The design requirements indicated in the measure are being implemented through the final design as described. There have not been any service interruptions thus far.
PSU-9: Require application of relevant construction mitigation measures to utility relocation and transmission line construction by others.	X	X			Ongoing	JPB has initiated coordination with PG&E regarding transmission line construction. PG&E is currently raising overcrossing lines in Segment 2.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
TRA-1a: Implement Construction Road Traffic Control Plan.	X	X			Ongoing	The D-B has begun traffic control design and permit applications with cities in Segments 2 and 4. Designs have been completed and approved for all cross-over bridges in Segments 2 and 4.
TRA-1c: Implement signal optimization and roadway geometry improvements at impacted intersections for the 2020 Project Condition.	X	X			Upcoming	This measure has not started
TRA-2a: Implement construction railway disruption control plan.	X	X			Ongoing	Minimization of railway disruption is being coordinated by the Site Specific Work Plan. A Construction Railway Disruption Control Plan was prepared to document the measures that are being implemented.
TRA-3b: In cooperation with the City and County of San Francisco, implement surface pedestrian facility improvements to address the Proposed Project's additional pedestrian movements at and immediately adjacent to the San Francisco 4th and King Station.	X	X	X		Upcoming	This measure has not started.
TRA-4b: Continue to improve bicycle facilities at Caltrain stations and partner with bike share programs where available following guidance in				X	Ongoing	The JPB adopted the Caltrain Bicycle Parking Management Plan in November 2017, and staff have been working to implement the Plan's recommendations to improve wayside bike parking facilities along

Peninsula Corridor Electrification Project
Monthly Progress Report

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
Caltrain's Bicycle Access and Parking Plan.						the corridor. Staff have also been coordinating with local jurisdictions that have launched bikeshare pilot programs to safely site bicycles near Caltrain stations.
NOI-CUMUL-1: Implement a phased program to reduce cumulative train noise along the Caltrain corridor as necessary to address future cumulative noise increases over FTA thresholds				X	Upcoming	This measure will be implemented during project operation.
NOI-CUMUL-2: Conduct project-level vibration analysis for Blended System operations and implement vibration reduction measures as necessary and appropriate for the Caltrain corridor				X	In Progress	CHSRA is conducting this analysis as part of the EIR/EIS for the San Francisco to San Jose section.
TRA-CUMUL-1: Implement a phased program to provide traffic improvements to reduce traffic delays near at-grade crossings and Caltrain stations				X	Upcoming	This measure will be implemented during project operation.
TRA-CUMUL-2: Implement technical solution to allow electric trolley bus transit across 16 th Street without OCS conflicts in cooperation with SFMTA.	X				Complete	Not applicable. SFMTA has elected to not electrify the 16 th Street crossing. This measure no longer applies.
Mitigation Measure TRA-CUMUL-3: As warranted, Caltrain and freight operators will partner to provide Plate H clearance				X	Upcoming	This measure will be implemented during project operation.

Mitigation Monitoring and Reporting

Mitigation Measure	Mitigation Timing				Status	Status Notes
	Pre-Construction	Construction	Post-Construction	Operation		
as feasible between San Jose and Bayshore.						
