

25th Avenue Grade Separation

November 1, 2018 TA Board of Directors Agenda Item #11a



Agenda


- I. Project Need and Description
- **II.** Project Benefits
- III. Schedule
- **IV.** Construction
- V. Next Steps



Project Need and Description



Project Location

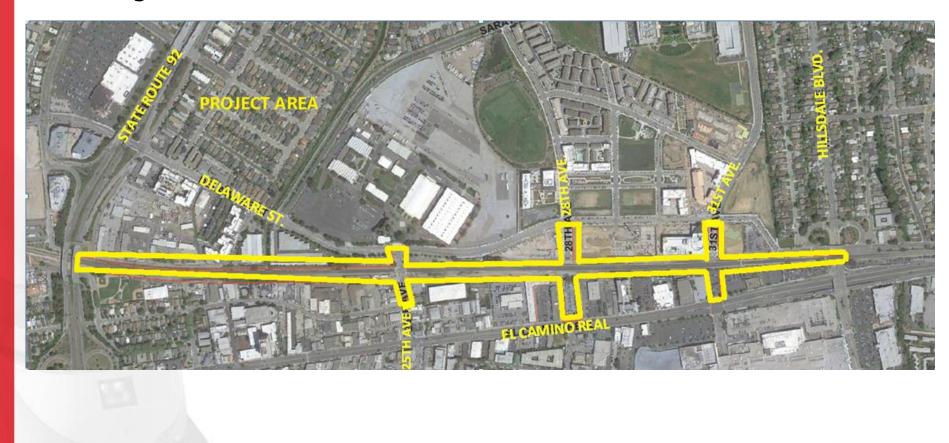

4



E. 25th Ave Railroad Crossing

- 92 Caltrain trains each weekday use this crossing, in addition to freight
- Lack of grade separation increases delays along corridor




Project Elements

Construct Grade Separation (elevated rails, lowered roads) between Hillsdale Blvd and Highway 92

- Five bridges
- Approx. 1 mile of MSE Wall
- New elevated station at Hillsdale



Elevated Track

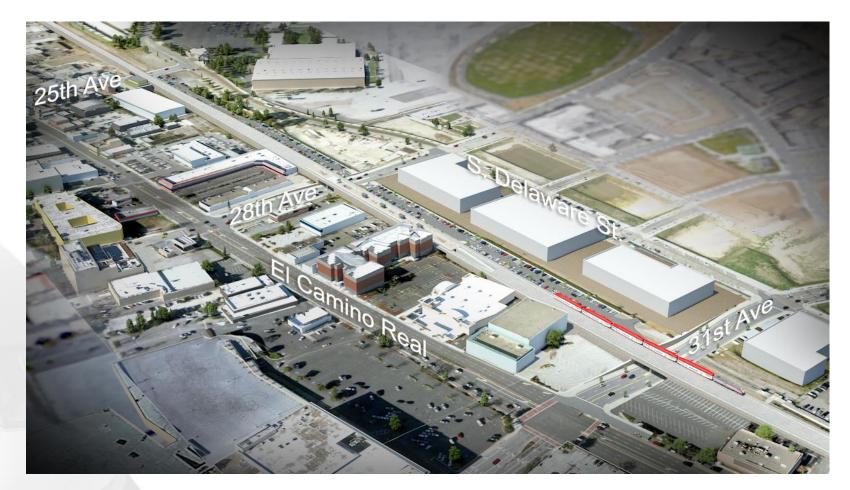



Grade Separation (25th Ave)





East-West Connection (28th Ave)





East-West Connection (31st Ave)





Relocated Hillsdale Station





Project Benefits




Project Benefits

- Safe rail operations
- Fewer system-wide delays
- Improved traffic flow
- Enhanced E-W connectivity
- Improved pedestrian and motorist safety
- Support Caltrain electrification



Project Funding, in Millions

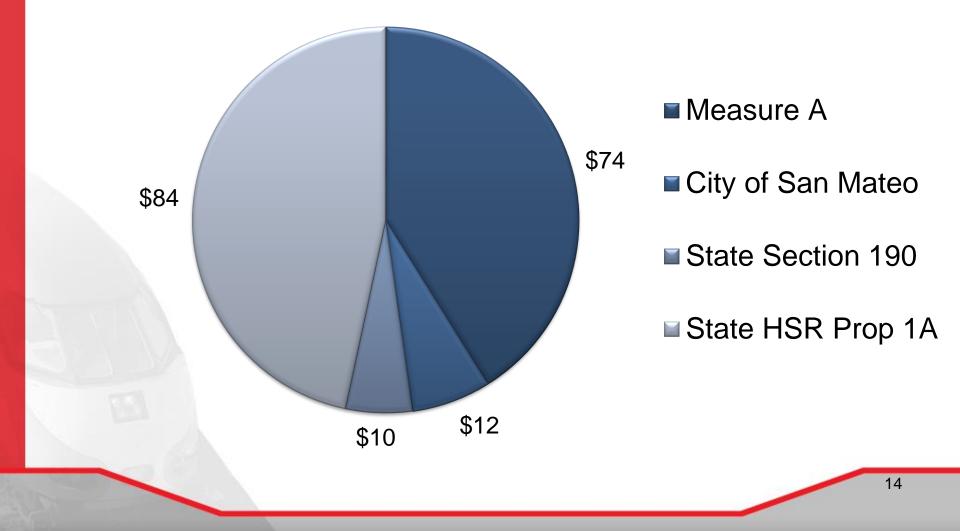



Schedule



Schedule

| Activity | Date |
|-----------------------|---|
| MSE Wall Construction | Sep 2018 - Oct 2019 |
| Station Closed | Sept 2019 – Feb. 2020 |
| Roads Completed | Feb. 2020 – 28 th Ave Aug. 2020 – 31 st Ave April 2020 – 25 th Ave |
| Project Completed | Oct. 2020 |



Hillsdale Station Closure

- Enhanced train service provided at Belmont Station
- Enhanced Samtrans bus and shuttle service provided between Hillsdale and Belmont Stations



Construction



Project Updates Bridges

Beresford Creek – Complete
25th Ave – Abutments & Columns Complete
28th Ave – Abutments on going
Pedestrian U/P – Installed bridge girders
31st Ave – Ready to install TPFOC Protection

Relocate Utilities:

- Third Party Utilities: On Going
- JPB Utilities: On Going

MSE Wall construction has begun



28th Ave Bridge







28th Ave Bridge









31st Ave Bridge










Pedestrian Underpass Bridge

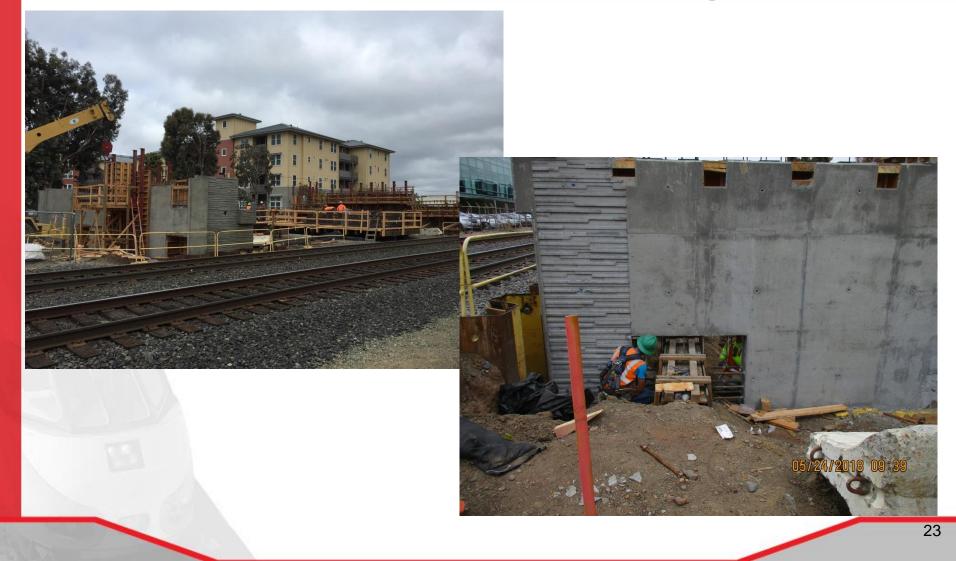



PG&E Gas Line Relocation





Next Steps



Next Steps

- Finalize settlement of time and cost impacts related to the Fiber Optic delay
- Review project estimates
- Return to the JPB board with a recommendation
- Public outreach



Questions
