



Peninsula Corridor Electrification Project Quarterly Update #6

Board of Directors
May 5, 2016
Agenda Item 7a



Major Contracts Update



Electrification Infrastructure Contract

2014	2015	2016
June: Pre- Qualification Process (6 firms)	Feb: RFP Issued Aug: Proposals Received (4 firms) Oct: Shortlisted (3 firms) Dec: Best and Final Offer (BAFO) Issued	Feb: BAFO Proposal Received March: Apparent Best Value Proposal

Best and Final Offer Process

- Competition between Three Shortlisted Firms
- Goal to Improve Initial Proposals Received
 - Modified work windows to allow more access
 - Strategic weekend closure in tunnels allowed
 - Utilization of current signal houses w/ existing capacity
- BAFO Proposal Results
 - Seven month reduction in schedule
 - Significant cost savings
 - Best value proposal with highest technical score and lowest cost

Electric Train (EMU) Contract

2014	2015	2016
May: Request for Information (6 firms)	Jan – June: Compatible Boarding Heights Discussion (2-4 firms) July: RFP Issued based on JPB Direction	Feb: Proposal Received

Contract Next Steps


- For Both Infrastructure and Electric Vehicles
- Continue Negotiations on Price
- Discuss / Finalize Policy Decisions
- Contract Award
 - Limited Notice to Proceed for six months
 - Full Notice to Proceed in 2017

Funding Update

Funding Update

- Regional 7-party Supplemental MOU (May)
- State/CHSRA Agreement (June/July)
- Cap and Trade Grant Award (August)
- FTA Core Capacity Award (End of 2016)

Cost and Funding History

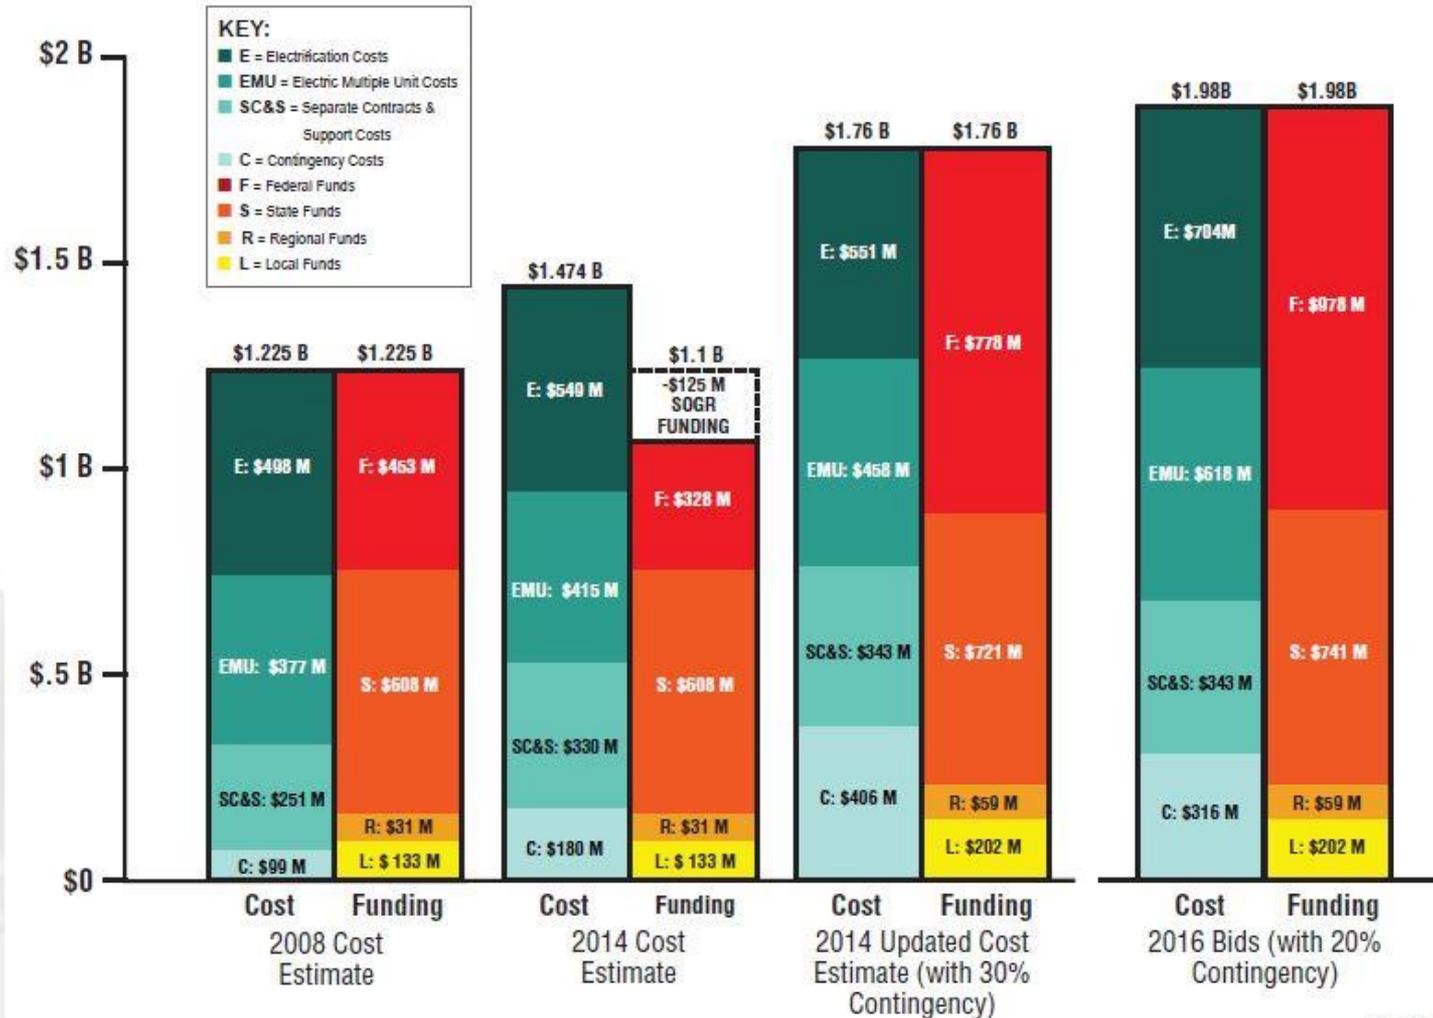

Electric Train (EMU) Policy Discussion



Bathrooms



Board Action (July 2015)

- RFP for Electric Trains
 - Design vehicle with one bathroom per train
 - Option for no bathrooms
- Consider additional bathrooms at stations

Public Feedback Electric Trains

- Sources
 - Rider Surveys in 2014, 2015, 2016 (~10,000 responses)
 - Public meetings (18)
 - Email, Website, Social Media
- Priority: #1 more seats, #2 more standing space
- Support for bathroom dips when capacity tradeoffs explained
- Majority desire at least one bathroom onboard (especially for special events and unexpected incidents)

Technical Information

- 1 Bathroom per Train, Cost for Fleet
 - \$2.8m (proposal)
 - Annual Operation and Maintenance Costs
- Capacity
 - One bathroom eliminates approximately 12 seats or 24 standees (proposal)

ADA Considerations

- Current law
 - Does not require any bathrooms or any specific number per train
 - If one is included, both bathroom and car must be ADA accessible and clearly marked
- Bathrooms would likely be in the second car and all passengers expecting to need it would be encouraged to use this car
- One bathroom per train is acceptable to FTA

Bathrooms at Stations

- Public bathrooms SF and Diridon
- Private bathrooms at several stations for patrons of a private business
- Costs Standalone Facility
 - \$134,000 capital cost per unit (Portland Loo estimate for installation in Portland)
 - Additional hookup costs
 - Annual Operation and Maintenance costs
- Other considerations such as security

Information Items



Bicycles




Copyright www.planbike.com 2011


Bicycle Elements

- JPB Action (July 2015)
 - 8:1 ratio seats to bikes (current system is 9:1)
 - \$3m capital commitment to bike parking at stations
- Bike Parking Management Plan
 - Ongoing, kickoff March 2016
 - Will identify needs and implementation approach
- Additional public involvement on onboard bike configuration post-award

Additional Doors

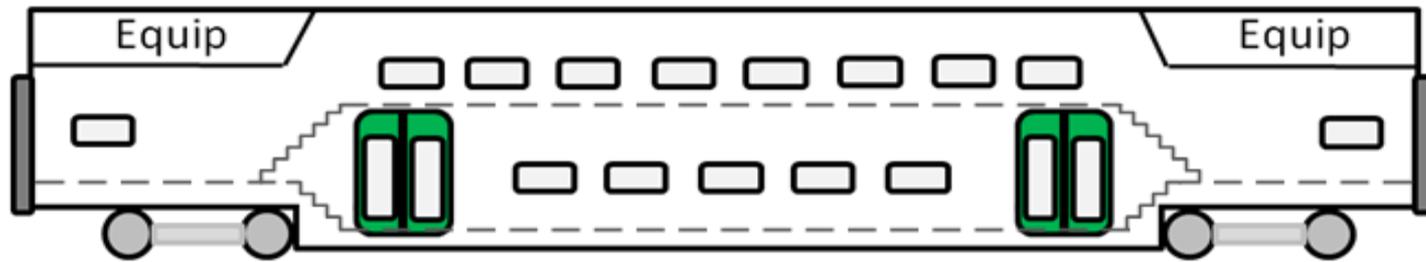

“Off the shelf” option. Low-level doors only.

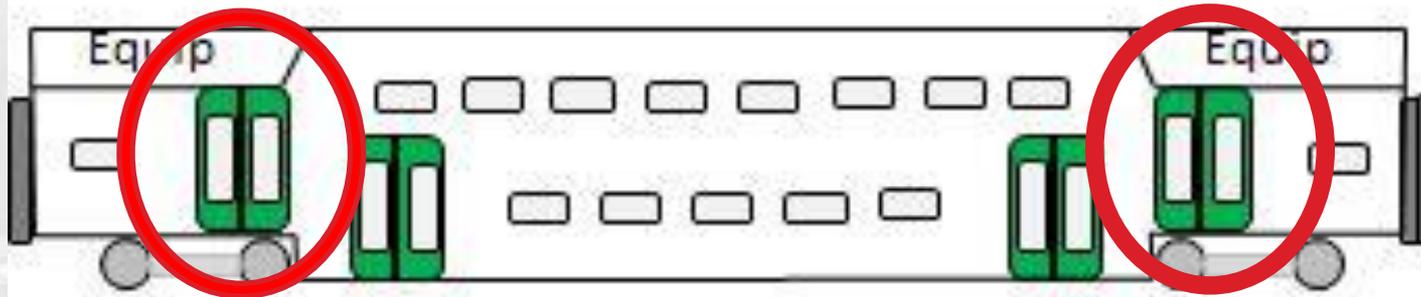

Dual doors option. Initially, upper doors to be sealed, with seats in front.


Dual Doors

- Context
 - Requested by stakeholders
 - “Not to preclude” future HSR boarding decisions
 - Customized vehicle
- Technical Information
 - Requires internal lift if upper doors opened
 - Cost of upper doors, plus lift \$30m (proposal)

Interior Lift Example



Schedule Refinement

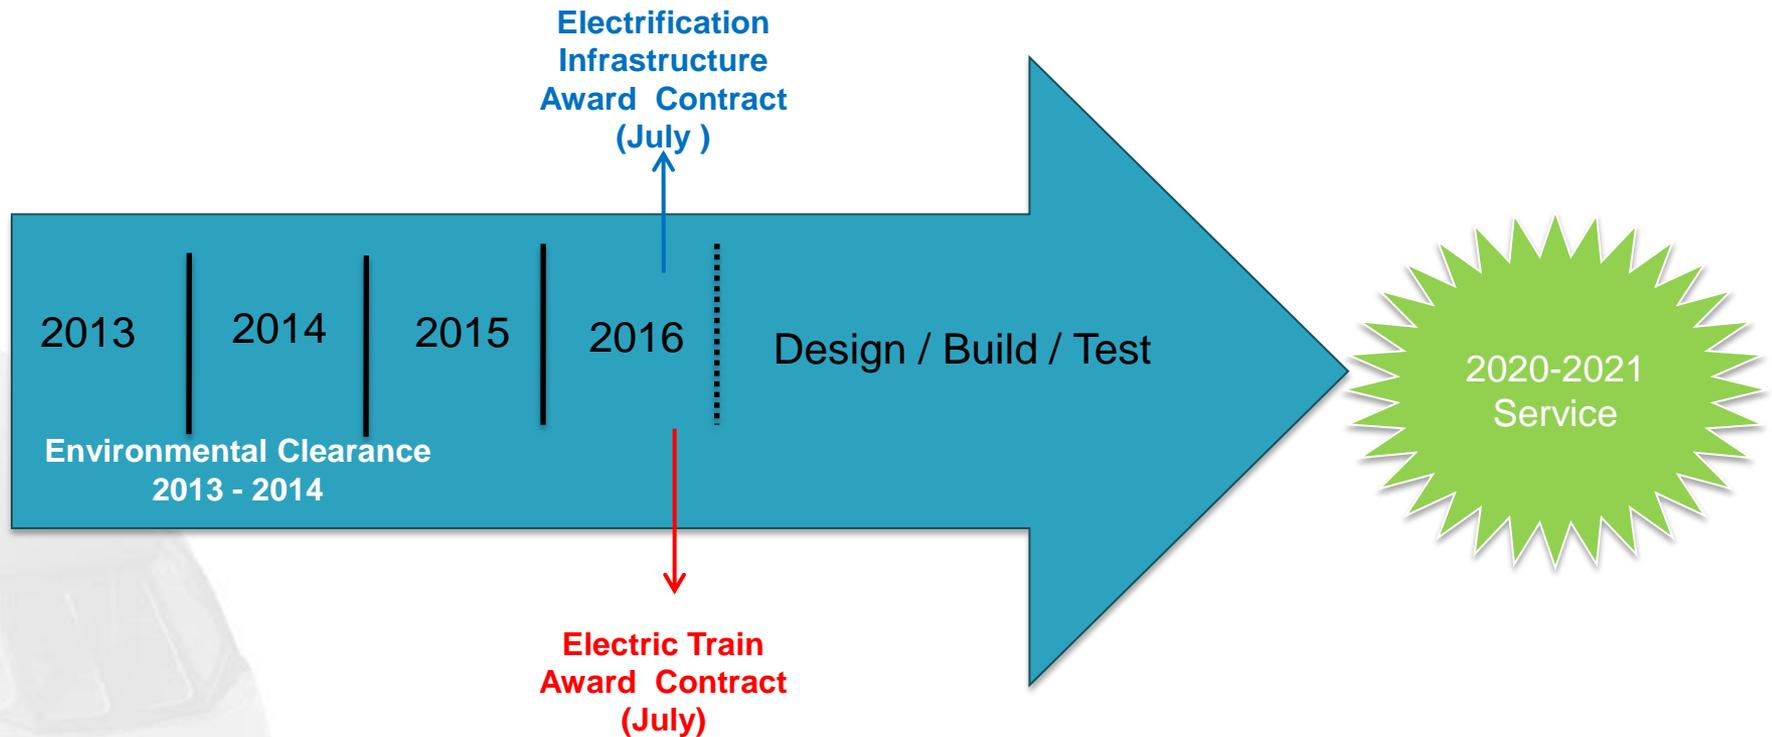

Note: Initial electric trains sets received in 2020 with final delivery in mid- 2021

Timeline

- May Solicit Public Feedback
 - CAC, BAC, CAAC, CSCG, PCWG, LPMG, C3, partner agencies, advocacy groups and customers
- June JPB Bathroom Policy Decision
- July Award Contract

Questions

More information / leave comments:

website: www.caltrain.com/calmod

email: calmod@caltrain.com

phone: 650.508.6499
